

Commercial Dashboard User Guide

The Marina – Marina Village (Programme 1, Triple Bay)

A simple, step-by-step guide with pictures

Website: <https://commercial-dashboard-kkz4.onrender.com>

Version 1.0 · September 2026 · Prepared for the Commercial team

What is in this guide

1. What the dashboard is, in one minute
2. Logging in (on a computer or a phone)
3. Finding your way around the screen
4. The home page: Executive Summary
5. How every list works (search, filter, add, edit, export, history)
6. The monthly routine, step by step
7. Importing your Excel monthly report
8. The modules, one by one
9. Locking a month and generating the report
10. Settings, users and backups
11. Who can do what (roles)
12. If something goes wrong

Reading tip. Every picture has red numbered circles. The text under the picture explains what each number is. You can jump straight to the chapter you need; each one stands on its own.

1. What the dashboard is, in one minute

The Commercial Dashboard is a website that replaces the monthly commercial report you used to build in Excel. Everything that used to live in the Excel schedules now lives in the dashboard:

- **Cost Report** (Schedules A and B) – budget, committed cost, changes, final account, certified to date.
- **Change Management Tracker** (Schedule C) – every RFC, PVO, VO, EI and DVO.
- **Claims, Early Warnings, Risks, Provisional Sums, Bonds & Insurance** (Schedules D to G).
- **Invoices & Payments** with the IPC log per contract and the **Final Account Status** (Schedule H).
- **Cash Flow** (Schedule I) and **Budget Transfers** (Schedule J).
- **Executive Summary** and **Minutes of Meeting**.


The big difference from Excel: **you only type the facts** (a new change, an IPC, a bond expiry date). The dashboard does all the sums, colours the warnings, and prints the monthly report as a PDF or an Excel file. Every month is **locked** when it is issued, so the next month can show what moved.

Golden rule: type each fact once, in the right list. The cost report and the executive summary update themselves.

You do not need to install anything. It works in any web browser, on a laptop or on a phone.

2. Logging in

- 1 Open your browser (Edge, Chrome or Safari) and go to **https://commercial-dashboard-kkz4.onrender.com**.
- 2 Type your **email** 1 and your **password** 2 .
- 3 Click **Sign in** 3 .



The login page. An Admin creates your login under Settings → Users (see chapter 10).

First time? The site may take up to a minute to wake up if nobody has used it for a while. Just wait; do not refresh many times.

Office laptop says "Login failed"? Some company networks block the login. Try your phone, or another browser. If it works on the phone, ask IT to allow the site address.

On a phone

The same address works on a phone. The menu is hidden behind the **three lines** button at the top left. Tap it to open the list of pages.

1TB01031 · Marina Villag...

1TB01031CM

1TB01031 · 1TB01031.01 · MODULE 11

Executive Summary

Monthly Report No 50 – Aug'26 · cut-off 31-Aug-26 · all amounts SAR

Locked

Checklist 0/12

L1 – L2 check OK

APPROVED BUDGET

E

880,852,840.00

LAT EST BUDGET

G

782,898,187.27

incl. transfers -97,954,652.73

COMMITTED

I

782,758,687.27

incl. DVOs -139,500.00

ANTICIPATED FINAL ACCOUNT

N

782,758,687.27

PVO/RFC/EW/claims 0.00

VARIANCE TO LAT EST BUDGET

O

-139,500.00

under budget

CERTIFIED TO DATE

P

733,924,921.33

CD

Commercial Dashboard

1TB01031CM

MODULES

Project Setup

1

Cost Report

2

Change Management

3

Claims & Disputes

4

Early Warnings & Risks

5

Provisional Sums

6

Bonds & Insurance

7

Invoices & Payments

8

Final Account Status

Cash Flow

9

Budget Transfers

10

Executive Summary

11

Minutes of Meeting

Monthly Report

12

SYSTEM

Change history

Settings

N

All amounts in SAR · Dates DD-MMM-YY

3. Finding your way around the screen

The screenshot shows the Commercial Dashboard interface. The top bar contains navigation elements: a dropdown for Programme (1TB01031 - Marina Villag...), a dropdown for Asset (1TB01031.01 - The Marina), a dropdown for Reporting Period (Monthly Report No 50 - ...), a Locked status indicator, and a user profile (CM Commercial Manager Admin). The left sidebar lists modules: Project Setup, Cost Report, Change Management, Claims & Disputes, Early Warnings & Risks, Provisional Sums, Bonds & Insurance, Invoices & Payments, Final Account Status, Cash Flow, Budget Transfers, Executive Summary (highlighted), Minutes of Meeting, and Monthly Report. The main content area displays an Executive Summary for Module 11, showing various financial metrics and key issues.

APPROVED BUDGET	LATEST BUDGET	COMMITTED	ANTICIPATED FINAL ACCOUNT
880,852,840.00	782,898,187.27 Incl transfers -97,954,652.73	782,758,687.27 Incl DVOs -139,500.00	782,758,687.27 PVO/RFC/EW/claims 0.00

VARIANCE TO LATEST BUDGET	CERTIFIED TO DATE	WORKS TO COMPLETE	PERIOD MOVEMENT
-139,500.00 under budget	733,924,921.33 94% of anticipated final account	48,833,765.94	782,758,687.27 no previous period

OPEN CHANGES BY STAGE	OPEN CLAIMS	OPEN EARLY WARNINGS	BONDS & INSURANCE EXPIRING
0 RFC, 1 PVO, 0 VO, 3 DVO 121 change(s) open in total	7 46,455,401.69 claimed and pending	6 12,505,062.89 potential cost - 2 open...	30 30 expired - 0 within 30 days - 0 with...

Key issues this period (Monthly Report No 50 - Aug'26)

Al Saad main works: final account under negotiation; DVO closure of items 134, 135 and 142 reduced PVO by SAR 3.85m.
Elmar boardwalk: EOT-01 cost claim (SAR 0.85m) and additional slipway (SAR 6.0m) carried as early warnings.
MME advance payment bond expires 28-Feb-26 - extension requested.

Actions (3 open, + Add)

- MCM-50-03 Elmar early warnings** (8d)
Confirm scope and raise RFC with Elmar.
N. Chintawar - due 18-Sep-26 · MCM-50 · Monthly Commercial Meeting - August 2026
- MCM-50-01 Al Saad final account** (15d)
Issue Employer's response to final account statement.
N. Chintawar - due 25-Sep-26 · MCM-50 · Monthly Commercial Meeting - August 2026
- MCM-50-02 MME advance payment bond** (20d)
Obtain bond extension from MME to 30-Jun-27.
B. Lombard - due 30-Sep-26 · MCM-50 · Monthly Commercial Meeting - August 2026

The screen has three parts: the menu on the left, the blue bar at the top, and the page in the middle.

- **1 Menu.** One line per module, numbered 1 to 12 like the Excel schedules. Click a line to open that page. "Change history" and "Settings" are at the bottom.
- **2 Programme.** Which programme you are looking at (1TB01031 Marina Village).
- **3 Asset.** The asset inside the programme (1TB01031.01 The Marina).
- **4 Reporting period.** The month you are working in, for example "Monthly Report No 50 – Aug'26". The little padlock tells you if the month is **Locked** (issued, read-only) or **Open** (you can still type).
- **5 You.** Your name and role. Click it to sign out.
- **6 The page.** Whatever you chose in the menu.

The period matters. Everything you see and type belongs to the period shown in the top bar. Before you start a new month, make sure the top bar shows the new month (chapter 6 explains how to create it).

4. The home page: Executive Summary

When you log in you land on the Executive Summary. It is the one-page picture of the month, the same numbers that go on the first pages of the monthly report.

Commercial Dashboard | PROGRAMME: 1TB01031 · Marina Villag... | ASSET: 1TB01031.01 · The Marina | REPORTING PERIOD: Monthly Report No 50 - ... | Locked | Commercial Manager Admin

Executive Summary
Monthly Report No 50 - Aug'26 · cut-off 31-Aug-26 · all amounts SAR

APPROVED BUDGET (E)
880,852,840.00

LATEST BUDGET (G)
782,898,187.27
incl transfers -97,954,652.73

COMMITTED (I)
782,758,687.27
incl DVOs -139,500.00

ANTICIPATED FINAL ACCOUNT (N)
782,758,687.27
PVO/RFC/EW/claims 0.00

VARIANCE TO LATEST BUDGET (O)
-139,500.00
under budget

CERTIFIED TO DATE (P)
733,924,921.33
94% of anticipated final account

WORKS TO COMPLETE (Q)
48,833,765.94

PERIOD MOVEMENT (S)
782,758,687.27
no previous period

OPEN CHANGES BY STAGE
RFC: 0, PVO: 1, VO: 0, DVO: 3
121 change(s) open in total

OPEN CLAIMS
7
46,455,401.69 claimed and pending

OPEN EARLY WARNINGS
6
12,505,062.89 potential cost · 2 open...

BONDS & INSURANCE EXPIRING
30
30 expired · 0 within 30 days · 0 with...

Key issues this period | Monthly Report No 50 - Aug'26
Al Saad main works: final account under negotiation; DVO closure of items 134, 135 and 142 reduced PVO by SAR 3.85m.
Elmar boardwalk: EOT-01 cost claim (SAR 0.85m) and additional slipway (SAR 6.0m) carried as early warnings.
MME advance payment bond expires 28-Feb-26 - extension requested.

Actions | 3 open | + Add

- MCM-50-03 Elmar early warnings** (8d)
Confirm scope and raise RFC with Elmar.
N. Chintawar · due 18-Sep-26 · MCM-50 · Monthly Commercial Meeting - August 2026
- MCM-50-01 Al Saad final account** (15d)
Issue Employer's response to final account statement.
N. Chintawar · due 25-Sep-26 · MCM-50 · Monthly Commercial Meeting - August 2026
- MCM-50-02 MME advance payment bond** (20d)
Obtain bond extension from MME to 30-Jun-27.
B. Lombard · due 30-Sep-26 · MCM-50 · Monthly Commercial Meeting - August 2026

The Executive Summary for Monthly Report No 50 - Aug'26.

What the eight big numbers mean

Card	In plain words
Approved Budget (E)	The budget as originally approved, all lines added up.
Latest Budget (G)	Approved budget plus or minus budget transfers.
Committed (I)	Latest budget plus approved (determined) variation orders. What we are contractually bound to.
Anticipated Final Account (N)	Committed, plus potential changes, RFCs, early warnings and claims. Our best estimate of the final bill.
Variance to Latest Budget (O)	Anticipated final account minus latest budget. Green = under budget, red = over.
Certified to Date (P)	The value certified so far in the IPC logs.
Works to Complete (Q)	Anticipated final account minus certified to date.
Period Movement (S)	How much the anticipated final account moved since last month's locked report.

Below the numbers you see the **open items** (changes by stage, open claims, early warnings, bonds expiring), the **Key issues** box (type the month's headline issues here; they print on the report), and the **Actions** list from the minutes of meeting.

The three chips at the top right tell you at a glance: is the period **Locked**, how many **checklist** items are done, and whether the **Level 1 – Level 2 check** of the cost report is OK.

5. How every list works

Almost every page is a **list** (the app calls it a register): changes, claims, bonds, IPCs and so on. They all work the same way, so once you know one, you know them all.

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 50 - ... Locked

MODULE 3

Change Management Tracker

Every change in one record, followed from Early Warning → RFC → PVO → VO → EI → DVO → Funding. Approved DVOs, live PVO / VOs and RFCs feed the cost report automatically.

CHANGES
161
121 open

PENDING OVER 30 / 60 DAYS
0 / 107
open items by days since raised

COST REPORT - DVO (H)
7,917,459.86
PVO / VO (J) 5,794,176.81

COST REPORT - RFC (K)
0.00
all changes linked to a cost line

Status matrix Number of changes at each stage by that stage's status

Stage	Cancelled	Approved	Pending	Superseded	Transferred	Review Complete	Other	Total
RFC	50	101	0	2	0	1	0	154
PVO	21	100	1	1	0	0	1	124
VO	15	96	0	0	0	0	1	112
DVO	10	96	3	0	0	0	0	109
Total	96	393	4	3	0	1	2	499

Days open > 30 **Days open > 60** Highlighting applies to open changes only. Link each change to its [cost report line](#) so its value flows into columns H, J and K.

Contractor / Consultant	Project stage	Change category	Initiated by	Action pending by	Actions
Al Saad General Contracting Co. Ltd.	Post-Contract Variation	Design Dev	Employer	None	History Edit Delete
Al Saad General Contracting Co. Ltd.	Post-Contract Variation	Design Dev	Employer	None	History Edit Delete

The Change Management Tracker. The tools above the table are the same on every list.

- 1 **Search.** Type a word or a number; the table shows only matching rows.
- 2 **Filters.** Narrow the list by status, package, contractor and so on.
- 3 **Export.** Downloads the list as an Excel file.
- 4 **Import.** Loads rows from an Excel file (for a single list). For the whole monthly report use chapter 7 instead.
- 5 **Add.** Opens an empty form to add a new row.
- 6 **Sort.** Click any column heading to sort by it. Click again to reverse.
- 7 **History.** Who changed this row, when, and what the old value was.
- 8 **Edit.** Opens the row in a form so you can change it.
- 9 **Delete.** Removes the row (it asks you to confirm).

Filters

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

Change history

Settings

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 50 - ...

Locked

CM Commercial ManagerAdmin

MODULE 3

Change Management Tracker

Every change in one record, followed from Early Warning → RFC → PVO → VO → EI → DVO → Funding. Approved DVOs, live PVO / VOs and RFCs feed the cost report automatically.

CHANGES161121 open

PENDING OVER 30 / 60 DAYS0 / 107open items by days since raised

COST REPORT – DVO (H)7,917,459.86PVO / VO (J) 5,794,176.81

COST REPORT – RFC (K)0.00all changes linked to a cost line

Status matrix

Number of changes at each stage by that stage's status

Stage	Cancelled	Approved	Pending	Superseded	Transferred	Review Complete	Other	Total
RFC	50	101	0	2	0	1	0	154
PVO	21	100	1	1	0	0	1	124
VO	15	96	0	0	0	0	1	112
DVO	10	96	3	0	0	0	0	109
Total	96	393	4	3	0	1	2	499

Days open > 30

Days open > 60

Highlighting applies to open changes only. Link each change to its [cost report line](#) so its value flows into columns H, J and K.

1

Q Search change management tracker...

Filters

Export

Import

+ Add Change

Overall statusAll

Project / AssetAll

PackageAll

Contractor / ConsultantAll

Project stageAll

Change categoryAll

Initiated byAll

Click Filters and choose values. "Clear" removes them again.

Page 10 of 36

Adding or editing a row

The form. Fields with a star are required. Sections can be opened and closed. **2** Save stores the row; **3** Cancel closes without saving.

- Money is typed as a plain number, for example 1250000 . The dashboard shows it as 1,250,000.00 SAR.
- Dates are picked from the calendar and shown as **DD-MMM-YY**, for example 31-Aug-26.
- Dropdowns (package, contractor, status) only offer values from Settings. If a value is missing, an Admin adds it under Settings.
- If something is wrong, the field turns red with a message. Fix it and click Save again.

Change history

CD Commercial Dashboard

MODULES

Project Setup

Cost Report

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

Change history

Settings

PROGRAMME

ASSET

REPORTING PERIOD

1TB01

1

Change history · CH-001

10-Sep-26 12:36 · Commercial Manager

import

Imported Change "CH-001"

programme: (blank) → 1

item no: (blank) → CH-001

description: (blank) → Changes to Amaala BIM Requirements

overall status: (blank) → 81

date raised: (blank) → 2021-10-18

asset: (blank) → 1

package: (blank) → 563

contractor: (blank) → 151

cost line: (blank) → 483

project stage: (blank) → 37

change category: (blank) → 53

initiated by: (blank) → 41

action pending by: (blank) → None

closed date: (blank) → 2022-08-21

ew ref: (blank) → 0

rfc ref: (blank) → 1

rfc rev: (blank) → 0

rfc date: (blank) → 2021-10-18

rfc status: (blank) → 81

rfc aconex ref: (blank) → AMA-WTRAN-000150

rfc time impact: (blank) → 0

rfc tracker amount: (blank) → 175000

rfc cr amount: (blank) → 0

pvo ref: (blank) → 1

pvo rev: (blank) → 0

pvo date: (blank) → 2021-10-18

pvo status: (blank) → 81

pvo aconex ref: (blank) → AMA-WTRAN-000150

pvo time impact: (blank) → 0

pvo tracker amount: (blank) → 175000

pvo cr amount: (blank) → 175000

vo ref: (blank) → VO 01

vo date: (blank) → 2021-11-12

vo status: (blank) → 81

vo cr amount: (blank) → 175000

vo contractor amount: (blank) → 0

vo employer aconex ref: (blank) → AMA-WTRAN-000930

vo employer date: (blank) → 2022-08-21

CM Commercial Manager

Admin

DVOs, live PVO / VO and RFCs feed the cost

COST REPORT – RFC (K)

0.00

all changes linked to a cost line

number of changes at each stage by that stage's status

Review Complete	Other	Total
1	0	154
0	1	124
0	1	112
0	0	109
1	2	499

its value flows into columns H, J and K.

Export Import + Add Change

Action pending by	Actions
None	
None	

Every change is recorded: who, when, old value, new value. Nothing is ever lost silently.

Colours

Coloured chips carry the same meaning everywhere:

green = fine / approved / closed

amber = attention soon

red = overdue / expired / rejected

 .

6. The monthly routine, step by step

This is the whole job for one month. It takes a few minutes of clicking plus the time you spend typing the month's facts.

- 1 Create the new month.** Go to **Settings → Reporting Periods → Add**. Type the report number (for example 51), the cut-off date (30-Sep-26) and the label "Monthly Report No 51 – Sep'26". Save. Then choose it in the top bar.
- 2 Record the month's facts** in each module: new changes and updates to their stages, new IPCs, new early warnings, bond renewals, budget transfers, provisional sum instructions, claim letters.
- 3 Check the cost report.** Open Cost Report → Level 2. The columns update themselves. The "Level 1 – Level 2 check" chip must be green.
- 4 Write the key issues** in the box on the Executive Summary, and add the minutes of the monthly meeting under Executive Summary → Minutes of Meeting.
- 5 Tick the checklist** on Project Setup and fill in Prepared by / Reviewed by / Approved by.
- 6 Lock the month** (Admin only): Settings → Reporting Periods → Lock. The month freezes; nothing can change by accident.
- 7 Generate the report:** Monthly Report → Generate PDF and Generate Excel. Send them out as usual.

Alternative for step 2: if you still prepare the month in your Excel workbook, upload it instead of typing. Chapter 7 shows how. The dashboard reads all the schedules in one go.

Locked months cannot be edited. If you really must correct an issued month, an Admin can Unlock it in Settings → Reporting Periods, make the correction, and Lock it again.

7. Importing your Excel monthly report

You can upload your monthly report workbook (the one with Schedule A to J, FA Status, Early Warning and the Schedule H sheets) exactly as it is. The dashboard recognises the layout, cleans it up and records everything against the reporting period.

The screenshot shows the 'Commercial Dashboard' interface. The top navigation bar includes filters for 'PROGRAMME' (1TB01031 · Marina Villag...), 'ASSET' (1TB01031.01 · The Marina), and 'REPORTING PERIOD' (Monthly Report No 50 - ...). The user is logged in as 'Commercial Manager Admin'. The sidebar lists various modules, with 'Monthly Report' selected. The main content area displays the 'Import monthly workbook' interface, which includes a step-by-step guide for importing a workbook. Step 1 is highlighted, showing a file upload button and a 'Read the workbook' button.

Monthly Report → Import monthly workbook. Step 1: choose the file and the period.

- 1 Open **Monthly Report** in the menu, then click **Import monthly workbook**.
- 2 Click **Choose file** 1 and pick your Excel workbook (.xlsx).
- 3 Choose the period. For a month that does not exist yet choose **New period** 2 ; the report number and cut-off date are filled in from the workbook's Data Input sheet. Check them.
- 4 Click **Read the workbook** 3 . Nothing is saved yet. The upload takes a moment for a large file.
- 5 A green box confirms that your report layout was recognised. Below it, each sheet is listed with the register it goes to and the columns it read. Normally there is nothing to change.
- 6 Leave the two boxes ticked: **create missing packages, contractors and dropdown values**, and **Lock the period after importing** (for past months).
- 7 Click **Import**. A results table shows how many rows were added or updated per sheet, and any row that could not be read with the reason.

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 50 - ... Locked

CM Commercial Manager Admin

MODULES

- Project Setup 1
- Cost Report 2
- Change Management 3
- Claims & Disputes 4
- Early Warnings & Risks 5
- Provisional Sums 6
- Bonds & Insurance 7
- Invoices & Payments 8
- Final Account Status
- Cash Flow 9
- Budget Transfers 10
- Executive Summary 11
- Minutes of Meeting
- Monthly Report 12**

SYSTEM

- Change history
- Settings

All amounts in SAR. Dates DD-MMM-YY

< Monthly Report

MODULE 12

Import monthly workbook

Upload one of your Excel monthly reports and the app records it against a reporting period. Import past months in date order, locking each one, to build the history; then each new month shows its movement against the last.

Choose the workbook and the month it belongs to

Your monthly report workbook (.xlsx). The app reads every sheet it recognises: cost report lines, change tracker, claims, early warnings, risks, provisional sums, bonds, contracts, IPC log, budget transfers, project team.

Excel file: Choose File No file chosen

☐ Existing period ☒ New period

Report No: 51

Cut-off date (month end): mm/dd/yyyy

Read the workbook Nothing is saved at this step; you review the app's reading first.

The import page after the workbook was read: one block per sheet, with the columns it recognised.

What happens to your numbers

- Rows are matched by their key (cost code, item number, claim number, IPC number). Uploading the next month **updates** the existing rows and adds the new ones. Nothing is duplicated.
- The cost report reproduces Schedule B: DVOs feed column H, live PVO/VOs feed J, early warnings feed L. The totals for E, F, G, H, J and L tie to the Excel exactly.
- Certified to date (P) is taken from the IPC logs, which are more up to date than the certified column in Schedule B.
- Contractor names are tidied to one spelling each (for example "Al Saad", "ALSAAD GENERAL CONTRACTING" and "ALS - Prelims" all become Al Saad General Contracting Co. Ltd.).

Import months in date order (August, then September ...) and lock each one. That is what makes the "movement" columns work.

8. The modules, one by one

Module 1 – Project Setup & Report Control

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

Change history

Settings

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 50 – ...

Locked

CM Commercial ManagerAdmin

MODULE 1

Project Setup & Report Control

The cover, index and data-input sheet of the monthly report: who, what and which period.

Project particulars

Edit

Programme nameMarina Village (Programme 1 – Triple Bay)

Programme code1TB01031

Asset nameThe Marina

Asset code1TB01031.01

ClientClient (edit me)

LocationLocation (edit me)

Shown for the Programme and Asset selected in the top bar. Other programmes / assets are managed under Settings.

Report control

Locked

Unlock period

Report No50

Reporting periodMonthly

Period31-Aug-26

Locked10-Sep-26 by Commercial Manager

Report number and dates come from the period selected in the top bar.
[Manage reporting periods](#)

Aconex reference

AMAALA/THE MARINA/MONTHLY REPORT 50

Document / transmittal reference for this month's report.

PREPARED BY

Nikesh Chintav

09/03/20:📅

REVIEWED BY

Blake Lombarc

09/04/20:📅

APPROVED BY

Michael Hanse

09/05/20:📅

Save report control

Report checklist

0 of 12 done

Tick each module once its section of Monthly Report No 50 – Aug'26 is complete. The checklist is kept per reporting period.

#	Module	Status	Done by	Comment
---	--------	--------	---------	---------

Project particulars, the report checklist, the distribution list and the sign-off names for the current period.

Use it once a month: tick the checklist as the report comes together and fill in Prepared by / Reviewed by / Approved by with the dates. These print on the cover of the report.

Page 16 of 36

Module 2 – Cost Report Level 1 & 2

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

Change history

Settings

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 50 – ...

Locked

CM Commercial ManagerAdmin

MODULE 2

Cost Report Level 1 & 2

Schedule A (Level 1, by asset) and Schedule B (Level 2, by package / contractor). All formulas are calculated by the app.

Monthly Report No 50 – Aug'26

No previous period yet

Level 1 – Level 2 check OK

Recalculate

Export Level 1 & 2 (Excel)

1Level 1 – Executive

2Level 2 – Detailed

3Line setup

Asset code	Asset	Cost category	Lines	E	Approved Baseline Budget	F	Budget Transfers auto	G	Awarded Contract / Latest Budget = E + F	H	Determined Variation Orders (DVO) auto	I
1TB01031.01	The Marina	Professional Services	7		28,037,904.00		52,544.33		28,090,448.33		0.00	
1TB01031.01	The Marina	Early Works	2		8,996,107.00		0.00		8,996,107.00		-139,500.00	
1TB01031.01	The Marina	Construction Works	36		825,126,893.00		-98,007,197.06		727,119,695.94		0.00	
1TB01031.01	The Marina	Management Supervision	1		17,523,690.00		0.00		17,523,690.00		0.00	
1TB01031.01	The Marina	Commercial Management	1		1,168,246.00		0.00		1,168,246.00		0.00	
Total					880,852,840.00		-97,954,652.73		782,898,187.27		-139,500.00	
Check: Level 1 total – Level 2 total (must be zero)					0.00		0.00		0.00		0.00	

Approved Baseline Budget vs Anticipated Final Account by package

SAR. Hover a package for the exact values; the Level 2 table holds the same figures.

Approved Baseline Budget

Anticipated Final Account

500M

400M

300M

1 Level 1 – Executive (Schedule A, by asset and cost category). 2 Level 2 – Detailed (Schedule B, line by line). 3 Line setup, where the lines themselves are added or changed.

Every column is calculated by the dashboard; you never type into the cost report itself except on the Line setup tab. Column letters follow the Excel:

Column	Comes from
E Approved Baseline Budget	Line setup (typed once)
F Budget Transfers	Budget Transfers module (plus transfers brought forward from the Excel)
G Latest Budget	E + F
H Determined VOs	Change Management: approved DVOs
I Committed	G + H
J Potential VOs, K RFCs	Change Management: live PVO / VO and RFC amounts
L Early Warnings	Early Warnings module (open items)
M Claims	Claims module (claims linked to a cost line)
N Anticipated Final Account	I + J + K + L + M
O Variance	N – G
P Certified to Date	Invoices & Payments: latest cumulative certified per contract
Q Works to Complete	N – P
R Previous, S Movement	Last month's locked report and N – R

CD Commercial Dashboard

PROGRAMME
1TB01031 · Marina Villag...

ASSET
1TB01031.01 · The Marina

REPORTING PERIOD
Monthly Report No 50 – ...

Locked

CM Commercial Manager
Admin

MODULES

- Project Setup 1
- Cost Report 2**
- Change Management 3
- Claims & Disputes 4
- Early Warnings & Risks 5
- Provisional Sums 6
- Bonds & Insurance 7
- Invoices & Payments 8
- Final Account Status
- Cash Flow 9
- Budget Transfers 10
- Executive Summary 11
- Minutes of Meeting
- Monthly Report 12

SYSTEM

- Change history
- Settings

MODULE 2
Cost Report Level 1 & 2
Schedule A (Level 1, by asset) and Schedule B (Level 2, by package / contractor). All formulas are calculated by the app.

Monthly Report No 50 – Aug'26
No previous period yet
Level 1 – Level 2 check OK
Recalculate
Export Level 1 & 2 (Excel)

Level 1 – Executive
Level 2 – Detailed
Line setup

Show
All assets
47 line(s) · double-click a row to edit

A Code	B Package	C Name	D Contractor / Sub-contractor
COMMITTED			
PS.031D03	WSP Consultants	WSP Consultants - Employers ...	WSP Middle East
PS.031D04	Becon - Marine Relocation	Becon Developments Co - Co...	Beacon Development Company
PS.031D01	5 Ocean - Marine Survey 2210091	Five Oceans Marine Survey - ...	Five Oceans Environmental Services LLC
PS.031D06	Sydney SeaPlane	Sydney Seaplane - Seaplane ...	Sydney Seaplanes Asia Limited
PS.031F03	Haskoning - Navigation Simulation	Haskoning - Navigation Simulat...	Haskoning DHV Saudia
PS.031F02	Kaust-King Abdullah University of Science	Kaust-King Abdullah University...	KAUST – King Abdullah University of Science & Tech
CN.031C01	ALS - Early Works	Al Saad - Early Works Package	Al Saad General Contracting Co. Ltd.
CN.031C03	JVD Early Works	JVD - Early Works	Dredging International Saudi Arabia (JVD)
CN.031C02	Al Saad Prelims	Preliminaries and General	Al Saad General Contracting Co. Ltd.
CN.031C02-2	Al Saad Main Works	Construction works (Excl Provi...	Al Saad General Contracting Co. Ltd.

Level 2. Committed and Uncommitted sections with subtotals and the grand total. Scroll sideways to see all columns.

Budget hold lines. The "Remaining budget" lines of each category (Professional Services, Construction Works...) are marked as budget hold. They absorb the changes and early warnings of their category, so the category total stays at the approved budget until the hold is used up, exactly like the Excel Schedule A.

CD Commercial Dashboard

MODULES

Project Setup 1

Cost Report 2

Change Management 3

Claims & Disputes 4

Early Warnings & Risks 5

Provisional Sums 6

Bonds & Insurance 7

Invoices & Payments 8

Final Account Status

Cash Flow 9

Budget Transfers 10

Executive Summary 11

Minutes of Meeting

Monthly Report 12

SYSTEM

Change history

Settings

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 50 - ...

Locked

CM Commercial Manager

Admin

MODULE 2

Cost Report Level 1 & 2

Schedule A (Level 1, by asset) and Schedule B (Level 2, by package / contractor). All formulas are calculated by the app.

Monthly Report No 50 - Aug'26

No previous period yet

Level 1 - Level 2 check OK

Recalculate

Export Level 1 & 2 (Excel)

Level 1 - Executive

Level 2 - Detailed

Line setup

Set up one line per package / contractor with its approved baseline budget (columns A-E). Packages and contractors come from [Settings](#). Use Import to load them from your Schedule B in one go.

Search cost report lines...

Filters

Export

Import

+ Add Cost line

Asset	Code	Package	Name / description
The Marina	PS.031D03	WSP Consultants	WSP Consultants - Employers Representative
The Marina	PS.031D04	Becon - Marine Relocation	Becon Developments Co - Coastal Conservation Management Plan and C
The Marina	PS.031D01	5 O Ocean - Marine Survey 2210091	Five Oceans Marine Survey - Coral Ecology Surveys - 2210091
The Marina	PS.031D06	Sydney SeaPlane	Sydney Seaplane - Seaplane Consultant - 1250665
The Marina	PS.031F03	Haskoning - Navigation Simulation	Haskoning - Navigation Simulation Study
The Marina	PS.031F02	Kaust-King Abdullah University of Science	Kaust- King Abdullah University of Science 2250235
The Marina	CN031C01	ALS - Early Works	Al Saad - Early Works Package
The Marina	CN031C03	JVD Early Works	JVD - Early Works
The Marina	CN031C02	Al Saad Prelims	Preliminaries and General
The Marina	CN031C02-2	Al Saad Main Works	Construction works (Excl Provisional Sums)

Line setup: the cost lines with their code, package, contractor, category and baseline budget.

Module 3 – Change Management Tracker

CD Commercial Dashboard

MODULES

Project Setup 1

Cost Report 2

Change Management 3

Claims & Disputes 4

Early Warnings & Risks 5

Provisional Sums 6

Bonds & Insurance 7

Invoices & Payments 8

Final Account Status

Cash Flow 9

Budget Transfers 10

Executive Summary 11

Minutes of Meeting

Monthly Report 12

SYSTEM

Change history

Settings

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 50 - ...

CM Commercial Manager

Admin

MODULE 3

Change Management Tracker

Every change in one record, followed from Early Warning → RFC → PVO → VO → EI → DVO → Funding. Approved DVOs, live PVO / VO and RFCs feed the cost report automatically.

CHANGES

161

121 open

PENDING OVER 30 / 60 DAYS

0 / 107

open items by days since raised

COST REPORT – DVO (H)

7,917,459.86

PVO / VO (J) 5,794,176.81

COST REPORT – RFC (K)

0.00

all changes linked to a cost line

Status matrix

Number of changes at each stage by that stage's status

Stage	Cancelled	Approved	Pending	Superseded	Transferred	Review Complete	Other	Total
RFC	50	101	0	2	0	1	0	154
PVO	21	100	1	1	0	0	1	124
VO	15	96	0	0	0	0	1	112
DVO	10	96	3	0	0	0	0	109
Total	96	393	4	3	0	1	2	499

Days open > 30

Days open > 60

Highlighting applies to open changes only. Link each change to its [cost report line](#) so its value flows into columns H, J and K.

Q Search change management tracker...

Filters

Refresh

Export

Import

+ Add Change

Contractor / Consultant	Project stage	Change category	Initiated by	Action pending by	Actions
Al Saad General Contracting Co. Ltd.	Post-Contract Variation	Design Dev	Employer	None	View Edit Delete
Al Saad General Contracting Co. Ltd.	Post-Contract Variation	Design Dev	Employer	None	View Edit Delete

Cards with the totals, the status matrix (how many changes at each stage and status) and the list of changes.

One row per change, followed from Early Warning → RFC → PVO → VO → EI → DVO → Funding. Open the row and fill in each stage as it happens (reference, date, status, amount). The dashboard works out the **current stage**, the **days open** (amber over 30, red over 60) and feeds columns H, J and K of the cost report. Link every change to its **cost report line** in the form, otherwise its value cannot flow into the cost report.

Module 4 – Claims & Disputes

CD Commercial Dashboard

MODULES

Project Setup

Cost Report

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

Change history

Settings

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 50 – ...

CM Commercial Manager

Admin

MODULE 4

Claims & Disputes

Schedule E: every claim with its notice compliance, detailed claim, assessment by each party and the determination.

CLAIMS

7

7 pending · none closed

EOT DAYS CLAIMED VS GRANTED

820 → 324

40% of days claimed granted

SAR CLAIMED VS DETERMINED

46,455,401.69 → 14,631,530.80

31% of value claimed determined

COST REPORT – CLAIMS (M)

19,471,955.92

7 claim(s) not linked to a cost line

Assessment ladder

Totals across all claims at each step of the assessment.

Party	Claims	EOT days	Compensable days	Cost (SAR)
Contractor's Claim	7	820	465	46,455,401.69
Engineer's Recommendation	3	324	147	4,840,425.12
Employer's Assessment	1	324	177	0.00
Determination / Agreement	1	324	0	14,631,530.80

Notice compliance

Business days use the Sunday–Thursday working week. Public holidays are not excluded.

Notice later than 28 business days

0

Detailed claim later than 42 business days

0

Column M of the [cost report](#) carries, per claim: the Determination, else the Employer's assessment, else the Engineer's recommendation, else the Contractor's claim. Rejected claims and claims already included in the lump sum carry zero.

Q Search claims & disputes...

Filters

Export

Import

+ Add Claim

Claim No ^	Description ^	Status ^	Claim type ^	Asset code ^	Contractor / Consultant ^
CL-001	Notice of Disatisfaction - Engineer's Instruction N...	Pending	EOT	The Marina	AlSaad General Contracting Co. Ltd.
CL-002	Notice of Disatisfaction - Engineer's Instruction N...	Pending	Prolongation	The Marina	AlSaad General Contracting Co. Ltd.
CL-003	Notice of Dissatisfaction on Engineer's Determina...	Pending	Other	The Marina	AlSaad General Contracting Co. Ltd.
CL-004	Extension of time - Precast Elements for fixed jetti...	Pending	EOT	The Marina	AlSaad General Contracting Co. Ltd.

Summary cards and the claims register.

Type the dates of the notice and of the detailed claim; the dashboard counts business days (Sunday to Thursday) and shows whether the 28-day and 42-day limits were met. Record the contractor's claim, the engineer's recommendation, the employer's assessment and the determination in their own sections.

Module 5 – Early Warnings and Risks & Opportunities

CD Commercial Dashboard

MODULES

Project Setup

Cost Report

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

Change history

Settings

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 50 – ...

CM Commercial Manager

Admin

MODULE 5

Early Warnings & Risks / Opportunities

Early warning notices (feeding column L of the cost report) and the commercial risk & opportunity register with its heat map.

Early Warnings (6)

Risks & Opportunities (2)

EARLY WARNINGS

6

6 open · 0 converted to RFC · 0 closed

OPEN – POTENTIAL COST (L)

12,505,062.89

all open items linked to a cost line

OPEN – POTENTIAL TIME

0 days

sum of potential time impact

OPEN BY LIKELIHOOD

Low 0

Med 2

High 4

Open early warnings feed column L of the [cost report](#). When one becomes an RFC, set its status to *Converted to RFC* and link the change item so the value moves to the change tracker instead.

Q Search early warnings...

Filters

Export

Import

+ Add Early Warning

EW No ^	Date raised ^	Raised by ^	Package ^	Contractor / Consultant ^	Description ^
EW	31-Aug-26	Contractor	Elmar-Hijaz Boardwalk and Jetties	Elmar Marinas Khaleej LLC	Additional Slipway at Nabateen Se
EW-22	31-Aug-26	Contractor	Al Saad Prelims	Al Saad General Contracting Co. Ltd.	Non Provision of Employer's Facil
EW-22-2	31-Aug-26	Contractor	Elmar-Hijaz Boardwalk and Jetties	Elmar Marinas Khaleej LLC	Elmar EOT-01 Cost Claim
EW-23	31-Aug-26	Contractor	MME-MME Marine Engg	MME – Majestic Marine Engineering LLC	EOT-02 COST - MME - Eextensio
EW-23-2	31-Aug-26	Contractor	MME-MME Marine Engg	MME – Majestic Marine Engineering LLC	Additional scope of Tographic Su
EW-23-3	31-Aug-26	Contractor	Elmar-Hijaz Boardwalk and Jetties	Elmar Marinas Khaleej LLC	MEP works, Aerodrom Installation,

6 of 6 early warnings · double-click a row to edit

All amounts in SAR · Dates DD-MMM-YY

Two registers on one page, with the heat map of risks and opportunities.

Open early warnings feed column L of the cost report. When an early warning becomes an RFC, set its status to "Converted to RFC" and it drops out of column L (the RFC takes over in column K/J).

Page 22 of 36

Module 6 – Provisional Sums

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

Change history

Settings

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 50 – ...

Locked

CM Commercial Manager

Admin

MODULE 6

Provisional Sums

Provisional sum allowances, what has been instructed against each, and the saving or extra that results.

TOTAL BUDGET

124,000,000.00

16 provisional sum(s)

TOTAL INSTRUCTED

50,477,392.65

5 of 16 item(s) with a contract value

TOTAL SAVING

28,522,607.35

Instructed value below budget

BY STATUS

Pending 15

Approved 1

(Saving) / Extra = Contract value – Budget. Savings show in green with a minus sign, extras in red. The totals row at the bottom of the table follows your search and filters. Statuses are managed under Settings → Provisional Sum Statuses.

Q Search provisional sums...

Filters

Export

Import

+ Add Provisional Sum

Item	Description	Status	Contractor	Budget	Contract value
PS-01	Allowance for Marine furniture steel support	Pending	Al Saad General Contracting Co. Ltd.	5,000,000.00	520,531.00
PS-02	Allowance for coordination with utilities	Pending	Al Saad General Contracting Co. Ltd.	2,500,000.00	—
PS-03	Dry stack access ramp	Pending	Al Saad General Contracting Co. Ltd.	1,000,000.00	—
PS-04	ECO Marine habitat to promote marine environment	Pending	Al Saad General Contracting Co. Ltd.	15,000,000.00	—
PS-05	Archl finish coordinated with external public realm	Pending	Al Saad General Contracting Co. Ltd.	2,000,000.00	1,059,783.36
PS-06	Bridge interface	Pending	Al Saad General Contracting Co. Ltd.	5,000,000.00	—
PS-07	Porous edge treatment following wave study	Approved	Al Saad General Contracting Co. Ltd.	12,000,000.00	621,261.23
PS-08	shoring to quay wall due to reduced set back	Pending	Al Saad General Contracting Co. Ltd.	48,000,000.00	48,000,000.00
PS-09	Labs & testing requirements	Pending	Al Saad General Contracting Co. Ltd.	1,000,000.00	—

Budget, instructed value and the (saving) / extra, worked out for you.

Page 23 of 36

Module 7 – Bonds & Insurance

CDCommercial Dashboard

MODULES

Project Setup1

Cost Report2

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

Change history

Settings

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 50 – ...

Locked

CMCommercial Manager

Admin

MODULE 7

Bonds & Insurance

Every bond and insurance policy: what the contract requires, what has been provided, and when it expires.

BONDS & POLICIES

38

30 expired · 0 within 30 days · 0 with...

PROVIDED VS REQUIRED

683,882,463.51 / 314,714,52...

total face value held vs total contrac...

SHORT FALLS

2

0.06 below requirement in total

CHECKS OUT STANDING

Not approved 10

Bank not verified 5

Bonds & Insurance expiring soon

30 within 60 days

30 already expired.

expired 679dG-10b · Professional Indemnity · WSP Middle East31-Oct-24

expired 649dG-12 · Workmen's Compensation · WSP Middle East30-Nov-24

expired 618dG-05 · Advance Payment Bond · Al Saad General Contracting Co. Ltd.31-Dec-24

expired 537dG-03 · Public/Third Party Liability · Al Saad General Contracting Co. Ltd.22-Mar-25

expired 537dG-11 · Public/Third Party Liability · WSP Middle East22-Mar-25

expired 528dG-04 · Contractors All Risks · Al Saad General Contracting Co. Ltd.31-Mar-25

expired 511dG-02 · Professional Indemnity · Al Saad General Contracting Co. Ltd.17-Apr-25

expired 467dG-20 · Advance Payment Bond · Al Saad General Contracting Co. Ltd.31-May-25

Open the Bonds & Insurance log →

Rows turn amber within 60 days of expiry and red within 30 days or once expired. Contract requirement = the % entered × revised contract value (or the original sum if no cost line is linked), or the fixed SAR amount. Types are managed under Settings → Insurance / Bond Types.

Q Search bonds & insurance...

Filters

Export

Import

+ Add Bond / Insurance

Ref

Contractor / Consultant

Package

Type of bond / Insurance


Policy / I

Every bond and policy with its expiry. Rows turn amber 60 days before expiry and red 30 days before or once expired.


Contract requirement is either a percentage of the contract value or a fixed SAR amount; the variance to what was provided is calculated. Bonds expiring soon also appear on the Executive Summary.

Page 24 of 36

Module 8 – Invoices & Payments

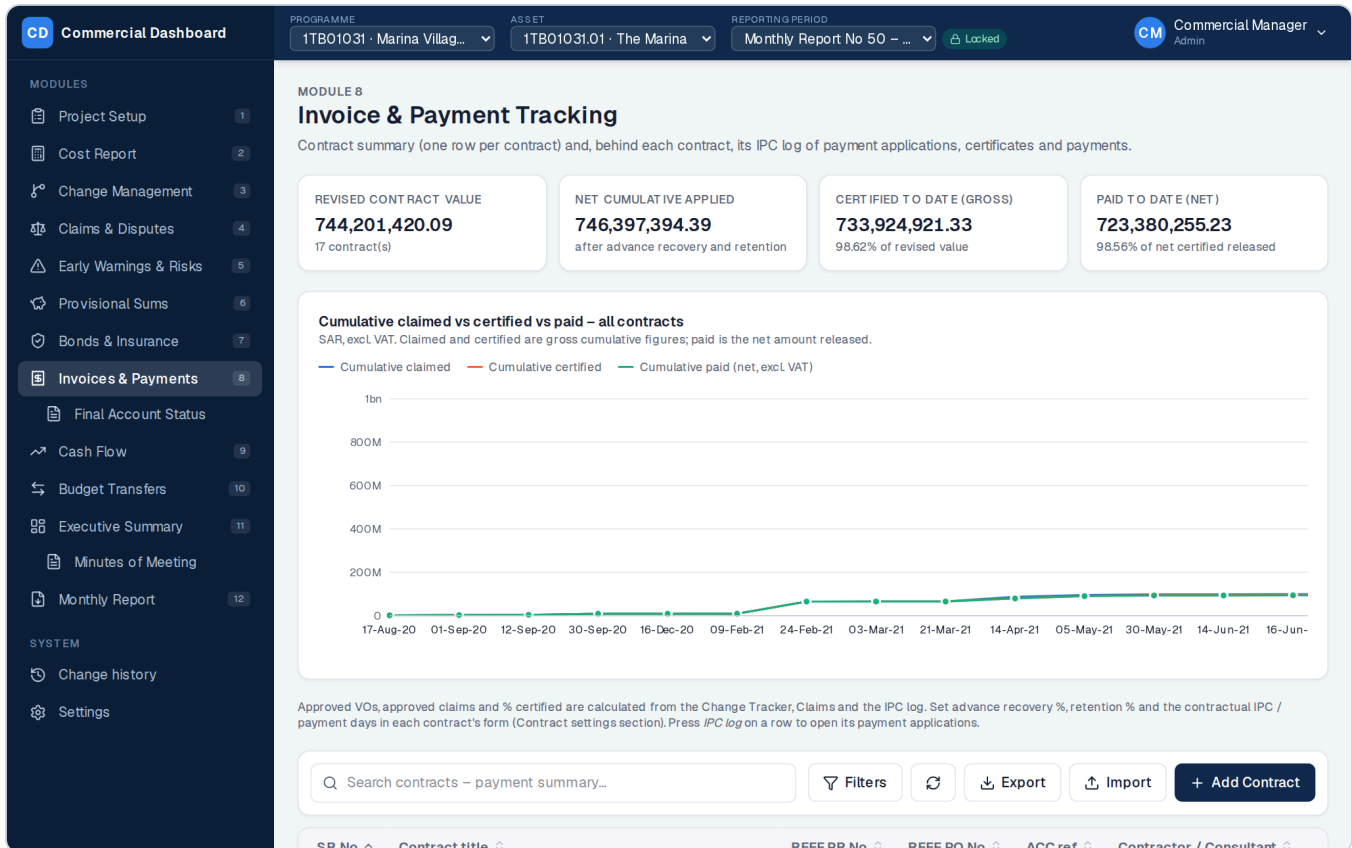

The contract summary (one row per contract) with cumulative applied, certified and paid, and the % certified.

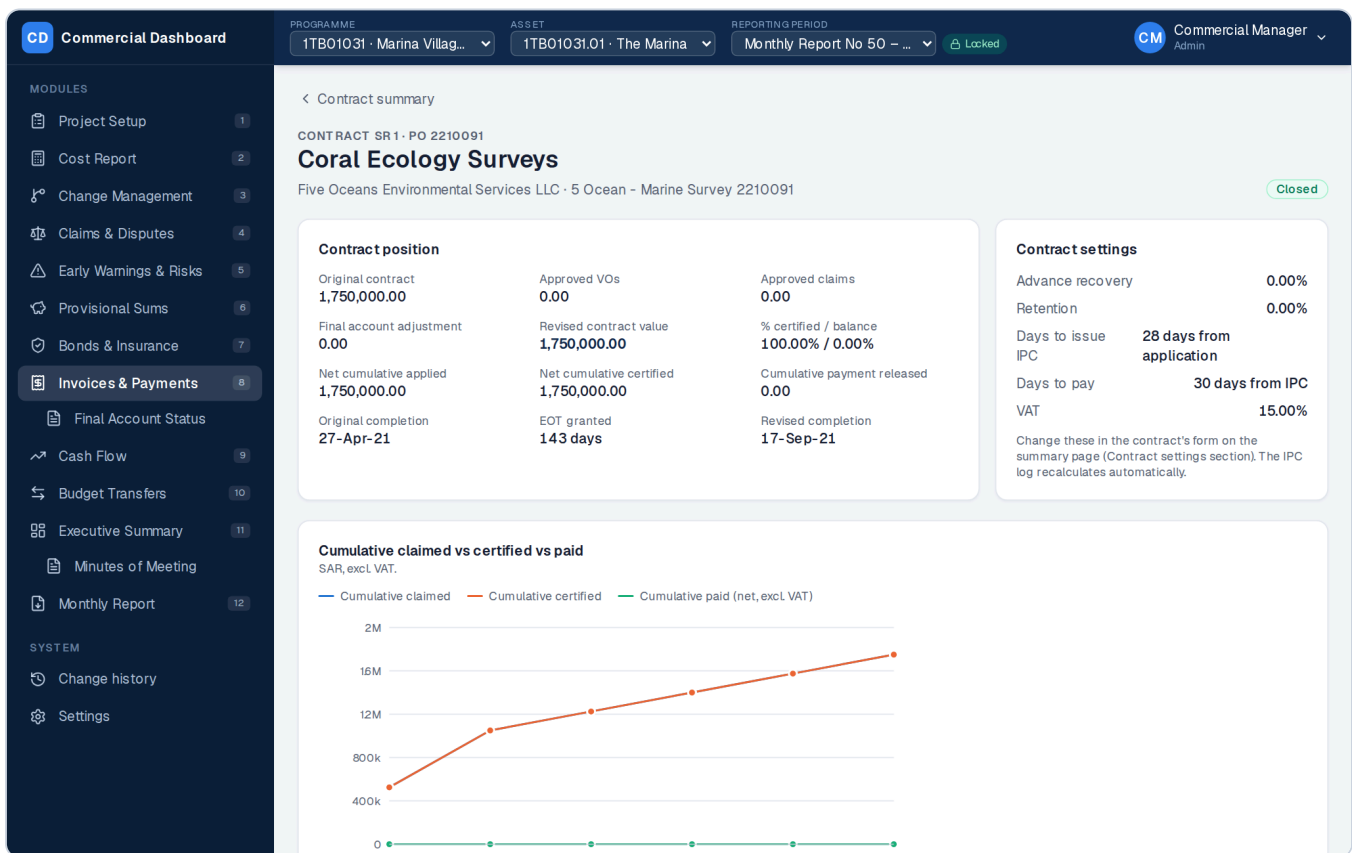

Click a contract to open its IPC log. Add one row per payment application. Due dates for the IPC and the payment are worked out from the contract settings (days to issue IPC, days to pay).

Module 8 – Final Account Status

CDCommercial Dashboard

MODULES

Project Setup1

Cost Report2

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

Change history

Settings

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 50 – ...

Locked

CMCommercial ManagerAdmin

MODULE 8

Final Account Status

One row per contract: is the final account statement open, signed or not required, and when is closure expected. Committed cost and the anticipated final account are read from the cost report line, so the totals tie to Schedule B.

OPEN6167,99,134.63 anticipated final account · 2 past forecast date

CLOSED (FAS SIGNED)5228,091,410.28 anticipated final account

NOT REQUIRED / DIRECT PAYMENT68,907,406.57 anticipated final account

TOTAL PACKAGES17404,197,951.48 total anticipated final account

Days remaining turn amber within 60 days of the forecast closure date and red once it has passed (open final accounts only). Link each row to its cost report line so the values stay in step with Schedule B.

Q Search final account status...

Filters

Export

Import

+ Add Final Account

ACC code	Package / description	Contractor / Consultant
PS.031D01	Five Oceans Marine Survey - Coral Ecology Surveys - 2210091	Five Oceans Environmental Services LLC
PS.031D03	WSP Consultants - Employers Representative	WSP Middle East
PS.031D04	Becon Developments Co - Coastal Conservation Management Plan and Coral Relocation	Beacon Development Company
PS.031D06	Sydney Seaplane - Seaplane Consultant - 1250665	Sydney Seaplanes Asia Limited
PS.031F02	Kaust-King Abdullah University of Science 2250235	KAUST – King Abdullah University of Science & Technology
PS.031F03	Haskoning - Navigation Simulation Study	Haskoning DHV Saudia
CN.031C01	AlSaad - Early Works Package	Al Saad General Contracting Co. Ltd.
CN.031C02	AlSaad-Marina Basin	Al Saad General Contracting Co. Ltd.

One row per contract: is the final account open, signed (closed) or not required, and when closure is expected. The committed cost and anticipated final account come from the cost report line.

Module 9 – Cash Flow

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

Change history

Settings

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 50 – ...

Locked

CM Commercial Manager

Admin

MODULE 9

Cash Flow

Monthly forecast per contract against the actual payments made, with the cumulative picture and what has been certified but not yet paid.

Monthly grid

Cumulative chart

Accruals (6)

Months: Sep'20 – Apr'26

Refresh

Export (Excel)

Type a forecast in any month and press Tab or click away to save. Actuals = net payments (excl VAT) by paid date from Payment Tracking, unless overridden. Click an actual to override it; clear the box to go back to the automatic value. Difference = Actual - Forecast (red = more than forecast).

Transaction No	Supplier	Line Description	Coding	CBS	Programme	
—	Five Oceans Environmental Services LLC	Coral Ecology Surveys	—	—	1TB01031	
—	Beacon Development Company	Coastal Conservation Manage...	—	—	1TB01031	
—	Al Saad General Contracting Co. Ltd.	Triple Bay Marina Basin - Early...	—	—	1TB01031	
—	Dredging International Saudi Arabia (JVD)	Triple Bay Marina Basin - Early...	—	—	1TB01031	
—	Five Oceans Environmental Services LLC	Marina Ecological Coral Surveys	—	—	1TB01031	
—	WSP Middle East	Marina Basin Supervision Con...	—	—	1TB01031	
—	Al Saad General Contracting Co. Ltd.	Triple Bay Marina Basin - Desi...	—	—	1TB01031	
—	Five Oceans Environmental Services LLC	Marina Ecological Coral Reloc...	—	—	1TB01031	
—	MME – Majestic Marine Engineering LLC	Design and Construction of FL...	—	—	1TB01031	
—	Al Saad General Contracting Co. Ltd.	Construction of Fixed Jetty for...	—	—	1TB01031	
—	Supreme Rubber LLC	Supply of Marine Furniture	—	—	1TB01031	
—	Elmar Marinas Khaleej LLC	Constructing Boardwalks & Je...	—	—	1TB01031	
—	Al Rajhi Takaful (Insurance)	Al Rajhi Takaful- Insurance - C...	—	—	1TB01031	
—	Al Rajhi Takaful (Insurance)	Al Rajhi Takaful- Insurance - O...	—	—	1TB01031	

Forecast, actual and difference per contract per month, with the cumulative chart. Actuals come from the paid dates in the IPC logs; you can overwrite a cell if needed.

Module 10 – Budget Transfers

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

Change history

Settings

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 50 – ...

Locked

CM Commercial ManagerAdmin

MODULE 10

Budget Transfers

Budget moved between packages. Approved transfers reduce the From package and increase the To package in column F of the cost report.

TRANSFERS3030 approved

APPROVED AMOUNT MOVED711,697,476.18total leaving From packages = total...

PENDING APPROVAL0.00not yet in the cost report

COST REPORT CHECKColumn F nets to zero30 approved not applied

These approved transfers are not in the cost report yet: BT-01(From package has no cost report line); BT-02 (From package has no cost report line); BT-03 (From package has no cost report line); BT-04 (From package has no cost report line); BT-05 (From package has no cost report line); BT-06 (From package has no cost report line); BT-07 (From package has no cost report line); BT-09 (From package has no cost report line); BT-10 (From package has no cost report line); BT-11 (From package has no cost report line); BT-12 (From package has no cost report line); BT-13 (To package has no cost report line); BT-14 (From package has no cost report line); BT-15 (From package has no cost report line); BT-16 (From package has no cost report line); BT-17 (From package has no cost report line); BT-18 (From package has no cost report line); BT-19 (From package has no cost report line); BT-21 (From package has no cost report line); BT-23 (From package has no cost report line); BT-24 (From package has no cost report line); BT-25 (From package has no cost report line); BT-26 (From package has no cost report line); BT-27 (From package has no cost report line); BT-28 (From package has no cost report line); BT-29 (From package has no cost report line); BT-30 (From package has no cost report line); BT-31 (From package has no cost report line); BT-31b (From package has no cost report line); BT-32 (From package has no cost report line). Open the transfer and choose the From / To cost line, or add the missing line on the Cost Report Line setup tab.

Net movement by package (as applied to cost report column F)

Package	Out	In	Net
No approved transfers applied yet.			

A transfer lands on the package's Level 2 line automatically. If a package has more than one line (several contractors), pick the line in the form. The In cost report column shows whether each transfer is currently applied. Column F on the Cost Report is now live.

Search budget transfers...

Filters

Export

Import

+ Add Budget transfer

Item	Description	Status	From package	To package
BT-00	REPRODUCTION TRANSFER - Transfer of Dis...	Approved	Budget Held - Construction	Into Budget Transfers - OUTGOING

Transfers between packages. Approved transfers linked to cost lines feed column F.

Module 11 – Minutes of Meeting

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 50 - ... Locked

CM Commercial Manager Admin

MODULES

- Project Setup 1
- Cost Report 2
- Change Management 3
- Claims & Disputes 4
- Early Warnings & Risks 5
- Provisional Sums 6
- Bonds & Insurance 7
- Invoices & Payments 8
- Final Account Status
- Cash Flow 9
- Budget Transfers 10
- Executive Summary 11
- Minutes of Meeting**
- Monthly Report 12

SYSTEM

- Change history
- Settings

All amounts in SAR · Dates DD-MMM-YY

< Executive Summary

MODULE 11

Minutes of Meeting

One row per meeting. Open the minutes to record items and actions; anything still open is carried forward to the next meeting automatically.

Q Search minutes of meeting...

Filters Refresh Export Import + Add Meeting

Meeting No	Title	Meeting date	Reporting period	Chair	Attendees
MCM-50	Monthly Commercial Meeting – August 2026	02-Sep-26	Monthly Report No 50 – Aug'26	Michael Hansen	M. Hansen, B. Lombard

1 of 1 minutes of meeting · double-click a row to edit

One meeting per month. Open items are carried forward automatically to the next meeting.

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 50 - ... Locked

CM Commercial Manager Admin

MODULES

- Project Setup 1
- Cost Report 2
- Change Management 3
- Claims & Disputes 4
- Early Warnings & Risks 5
- Provisional Sums 6
- Bonds & Insurance 7
- Invoices & Payments 8
- Final Account Status
- Cash Flow 9
- Budget Transfers 10
- Executive Summary 11
- Minutes of Meeting**
- Monthly Report 12

SYSTEM

- Change history
- Settings

All amounts in SAR · Dates DD-MMM-YY

< All meetings

MEETING MCM-50 · 02-SEP-26

Monthly Commercial Meeting – August 2026

Monthly Report No 50 – Aug'26 · RSG Site Office / Teams · Chair: Michael Hansen

Export all Items (Excel)

Attendees

M. Hansen B. Lombard N. Chintawar S. Fairfield (part)

Apologies: P. Donaghy

General notes

—

Items raised at this meeting

Item No, Topic, Discussion, Action, Owner, Due date and Status. Leave Item No blank to number automatically (MCM-50-01, -02, ...)

Q Search meeting items & actions...

Filters Refresh Export Import + Add Item

Item No	Topic	Action	Owner	Due date	Status	Days to c
MCM-50-01	AlSaad final account	Issue Employer's response to final account statem...	N. Chintawar	25-Sep-26	In progress	
MCM-50-02	MME advance payment bond	Obtain bond extension from MME to 30-Jun-27.	B. Lombard	30-Sep-26	Open	
MCM-50-03	Elmar early warnings	Confirm scope and raise RFC with Elmar.	N. Chintawar	18-Sep-26	Open	
MCM-50-04	Cash flow forecast	Update forecast for Oct-Dec on the Cash Flow p...	N. Chintawar	10-Sep-26	Closed	

4 of 4 meeting items & actions · double-click a row to edit

Inside a meeting: attendees, discussion items and actions with owner, due date and status.

9. Locking a month and generating the report

The screenshot shows the 'Reporting Periods' settings page in the Commercial Dashboard. The page has a dark sidebar with a list of modules and a main content area. The main content area has a header with filters for Programme, Asset, and Reporting Period. Below the header, there is a section titled 'REPORT CONTROL' with a sub-section 'Reporting Periods'. A blue box contains instructions: 'Month-end: press Lock on a period to freeze it. The app stores a copy (snapshot) of every module register at that moment so later reports can show This Period vs Previous Period. Unlock only if you need to correct something.' Below this, there is a search bar and buttons for Filters, Export, Import, and Add Reporting Period (labeled 2). A table lists reporting periods with columns: label, Status, Locked at, Locked by, Aconex ref, and Actions. The first row is 'Report No 50 - Aug/26' with status 'Locked', locked at '10-Sep-26', locked by 'Commercial Manager', and Aconex ref 'AMAALA/THE MARINA/MONTHLY REPORT 50'. The Actions column for this row has an 'Unlock' button (labeled 1), a clock icon, an edit icon, and a delete icon. Below the table, it says '1 of 1 reporting periods · double-click a row to edit'.

Settings → Reporting Periods. **1** Lock or Unlock a period (Admin). **2** Add the next month.

Locking takes a snapshot of every register and of the cost report. From then on the month is read-only and the next month compares itself against it ("previous period" and "movement" columns).

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina PROJECT/REPORT: **Monthly Report No 50 - ...** Locked

MODULE 12

Generate Monthly Report

Cover, index, minutes of meeting, executive summary and Schedules A to J as PDF or Excel, built from the locked snapshot of the chosen period.

Reporting period: Monthly Report No 50 - Aug'26 · Locked

Generate PDF **Generate Excel**

Locked - report uses the stored snapshot Lock the period under Settings → Reporting Periods (or on Project Setup) to freeze the figures before issuing.

Have the month in Excel already?
Upload your existing monthly report workbook and the app records it against a period. Import past months in order to build the history, then each new month shows its movement.

Import monthly workbook

Contents

- Cover page with project particulars and the Prepared / Reviewed / Approved block
- Index with checklist status and distribution list
- Minutes of Meeting for the period (carried-forward and new items)
- Executive Summary: KPIs, open items, key issues, actions, cost chart
- Schedule A** Cost Report - Level 1 (Executive)
- Schedule B** Cost Report - Level 2 (Detailed)
- Schedule C** Change Management Tracker
- Schedule D** Early Warnings & Risks / Opportunities
- Schedule E** Claims & Disputes
- Schedule F** Provisional Sums
- Schedule G** Bonds & Insurance
- Schedule H** Invoice & Payment Tracking and Final Account Status
- Schedule I** Cash Flow
- Schedule J** Budget Transfers

Sign-off block (current period)

PREPARED BY	REVIEWED BY	APPROVED BY
Nikesh Chintawar - Commercial Manager 03-Sep-26	Blake Lombard - Associate Commercial Director 04-Sep-26	Michael Hansen - Commercial Director 05-Sep-26

Fill these in on [Project Setup](#) → [Report control](#). Aconex reference and key issues come from the same place.

Monthly Report. **1** Choose the period. **2** Generate PDF. **3** Generate Excel.

The PDF contains the cover page with the sign-off block, the index, the minutes of meeting, the executive summary and Schedules A to J. The Excel has one sheet per schedule. If the period is still open the report is marked as a **draft from live data**; lock the period to issue the final version.

CD Commercial Dashboard

MODULES

Project Setup

Cost Report

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

Change history

Settings

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 50 - ...

Locked

CM

Commercial Manager

Admin

MODULE 12

Generate Monthly Report

Cover, index, minutes of meeting, executive summary and Schedules A to J as PDF or Excel, built from the locked snapshot of the chosen period.

Reporting period

Monthly Report No 50 - Aug'26 · Locked

Generate PDF

Generate Excel

Locked - report uses the stored snapshot

Lock the period under Settings → Reporting Periods (or on Project Setup) to freeze the figures before issuing.

Have the month in Excel already?

Upload your existing monthly report workbook and the app records it against a period. Import past months in order to build the history, then each new month shows its movement.

Import monthly workbook

Contents

Cover page with project particulars and the Prepared / Reviewed / Approved block

Index with checklist status and distribution list

Minutes of Meeting for the period (carried-forward and new items)

Executive Summary: KPIs, open items, key issues, actions, cost chart

Schedule A

Cost Report - Level 1 (Executive)

Schedule B

Cost Report - Level 2 (Detailed)

Schedule C

Change Management Tracker

Schedule D

Early Warnings & Risks / Opportunities

Schedule E

Claims & Disputes

Schedule F

Provisional Sums

Schedule G

Bonds & Insurance

Schedule H

Invoice & Payment Tracking and Final Account Status

Schedule I

Cash Flow

Schedule J

Budget Transfers

Sign-off block (current period)

PREPARED BY

Nikesh Chintawar

- Commercial Manager

03-Sep-26

REVIEWED BY

Blake Lombard - Associate Commercial Director

04-Sep-26

APPROVED BY

Michael Hansen - Commercial Director

05-Sep-26

Fill these in on [Project Setup](#) → [Report control](#). Aconex reference and key issues come from the same place.

The contents of the report and the sign-off block for the current period.

Page 32 of 36

10. Settings, users and backups

Commercial Dashboard

MODULES

- Project Setup
- Cost Report
- Change Management
- Claims & Disputes
- Early Warnings & Risks
- Provisional Sums
- Bonds & Insurance
- Invoices & Payments
- Final Account Status
- Cash Flow
- Budget Transfers
- Executive Summary
- Minutes of Meeting
- Monthly Report

SYSTEM

- Change history
- Settings**

Settings

Dropdown lists, project structure, reporting periods and users. Every list supports add / edit / delete, search, Excel import & export and change history.

Database backup [Download database](#)

Cloud backup is off (no BACKUP_GITHUB_* or BACKUP_S3_* settings). The database is the file data/commercial.db; use *Download database* to keep a copy. On a hosting service, set the backup settings so the database survives restarts.

Changes are uploaded within about 20 seconds, plus one dated copy per day. To restore, place the downloaded file at data/commercial.db (or upload it to the backup storage as backups/commercial.db) and restart the app.

PROJECT STRUCTURE

- Programmes** 1 → Top-level programmes (e.g. 1TB01031).
- Assets** 3 → Assets within a programme (e.g. 1TB01031.01).
- Clients** 1 → The employer / client organisations.
- Locations** 1 → Where the programmes / assets are located.

REPORT CONTROL

- Reporting Periods** 1 → One row per monthly report. Lock a period at month end to take a snapshot of every register.

COMMERCIAL LISTS

- Packages** 50 → Work packages / contracts that the cost report is broken down by.
- Contractors & Consultants** 13 → Every party you hold a contract or purchase order with.

DROPDOWN LISTS

Settings: every dropdown list, the project structure, reporting periods, users, the database backup and the Start over card (Admin only).

- **Dropdown lists** (packages, contractors, statuses, bond types, cost categories...): add or rename values here. The forms pick them up immediately.
- **Programmes and Assets**: the codes and names shown in the top bar.
- **Reporting Periods**: add the next month, lock and unlock (chapter 9).
- **Users**: add colleagues and choose their role (chapter 11).
- **Database backup**: the data is backed up automatically to a private GitHub repository within 20 seconds of every change. "Download database" gives you a copy to keep.
- **Start over**: wipes all project data (not users or settings). Only for a fresh start after a test import. It asks you to type DELETE.

CD Commercial Dashboard

MODULES

Project Setup

Cost Report

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

Change history

Settings

PROGRAMME

ASSET

REPORTING PERIOD

Commercial Manager

1TB01031 · Marina Villag...

1TB01031.01 · The Marina

Monthly Report No 50 - ...

Locked

< Settings

ACCESS

Users

People who can log in. Admin = full control, Editor = can add and change records, Viewer = read-only.

Search users...

Filters

Export

Import

Add User

Full name ^	Email (login) ^	Role ^	Active ^	Actions
Commercial Manager	admin@commercial.local	admin	Yes	

1 of 1 users · double-click a row to edit

Settings → Users. **1** Add a user: name, email, role and a first password. They can change the password later.

CD Commercial Dashboard

MODULES

Project Setup

Cost Report

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

Change history

Settings

PROGRAMME

ASSET

REPORTING PERIOD

Commercial Manager

1TB01031 · Marina Villag...

1TB01031.01 · The Marina

Monthly Report No 50 - ...

Locked

Change history

The latest 300 changes across every register: who changed what, and when.

10-Sep-26 12:47 · Commercial Manager

login

auth

Commercial Manager logged in

10-Sep-26 12:44 · Commercial Manager

login

auth

Commercial Manager logged in

10-Sep-26 12:43 · Commercial Manager

login

auth

Commercial Manager logged in

10-Sep-26 12:42 · Commercial Manager

login

auth

Commercial Manager logged in

10-Sep-26 12:42 · Commercial Manager

login

auth

Commercial Manager logged in

10-Sep-26 12:41 · Commercial Manager

login

auth

Commercial Manager logged in

10-Sep-26 12:40 · Commercial Manager

login

auth

Commercial Manager logged in

10-Sep-26 12:39 · Commercial Manager

login

auth

Commercial Manager logged in

10-Sep-26 12:39 · Commercial Manager

login

auth

Commercial Manager logged in

10-Sep-26 12:36 · Commercial Manager

login

auth

Commercial Manager logged in

Change history (System → Change history) lists every change made by anyone, newest first.

11. Who can do what

Role	Can see	Can add / edit / delete	Can lock periods, manage users, back up, start over
Viewer	Everything	No	No
Editor	Everything	Yes, in every module	No
Admin	Everything	Yes, in every module	Yes

Give Viewer to people who only read the report, Editor to the commercial team, and Admin to one or two people who issue the report.

12. If something goes wrong

What you see	What to do
"Login failed" on the office laptop	Try your phone or another browser. If the phone works, the office network is blocking the site; ask IT to allow the address.
The page takes a long time or shows a 502 message	The free hosting sleeps after 15 minutes without visitors and needs up to a minute to wake up. Wait, then reload once.
A field turns red when saving	Read the message under the field. Usually a required field is empty or a value is not in the dropdown list.
"This period is locked"	You are trying to change an issued month. Switch the top bar to the open month, or ask an Admin to unlock.
A dropdown does not have the package / contractor you need	Ask an Admin to add it under Settings, or tick "create missing values" when importing a workbook.
The import lists rows with errors	The rest of the file was imported. Fix the cells named in the message in Excel, then import the same file again choosing the same period; fixed rows are updated, nothing is duplicated.
The Level 1 – Level 2 check is red	A cost line is missing an asset or category. Open Cost Report → Line setup and complete the line.
Numbers on the Executive Summary look wrong	Check the top bar period, then the source module (a change not linked to a cost line, an early warning left Open, an IPC with a wrong cumulative value).

Health check for support: <https://commercial-dashboard-kkz4.onrender.com/api/health> shows whether the database and the backup are working.

Questions or ideas for the dashboard? Note them in the minutes of meeting under "Dashboard" so they are not forgotten.
