

The Marina Commercial Dashboard User Guide

The Marina (1TB01031) and Village Boutique Hotel (1TB01006) – AMAALA Triple Bay

A simple, step-by-step guide with pictures

Website: <https://commercial-dashboard-kkz4.onrender.com>

Version 2.36 · September 2026 · Prepared for the Commercial team

What is in this guide

1. What the dashboard is, in one minute
2. Logging in (on a computer or a phone)
3. Finding your way around the screen
4. The home page: Executive Summary
5. How every list works (search, filter, add, edit, export, history)
6. The monthly routine, step by step
7. Importing your Excel monthly report
8. The modules, one by one
9. Locking a month and generating the report
10. Settings, users and backups
11. Who can do what (roles)
12. Security: how the dashboard and its documents are protected
13. Automation: Claim EAR (Employer's Assessment Report)
14. Libraries: EOT Library and Contract Library
15. ASK ME: questions in plain English
16. If something goes wrong

Reading tip. Every picture has red numbered circles. The text under the picture explains what each number is. You can jump straight to the chapter you need; each one stands on its own.

1. What the dashboard is, in one minute

The Marina Commercial Dashboard is a website that replaces the monthly commercial report you used to build in Excel. Everything that used to live in the Excel schedules now lives in the dashboard:

- **Cost Report** (Schedules A and B) – budget, committed cost, changes, final account, certified to date.
- **Change Management Tracker** (Schedule C) – every RFC, PVO, VO, EI and DVO.
- **Early Warnings, Risks, Provisional Sums, Bonds & Insurance** (Schedules D, F and G). Claims & Disputes (Schedule E) come from the Claims Tracker import, not from the monthly workbook.
- **Invoices & Payments** with the IPC log per contract and the **Final Account Status** (Schedule H).
- **Cash Flow** (Schedule I) and **Budget Transfers** (Schedule J).
- **Executive Summary** and **Minutes of Meeting**.


The big difference from Excel: **you only type the facts** (a new change, an IPC, a bond expiry date). The dashboard does all the sums, colours the warnings, and prints the monthly report as a PDF or an Excel file. Every month is **locked** when it is issued, so the next month can show what moved.

Golden rule: type each fact once, in the right list. The cost report and the executive summary update themselves.

You do not need to install anything. It works in any web browser, on a laptop or on a phone.

2. Logging in

- 1 Open your browser (Edge, Chrome or Safari) and go to **https://commercial-dashboard-kkz4.onrender.com**.
- 2 Type your **email** 1 and your **password** 2 .
- 3 Click **Sign in** 3 .



The login page. An Admin creates your login under Settings → Users (see chapter 10).

First time? The site may take up to a minute to wake up if nobody has used it for a while. Just wait; do not refresh many times.

Office laptop says "Login failed"? Some company networks block the login. Try your phone, or another browser. If it works on the phone, ask IT to allow the site address.

On a phone

The same address works on a phone. The menu is hidden behind the **three lines** button at the top left. Tap it to open the list of pages.

1TB01031 · Marina Villag...

1TB01031 · CM

1TB01031 · 1TB01031.01 · MODULE 11

Executive Summary

Monthly Report No 51 – Sep'26 · cut-off 30-Sep-26 · all amounts SAR

Open

Checklist 0/12

L1 – L2 check OK

PDF

Excel

APPROVED BUDGET

E

880,852,840.00

LATEST BUDGET

G

782,898,187.27

incl. transfers -97,954,652.73

COMMITTED

I

735,395,313.45

incl. DVOs 8,007,274.86

ANTICIPATED FINAL ACCOUNT

N

748,844,738.15

PVO/RFC/EW/claims 13,449,424.70

VARIANCE TO LATEST BUDGET

O

-34,053,449.12

under budget

N

CERTIFIED TO DATE

P

CD

Commercial Dashboard

1TB01031 · CM

MODULES

Project Setup

1

Cost Report

2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management

3

Claims & Disputes

4

Early Warnings & Risks

5

Provisional Sums

6

Bonds & Insurance

7

Invoices & Payments

8

Final Account Status

Cash Flow

9

Budget Transfers

10

Executive Summary

11

Minutes of Meeting

Monthly Report

12

SYSTEM

N

All amounts in SAR · Dates DD-MMM-YY

3. Finding your way around the screen

The screenshot shows the Commercial Dashboard interface. The left sidebar contains a menu with 12 modules, numbered 1 to 12. The top blue bar contains navigation elements for project selection, asset selection, reporting period selection, and user profile. The main content area displays an 'Executive Summary' for 'Monthly Report No 51 - Sep'26' with various financial metrics and a table of movements.

Callouts:

- 1** Menu: The left sidebar menu.
- 2** Project / Asset: The dropdown menu for selecting the project/asset.
- 3** Sub-asset: The dropdown menu for selecting the sub-asset.
- 4** Reporting period: The dropdown menu for selecting the reporting period.
- 5** You: The user profile dropdown menu.
- 6** The page: The main content area.

Executive Summary Data:

Metric	Value
APPROVED BUDGET	880,852,840.00
LATEST BUDGET	782,898,187.27
COMMITTED	735,395,313.45
ANTICIPATED FINAL ACCOUNT	748,844,738.15
VARIANCE TO LATEST BUDGET	-34,053,449.12
CERTIFIED TO DATE	735,627,234.98
WORKS TO COMPLETE	13,217,503.17
PERIOD MOVEMENT	-4,760,000.00
OPEN CHANGES BY STAGE	1 RFC, 1 PVO, 0 VO, 2 DVO
OPEN CLAIMS	6
OPEN EARLY WARNINGS	6
BONDS & INSURANCE EXPIRING	29

Cost report table:

	Previous (Monthly Report No 50 – Aug'26)	This report	Movement
Approved Budget	880,852,840.00	880,852,840.00	-
Budget Transfers	-97,954,652.73	-97,954,652.73	-
Latest Budget	782,898,187.27	782,898,187.27	-
Determined VOs	7,917,459.86	8,007,274.86	+89,815.00
Committed	735,305,498.45	735,395,313.45	+89,815.00
Potential VOs	5,794,176.81	5,704,361.81	-89,815.00

The screen has three parts: the menu on the left, the blue bar at the top, and the page in the middle.

- 1 Menu.** One line per module, numbered 1 to 12 like the Excel schedules. Click a line to open that page. Under **Cost Report** there are three direct buttons: **Level 1 – Executive**, **Level 2 – Detailed** and **Line setup**. Under **Invoices & Payments** sits **Final Account Status**. "User guide", "Change history" and "Settings" are at the bottom.
- 2 Project / Asset.** Which stand-alone project you are looking at: **1TB01031 The Marina** or **1TB01006 Village Boutique Hotel (VBH)**. Each project keeps its own registers, its own reporting periods, its own report library and its own stored copies – nothing is shared between them except the dropdown lists (clients, contractors, statuses). Switching the project switches everything on the screen at once, and the dashboard remembers which report you were looking at in each project.
- 3 Sub-asset.** Shown only for a project with several assets (VBH: Branded Condos 1TB01006.01, Branded Residence .02, the Hotel .03 and Project Wide .99). It is the default asset for new rows and the name printed on report covers; every sub-asset of the project is always included in the figures. The Marina has one asset, so its code is simply displayed.
- 4 Reporting period.** The month you are working in, for example "Monthly Report No 50 – Aug'26". The little padlock tells you if the month is **Locked** (issued, read-only) or **Open** (you can still type).
- 5 You.** Your name and role. Click it to sign out.
- 6 The page.** Whatever you chose in the menu.

Executive Summary

Monthly Report No 47 – Aug'26 · cut-off 31-Aug-26 · all amounts SAR

APPROVED BUDGET: 854,010,655.25

LATEST BUDGET: 1,520,599,588.45
Incl. transfers 666,588,933.20

COMMITTED: 1,403,935,881.76
Incl. DVOs 269,973,278.71

ANTICIPATED FINAL ACCOUNT: 1,502,522,554.36
PVO/RFC/EW/claims 98,586,672.60

VARIANCE TO LATEST BUDGET: -18,077,034.09
under budget

CERTIFIED TO DATE: 1,456,666,271.50
97% of anticipated final account

WORKS TO COMPLETE: 45,856,282.86

PERIOD MOVEMENT: 0.00
no previous period

OPEN CHANGES BY STAGE:

Stage	Count
RFC	25
PVO	37
VO	28
DVO	80

74 change(s) open in total

OPEN CLAIMS: 0
0.00 claimed and pending

OPEN EARLY WARNINGS: 84
73,575,915.93 potential cost · 0 open rL

BONDS & INSURANCE EXPIRING: 42
34 expired · 4 within 30 days · 4 within ...

Movement since the last issued report
No earlier locked report yet. Import or enter the previous months in date order and lock each one; this panel then shows every change, month on month.

Change management status
How many changes have reached each stage, and their outcome.

Stage	Total	Approved	Pending	Cancelled
RFC	461	341	38	82
PVO	414	310	40	64
VO	386	292	49	45
DVO	339	228	81	30

DVO aging
81 determined variation order(s) still pending, by days since the DVO was raised.

Days	Count
Pending under 30 days	14
Pending 30 – 60 days	7
Pending 60 – 90 days	4
Overdue (over 90 days)	56

The Executive Summary with the Village Boutique Hotel project selected in the top bar: its own report (No 47 – Aug'26), its own figures, its own library.

Two projects, kept apart. The Marina and VBH never mix: importing a VBH workbook, locking a VBH month or editing a VBH register changes nothing in The Marina, and the other way round. Report numbers, cost codes and item numbers only need to be unique inside a project, so both projects can have a "Monthly Report No 47".

The period matters. Everything you see and type belongs to the period shown in the top bar. Before you start a new month, make sure the top bar shows the new month (chapter 6 explains how to create it).

Looking back at an issued month. Choose any locked month in the top bar (for example "Monthly Report No 50 – Aug'26"). The badge changes to **Issued · viewing** and every page, from the Executive Summary to the IPC logs, shows that month exactly as it was issued. Nothing can be edited while you look at an issued month; a green note on each list reminds you. Switch back to the open month to continue working.

4. The home page: Executive Summary

When you log in you land on the Executive Summary. It is the one-page picture of the month, the same numbers that go on the first pages of the monthly report.

Executive Summary
Monthly Report No 51 – Sep'26 · cut-off 30-Sep-26 · all amounts SAR

APPROVED BUDGET (E)
880,852,840.00

LATEST BUDGET (G)
782,898,187.27
incl transfers -97,954,652.73

COMMITTED (I)
735,395,313.45
incl DVOs 8,007,274.86

ANTICIPATED FINAL ACCOUNT (N)
748,844,738.15
PVO/RFC/EW/claims 13,449,424.70

VARIANCE TO LATEST BUDGET (O)
-34,053,449.12
under budget

CERTIFIED TO DATE (P)
735,627,234.98
98% of anticipated final account

WORKS TO COMPLETE (Q)
13,217,503.17

PERIOD MOVEMENT (S)
-4,760,000.00
vs Monthly Report No 50 – Aug'26

OPEN CHANGES BY STAGE
RFC: 1, PVO: 1, VO: 0, DVO: 2
121 change(s) open in total

OPEN CLAIMS
6
46,455,401.69 claimed and pending

OPEN EARLY WARNINGS
6
7,105,062.89 potential cost · 2 open r.l.

BONDS & INSURANCE EXPIRING
29
29 expired · 0 within 30 days · 0 with...

Movement since Monthly Report No 50 – Aug'26

Cost report	Previous (Monthly Report No 50 – Aug'26)	This report	Movement
E Approved Budget	880,852,840.00	880,852,840.00	–
F Budget Transfers	-97,954,652.73	-97,954,652.73	–
G Latest Budget	782,898,187.27	782,898,187.27	–
H Determined VOs	7,917,459.86	8,007,274.86	+89,815.00
I Committed	735,305,498.45	735,395,313.45	+89,815.00
J Potential VOs	5,794,176.81	5,704,361.81	-89,815.00

The Executive Summary for Monthly Report No 50 – Aug'26.

What the eight big numbers mean

Card	In plain words
Approved Budget (E)	The budget as originally approved, all lines added up.
Latest Budget (G)	Approved budget plus or minus budget transfers.
Committed (I)	Latest budget plus approved (determined) variation orders. What we are contractually bound to.
Anticipated Final Account (N)	Committed, plus potential changes, RFCs, early warnings and claims. Our best estimate of the final bill.
Variance to Latest Budget (O)	Anticipated final account minus latest budget. Green = under budget, red = over.
Certified to Date (P)	The value certified so far in the IPC logs.
Works to Complete (Q)	Anticipated final account minus certified to date.
Period Movement (S)	How much the anticipated final account moved since last month's locked report.

The three chips at the top right tell you at a glance: is the period **Locked**, how many **checklist** items are done, and whether the **Level 1 – Level 2 check** of the cost report is OK. The red **PDF** and green **Excel** buttons download this page as a print-ready file.

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

User guide (PDF)

Change history

Settings

↗

Movement since Monthly Report No 50 – Aug'26

Monthly Report No 50 – Aug'26

→

Monthly Report No 51 – Sep'26

PDF

Excel

Cost report	Previous (Monthly Report No 50 – Aug'26)	This report	Movement
E Approved Budget	880,852,840.00	880,852,840.00	–
F Budget Transfers	-97,954,652.73	-97,954,652.73	–
G Latest Budget	782,898,187.27	782,898,187.27	–
H Determined VOs	7,917,459.86	8,007,274.86	+89,815.00
I Committed	735,305,498.45	735,395,313.45	+89,815.00
J Potential VOs	5,794,176.81	5,704,361.81	-89,815.00
K RFCs	0.00	640,000.00	+640,000.00
L Early Warnings	12,505,062.89	7,105,062.89	-5,400,000.00
M Claims	0.00	0.00	–
N Anticipated Final Account	753,604,738.15	748,844,738.15	-4,760,000.00
O Variance to Budget	-29,293,449.12	-34,053,449.12	-4,760,000.00
P Certified to Date	733,924,921.33	735,627,234.98	+1,702,313.65
Q Works to Complete	19,679,816.82	13,217,503.17	-6,462,313.65

Changes by stage

Open changes at each stage and the cost-report amount they carry, previous report vs this one.

RFC

12 → 13

640,000.00

was 0.00 +640,000.00

PVO

7 → 7

0.00

was 0.00 –

VO

7 → 7

2,029,260.00

was 2,029,260.00 –

DVO

89 → 88

24,148,878.74

was 24,148,878.74 –

Changes (RFC / PVO / VO / DVO)

161 → 162 rows

+1 new

1 updated

cost-report amount: 36,826,671.86 → 37,556,486.86 (+729,815.00)

Claims & disputes

7 → 7 rows 1 updated

claimed (SAR): 46,455,401.69 → 46,455,401.69 (–)

CL-005 EOT-03 Extension of time - Precast Elements due to Delay in Utilities / Services related d


This panel appears as soon as an earlier month has been locked. It answers the question "what changed since last month?" line by line: a new RFC, a PVO that became a DVO, a claim determined, an early warning converted, a bond renewed, a new IPC, a final account closed. Green means favourable, red means adverse. It is printed in the monthly report and can be downloaded on its own with the PDF and Excel buttons on the panel.

Page 9 of 73

(this report's anticipated final account less the previous report's). The convention is set automatically when a monthly workbook is imported and can be seen under Settings → Programmes ("Level 1: remaining budget hold is a commitment").


Excel Level 1 check. When a monthly workbook is imported, the figures printed on its own Level 1 sheet (Development Budget, Anticipated Final Account, Variance to Budget, Last Month Anticipated Final Account, Variance to Last Month) are kept with the report. Cost Report → Level 1 shows them beside the dashboard's figures with a green tick or the difference, and the report library shows a chip per report ("Excel Level 1 ✓" or the difference). Reports imported before this version show the chip after a re-upload.

Key period movements

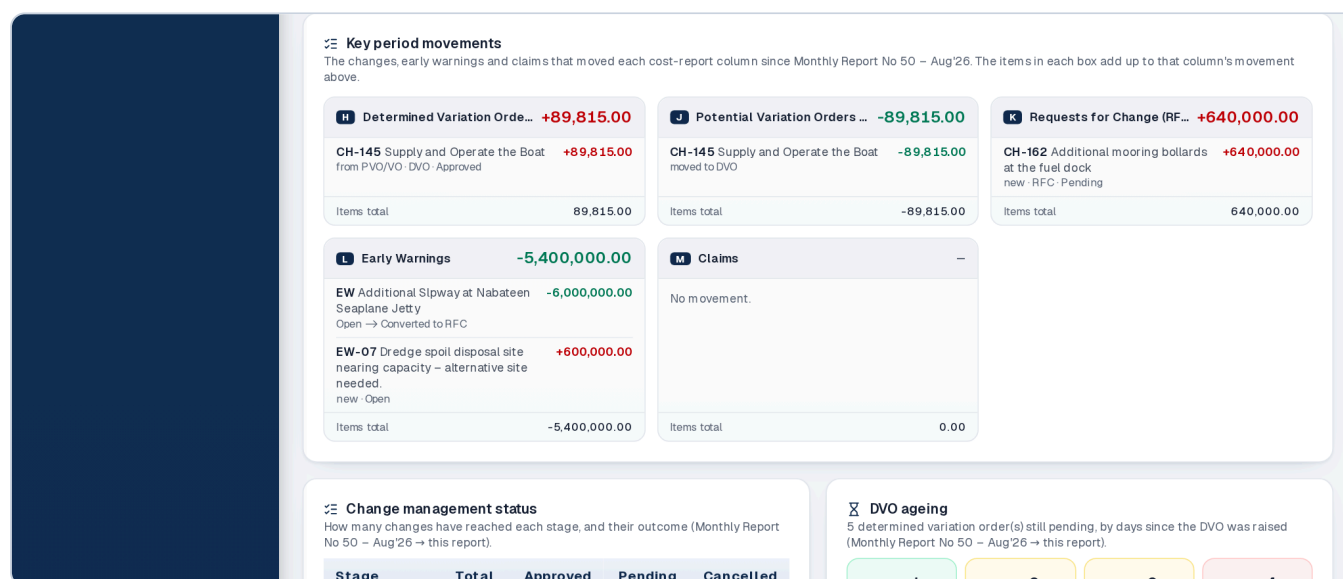

One box per cost report column: H (DVOs), J (PVOs and VO), K (RFCs), L (early warnings) and M (claims). Each box lists the items that moved that column and what happened to them; the items add up to the column's movement.

This is the same idea as the "Key Period Movements" block in the Excel executive summary, but built automatically. When a PVO becomes a DVO you see it leave box J (minus) and arrive in box H (plus). A brand-new RFC shows as "new" in box K. An early warning that was converted or closed shows as a minus in box L. If the items do not add up to the column's movement an amber chip says by how much: that usually means a change is not linked to a cost report line yet.

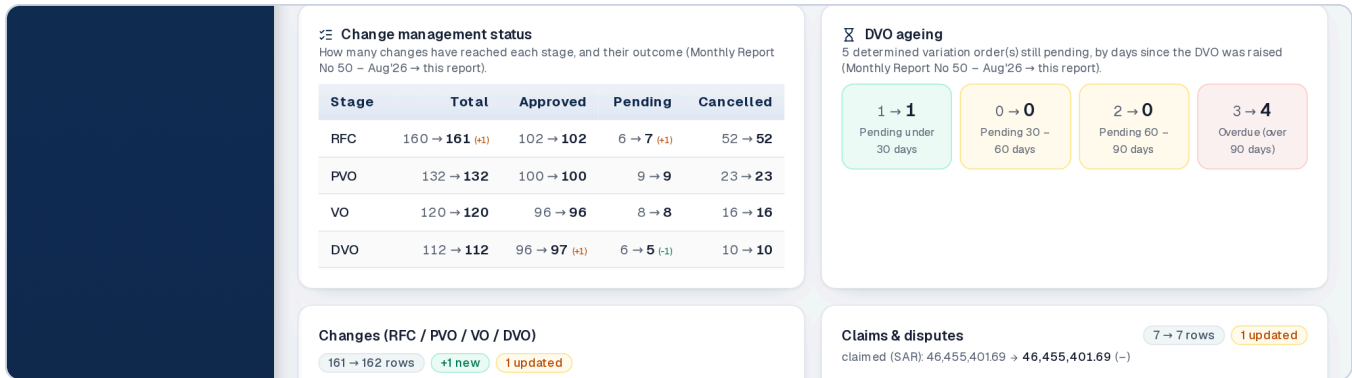

Left: how many changes have reached each stage and whether they are approved, pending or cancelled, last month → this month. Right: the DVOs still pending, grouped by how long they have been waiting; red means over 90 days.

Payment status tracker

Payment status tracker							
				17 contract(s) · certified 99% of revised value		49 late IPC(s) / payment(s)	
Contract	Contractor	Revised value	Certified to date	This period	% certified	Paid (net)	% paid
2200571 Active Triple Bay Marina Basin - Design and Build	Al Saad General Contra...	557,833,437.06	567,098,629.26	0.00	101.7%	567,098,629.26	
2240167 Active Design and Construction of Floating Pontoon	MME – Majestic Marine...	79,528,534.75	83,100,000.00	+1,702,313.65	104.5%	76,313,911.35	
2240276 Active Construction of Fixed Jetty for the Marina Ama...	Al Saad General Contra...	42,516,240.16	35,691,309.84	0.00	84.0%	35,691,309.84	
2250076 Active Constructing Boardwalks & Jetties for Hijaz Isl.	Elmar Marinas Khaleej...	28,247,178.71	19,809,003.40	0.00	70.1%	18,897,747.64	
2210172 Closed Marina Basin Supervision Consultant	WSP Middle East	13,900,878.64	12,617,276.95	0.00	90.8%	10,900,659.86	
2200593 Closed Marina Ecological Coral Relocation	Five Oceans Environme...	5,618,903.00	3,895,708.00	0.00	69.3%	3,895,708.00	
2200340 Closed Triple Bay Marina Basin - Early Contractor Inv...	Al Saad General Contra...	4,791,717.00	4,861,467.00	0.00	101.5%	4,861,467.00	
2200317 Closed Triple Bay Marina Basin - Early Contractor Inv...	Dredging International ...	3,995,139.75	3,995,140.00	0.00	100.0%	3,995,140.00	
2210091 Closed Coral Ecology Surveys	Five Oceans Environme...	1,750,000.00	1,750,000.00	0.00	100.0%	0.00	
2250226 Active Sydney Seaplane - Seaplane Consultant - 12...	Sydney Seaplanes Asia...	1,694,211.00	1,178,947.70	0.00	69.6%	1,178,947.70	

One row per contract: revised value, certified to date, certified this period, % certified, net paid, % of certified already paid, and how many IPCs or payments were late against the contract dates.

The green table gives you the payment position of every contract without opening the IPC log. Percent bars fill up as the contract is certified and paid. A red number in the "Late" columns means the IPC was issued, or the payment made, after the contractual due date; open the contract's IPC log under Invoices & Payments to see which ones. All three new sections print in the Executive Summary and Movement PDFs and Excel files.

Email the Report

CD Commercial Dashboard

PROGRAMME
 1TB01031 · Marina Villag...

ASSET
 1TB01031.01 · The Marina

REPORTING PERIOD
 Monthly Report No 51 – ...

CM Commercial Manager
 Admin

MODULES
 Project Setup 1
 Cost Report 2

1TB01031 · 1TB01031.01 · MODULE 11
Executive Summary
 Monthly Report No 51 – Sep'26 · cut-off 30-Sep-26 · all amounts SAR

Open Checklist 0/12 L1 – L2 check OK Email the Report
 PDF Excel

The blue **Email the Report** button sits in the Executive Summary header next to the PDF and Excel buttons.

Email the Report

To: nobody yet – add email addresses to the distribution list under Project Setup, or type them in Outlook
 Subject: 1TB01031·1TB01031.01 The Marina · Monthly Report No 51 – Sep'26 – Commercial summary (draft)
 Attachments: Executive Summary.pdf · Cost Report Level 1.pdf · Cost Report Level 2.pdf

Dear all,
 Please find attached the **Executive Summary**, **Cost Report Level 1 (Executive)** and **Cost Report Level 2 (Detailed)** for **Monthly Report No 51 – Sep'26 – 1TB01031.01 The Marina** (cut-off 30-Sep-26, draft from live data). The headline position is:

Cost report (SAR)	Monthly Report No 50 – Aug'26	This report	Movement
E Approved Baseline Budget	880,852,840.00	880,852,840.00	–
G Latest Budget (incl. transfers)	782,898,187.27	782,898,187.27	–
I Committed Costs	735,305,498.45	735,395,313.45	+89,815.00
J Potential VOs	5,794,176.81	5,704,361.81	-89,815.00
K Requests for Change	0.00	640,000.00	+640,000.00
L Early Warnings	12,505,062.89	7,105,062.89	-5,400,000.00
M Claims	0.00	0.00	–
N Anticipated Final Account	753,604,738.15	748,844,738.15	-4,760,000.00
O Variance to Latest Budget	-29,293,449.12	-34,053,449.12	-4,760,000.00
P Certified to Date	733,924,921.33	735,627,234.98	+1,702,313.65
Q Works to Complete	19,679,816.82	13,217,503.17	-6,462,313.65

Budget columns include the budget hold; change and forecast columns exclude it. Variance to Latest Budget: negative = under budget.

Key movements since Monthly Report No 50 – Aug'26

- H Determined Variation Orders (DVO): +89,815.00**
 CH-145 Supply and Operate the Boat (from PVO/VO · DVO · Approved): +89,815.00
- J Potential Variation Orders (PVO / VO): -89,815.00**
 CH-145 Supply and Operate the Boat (moved to DVO): -89,815.00
- K Requests for Change (RFC): +640,000.00**
 CH-162 Additional mooring bollards at the fuel dock (new · RFC · Pending): +640,000.00
- L Early Warnings: -5,400,000.00**

Buttons: Copy summary, Open mail app (text only), Open in Outlook with PDFs attached

The dashboard writes a short email for you: who it goes to, the subject, the headline table (last month, this month, movement), the key movements, the open items and your key issues. Nothing to type.

Press the button and check the preview. Then choose one of the three buttons at the bottom:

- Open in Outlook with PDFs attached** (on your PC). A small draft file is downloaded. Open it from your Downloads folder and Outlook shows the email ready to send, with the Executive Summary, Level 1 and Level 2 PDFs already attached. Check it, add anyone missing in "To", and press Send.
- Open mail app (text only)** (on your phone). Your mail app opens with the text summary. A web page cannot attach files on a phone, so attach the PDFs yourself if you need them.
- Copy summary.** Puts the formatted table and text on the clipboard so you can paste it into any email or Teams message.

The "To" list is filled from the email addresses in **Project Setup** → **Distribution list & project team**. Add everyone's email there once and every month's email is addressed automatically. If the month is not yet locked the subject says "(draft)".

5. How every list works

Almost every page is a **list** (the app calls it a register): changes, claims, bonds, IPCs and so on. They all work the same way, so once you know one, you know them all.

Commercial Dashboard | PROGRAMME: 1TB01031 · Marina Villag... | ASSET: 1TB01031.01 · The Marina | REPORTING PERIOD: Monthly Report No 51 - ... | CM Commercial Manager Admin

MODULE 3
Change Management Tracker
 Every change in one record, followed from Early Warning → RFC → PVO → VO → EI → DVO → Funding. Approved DVOs, live PVO / VO and RFCs feed the cost report automatically.

CHANGES
162
121 open

PENDING OVER 30 / 60 DAYS
0 / 106
open items by days since raised

COST REPORT - DVO (H)
8,007,274.86
PVO / VO (J) 5,704,361.81

COST REPORT - RFC (K)
640,000.00
all changes linked to a cost line

Status matrix
Number of changes at each stage by that stage's status

Stage	Cancelled	Approved	Pending	Superseded	Transferred	Review Complete	Other	Total
RFC	50	101	1	2	0	1	0	155
PVO	21	100	1	1	0	0	1	124
VO	15	96	0	0	0	0	1	112
DVO	10	97	2	0	0	0	0	109
Total	96	394	4	3	0	1	2	500

Days open > 30 Days open > 60 Highlighting applies to open changes only. Link each change to its cost report line so its value flows into columns H, J and K.

1 Search change management tracker... 2 Filters 3 Export 4 Import 5 Add Change

Contractor / Consultant	Project stage	Change category	Initiated by	Action pending by	Actions
Al Saad General Contracting Co. Ltd.	Post-Contract Variation	Design Dev	Employer	None	History Edit Delete
Al Saad General Contracting Co. Ltd.	Post-Contract Variation	Design Dev	Employer	None	History Edit Delete

The Change Management Tracker. The tools above the table are the same on every list.

- 1 **Search.** Type a word or a number; the table shows only matching rows.
- 2 **Filters.** Narrow the list by status, package, contractor and so on.
- 3 **Export.** Downloads the list as a formatted Excel file. For the version laid out exactly as in the monthly report use the red **PDF** and green **Excel** buttons in the page header.
- 4 **Import.** Loads rows from an Excel file (for a single list). For the whole monthly report use chapter 7 instead.
- 5 **Add.** Opens an empty form to add a new row.
- 6 **Sort.** Click any column heading to sort by it. Click again to reverse.
- 7 **History.** Who changed this row, when, and what the old value was.
- 8 **Edit.** Opens the row in a form so you can change it.
- 9 **Delete.** Removes the row (it asks you to confirm).

Filters

CD Commercial Dashboard

PROGRAMME
1TB01031 · Marina Villag...
ASSET
1TB01031.01 · The Marina
REPORTING PERIOD
Monthly Report No 51 – ...
Open
CM Commercial Manager
Admin

MODULES

- Project Setup 1
- Cost Report 2
- Level 1 – Executive
- Level 2 – Detailed
- Line setup
- Change Management 3**
- Claims & Disputes 4
- Early Warnings & Risks 5
- Provisional Sums 6
- Bonds & Insurance 7
- Invoices & Payments 8
- Final Account Status
- Cash Flow 9
- Budget Transfers 10
- Executive Summary 11
- Minutes of Meeting
- Monthly Report 12

SYSTEM

- User guide (PDF)
- Change history

MODULE 3
Change Management Tracker
Every change in one record, followed from Early Warning → RFC → PVO → VO → EI → DVO → Funding. Approved DVOs, live PVO / VOs and RFCs feed the cost report automatically.
PDF Excel

CHANGES
162
121 open

PENDING OVER 30 / 60 DAYS
0 / 106
open items by days since raised

COST REPORT – DVO (H)
8,007,274.86
PVO / VO (J) 5,704,361.81

COST REPORT – RFC (K)
640,000.00
all changes linked to a cost line

Status matrix
Number of changes at each stage by that stage's status

Stage	Cancelled	Approved	Pending	Superseded	Transferred	Review Complete	Other	Total
RFC	50	101	1	2	0	1	0	155
PVO	21	100	1	1	0	0	1	124
VO	15	96	0	0	0	0	1	112
DVO	10	97	2	0	0	0	0	109
Total	96	394	4	3	0	1	2	500

Days open > 30
Days open > 60
Highlighting applies to open changes only. Link each change to its [cost report line](#) so its value flows into columns H, J and K.

1
Filters
Refresh
Export
Import
+ Add Change

Overall status: All
Project / Asset: All
Package: All
Contractor / Consultant: All
Project stage: All
Change category: All
Initiated by: All

Click Filters and choose values. "Clear" removes them again.

Adding or editing a row

The form. Fields with a star are required. Sections can be opened and closed. **2** Save stores the row; **3** Cancel closes without saving.

- Money is typed as a plain number, for example 1250000 . The dashboard shows it as 1,250,000.00 SAR.
- Dates are picked from the calendar and shown as **DD-MMM-YY**, for example 31-Aug-26.
- Dropdowns (package, contractor, status) only offer values from Settings. If a value is missing, an Admin adds it under Settings.
- If something is wrong, the field turns red with a message. Fix it and click Save again.

Change history

Change history · CH-001

10-Sep-26 12:36 · Commercial Manager [import](#)

Imported Change "CH-001"

programme: (blank) → 1
 item no: (blank) → CH-001
 description: (blank) → Changes to Amaala BIM Requirements
 overall status: (blank) → 81
 date raised: (blank) → 2021-10-18
 asset: (blank) → 1
 package: (blank) → 563
 contractor: (blank) → 151
 cost line: (blank) → 483
 project stage: (blank) → 37
 change category: (blank) → 53
 initiated by: (blank) → 41
 action pending by: (blank) → None
 closed date: (blank) → 2022-08-21
 ew ref: (blank) → 0
 rfc ref: (blank) → 1
 rfc rev: (blank) → 0
 rfc date: (blank) → 2021-10-18
 rfc status: (blank) → 81
 rfc aconex ref: (blank) → AMA-WTRAN-000150
 rfc time impact: (blank) → 0
 rfc tracker amount: (blank) → 1750.00
 rfc cr amount: (blank) → 0
 pvo ref: (blank) → 1
 pvo rev: (blank) → 0
 pvo date: (blank) → 2021-10-18
 pvo status: (blank) → 81
 pvo aconex ref: (blank) → AMA-WTRAN-000150
 pvo time impact: (blank) → 0
 pvo tracker amount: (blank) → 1750.00
 pvo cr amount: (blank) → 1750.00
 vo ref: (blank) → VO 01
 vo date: (blank) → 2021-11-12
 vo status: (blank) → 81
 vo cr amount: (blank) → 1750.00
 vo contractor amount: (blank) → 0
 vo employer aconex ref: (blank) → AMA-WTRAN-000930
 vo employer date: (blank) → 2022-08-21

Every change is recorded: who, when, old value, new value. Nothing is ever lost silently.

Colours

Coloured chips carry the same meaning everywhere: **green = fine / approved / closed**

amber = attention soon

red = overdue / expired / rejected

What every Excel download looks like

Every Excel file the dashboard produces is a normal, fully editable workbook, formatted the same way: a navy title band with a link back to the dashboard, coloured column headers, alternating row shading, thin borders, real dates and money formats, a frozen header row with filters, coloured status cells (green for approved or closed, amber for pending or open, red for rejected, expired or overdue) and coloured sheet tabs. Totals are **live SUM formulas**, not typed numbers. The cost report goes further: on Level 2 the columns G, I, N, O, Q and S are formulas of the input columns, the category sub-totals and grand totals are SUMs, and on Level 1 every category figure is a SUMIFS formula over Level 2 while Development Budget, Committed, Anticipated Final Account and the variances are formulas of the rows above, so you can change a line in Excel and both sheets recalculate. Two check cells at the foot of Level 1 must read zero. The full monthly report has an Index sheet whose titles are links to each schedule, and each sheet has a "◀ Index" link in its title band. A file you downloaded can be edited and uploaded again through the Import buttons or the Stand-alone imports; the dashboard finds the header row below the title band by itself.

6. The monthly routine, step by step

This is the whole job for one month. It takes a few minutes of clicking plus the time you spend typing the month's facts.

- 1 Create the new month.** Open **Monthly Report** → **New month (manual entry)**. The next report number and month-end date are already filled in; press **Start**. The month is created, becomes the current period in the top bar and gets its checklist. (You can still add a period under Settings → Reporting Periods if you prefer.)
- 2 Record the month's facts** in each module: new changes and updates to their stages, new IPCs, new early warnings, bond renewals, budget transfers, provisional sum instructions, claim letters.
- 3 Check the cost report.** Open Cost Report → Level 2. The columns update themselves. The "Level 1 – Level 2 check" chip must be green.
- 4 Write the key issues** in the box on the Executive Summary, and add the minutes of the monthly meeting under Executive Summary → Minutes of Meeting.
- 5 Tick the checklist** on Project Setup and fill in Prepared by / Reviewed by / Approved by.
- 6 Lock the month** (Admin only): the **Lock & issue** button at the bottom of the New month page, or Settings → Reporting Periods → Lock. The month freezes; nothing can change by accident.
- 7 Generate the report:** Monthly Report → Generate PDF and Generate Excel. Send them out as usual. Any single page (Executive Summary, Level 1, Level 2, a schedule, the movement analysis) can also be downloaded on its own with the PDF / Excel buttons on that page.
- 8 Compare months:** pick any earlier locked month in the top bar to see that report; pick the current month to see the movement panel comparing it with the last issued one.

The New month page: manual entry without Excel

The screenshot displays the 'New monthly report – manual entry' page. The top navigation bar includes the 'The Marina' logo, programme and asset dropdowns, a reporting period dropdown, and a user profile. The left sidebar lists various modules, with 'Monthly Report' and 'New month (manual entry)' highlighted. The main content area is titled 'New monthly report – manual entry' and contains two main steps:

- 1 Start the month**: A button labeled 'Open' leads to a screen where you are working on 'Monthly Report No 52 – Oct'26'. A note states: 'You are working on Monthly Report No 52 – Oct'26 (cut-off 2026-10-31). Everything you type in the modules below belongs to this report.'
- 2 Enter the month, module by module**: A section with a '0 of 12 ticked' indicator. It lists 12 modules, each with a radio button, a column reference, a '0 this month' indicator, and an 'Open' button:
 - Budget transfers** (column F): Record the budget transfers approved this month.
 - Cost report lines** (column E-S): Add a line for any new contract or package; existing lines carry forward automatically.
 - Change management** (column H, J, K): New RFCs, PVOs that became VOs or DVOs, revised amounts and statuses.
 - Early warnings & risks** (column L): Raise new early warnings; close or convert the ones that became changes.
 - Claims & disputes** (column M): New claims, assessments received and determinations issued.
 - Provisional sums**: Instructions issued and expenditure against each provisional sum.
 - Bonds & insurance**: New or renewed certificates and their expiry dates.
 - Invoices & payments** (column P): Add this month's payment application / IPC for every live contract, and update the final account status.
 - Cash flow**: This month's actual and the updated forecast.
 - Minutes, actions and key issues**: Minutes of the commercial meeting, open actions, and the Key issues text on the Executive Summary.
 - Report control**: Prepared / reviewed / approved by Aconex reference, distribution list.

Three steps on one page: start the month, enter it module by module (each row opens the module, shows how many rows were added or changed this month and which cost report column it feeds, and has a tick box), then review and Lock & issue.

A month entered by hand and a month imported from Excel produce exactly the same outputs: the Executive Summary, movement, Level 1 and Level 2, every schedule, the Claims and Final Account status reports, the emails and the full monthly report are all built from the registers, never from the Excel file. Import when you have the workbook; type when you do not; mix the two freely (for example, type the month and use a stand-alone import for the IPC logs).

Alternative for step 2: if you still prepare the month in your Excel workbook, upload it instead of typing. Chapter 7 shows how. The dashboard reads all the schedules in one go.

Locked months cannot be edited. If you really must correct an issued month, an Admin can Unlock it in Settings → Reporting Periods, make the correction, and Lock it again.

7. Importing your Excel monthly report

You can upload your monthly report workbook exactly as it is. The dashboard recognises both layouts – **The Marina CM Report** (Schedule A to J, FA Status, Early Warning and the Schedule H sheets) and the **VBH Commercial Report** (SCHD A to G, DATA, Report Data, FA Status R1, Early Warning and the "Schedule H ..." sheets) – cleans it up and records everything against a reporting period of the project selected in the top bar. Select the right project first: a VBH workbook goes into the VBH library, a Marina workbook into The Marina's.

Several reports in one go

ST AND-ALONE IMPORTS

Import monthly workbook

Upload one of your Excel monthly reports and the app records it against a reporting period. Each month is stored as its own report, so months can be loaded in any order and each one shows its movement against the last. Claims & Disputes, Bonds & Insurance and Final Account Status are never taken from the workbook: they come only from their stand-alone imports (Claims Tracker, Bonds & Insurance, Final Account Status).

Several reports in one go

Choose all the monthly report workbooks you want in the library (hold Ctrl / ⌘ while picking). Each file is read, its report number and cut-off are taken from the workbook itself, and the reports are imported from the lowest number up – every month is stored as its own report and the highest becomes the live one. A report that already exists and is open is replaced; a locked one is skipped. Files in a layout the app does not recognise are listed so you can import them one at a time below.

Excel files (.xlsx) – as many as you like

Choose Files 2 files ☒ Lock each report after importing [Import 2 reports](#)

File	Report	Result
VBH_Commercial_Report_No_47_Final.xlsx	No 47 · 2026-08-31	Skipped Monthly Report No 47 – Aug'26 is locked (issued). Unlock it in the report library first if it should be replaced.
VBH_Commercial_Report_No_46_Final.xlsx	No 46 · 2026-07-31	Imported Monthly Report No 46 – Jul'26: 1086 added, 0 updated · locked

[Open the report library →](#) [Executive summary →](#)

1 Choose the workbook and the month it belongs to

Your monthly report workbook (.xlsx). The app reads every sheet it recognises: cost report lines, change tracker, claims, early warnings, risks, provisional sums, bonds, contracts, IPC log, budget transfers, project team.

Excel file ☐ Existing period ☒ New period

Report No Cut-off date (month end)

[Read the workbook](#) Nothing is saved at this step; you review the app's reading first.

[1 report\(s\) imported into the library.](#)

The top card of the import page: pick all the workbooks at once. Each file is read, its report number and cut-off are taken from the workbook itself, and the reports are imported from the lowest number up.

- 1 Check the top bar shows the project the workbooks belong to (The Marina or VBH).
- 2 In the left menu, under **Stand-alone imports**, click **Monthly report workbook**. The first card is **Several reports in one go**.
- 3 Click **Choose files** and pick every workbook you want in the library – hold **Ctrl** (Windows) or **⌘** (Mac) while clicking to select several. Leave **Lock each report after importing** ticked for past months.
- 4 Click **Import N reports**. The table fills in as the dashboard works: **Reading...**, then the report number and cut-off it found, then **Imported** with how many rows were added. Older months are imported first and stored as their own reports; the highest number becomes the live report.

- 5 A report that already exists and is open is **replaced** by the new file; a locked one is **skipped** (unlock it in the library first if it should be replaced). A file in a layout the dashboard does not recognise is also skipped – import it on its own with the card below and map its sheets by hand.
- 6 Click **Open the report library** to see every report with its stored copy, then run the three stand-alone imports (Bonds & Insurance, Final Account Status, Claims Tracker) for the months that need them.

One report at a time

The screenshot shows the 'Import monthly workbook' interface in the Commercial Dashboard. The top navigation bar includes filters for Programme (1TB01031 · Marina Villag...), Asset (1TB01031.01 · The Marina), and Reporting Period (Monthly Report No 51 - ...). The sidebar lists modules, with 'Monthly Report' highlighted. The main content area shows the 'Import monthly workbook' form with three numbered steps: 1. Choose the workbook and the month it belongs to (with a file upload button and a dropdown for the reporting period), 2. Existing period / New period (radio buttons), and 3. Read the workbook (a button). The current state shows 'No file chosen' and 'Monthly Report No 51 - Sep'26 · Open'.

Stand-alone imports → Monthly report workbook. Step 1: choose the file and the period.

- 1 In the left menu, under **Stand-alone imports**, click **Monthly report workbook** (the Monthly Report page also has a button for it).
- 2 Click **Choose file** 1 and pick your Excel workbook (.xlsx).
- 3 Choose the period. For a month that does not exist yet choose **New period** 2 ; the report number and cut-off date are filled in from the workbook (Data Input sheet for The Marina, Report Data sheet for VBH). Check them.
- 4 Click **Read the workbook** 3 . Nothing is saved yet. The upload takes a moment for a large file.
- 5 A green box confirms that your report layout was recognised. Below it, each sheet is listed with the register it goes to and the columns it read. Normally there is nothing to change.
- 6 Leave the two boxes ticked: **create missing packages, contractors and dropdown values**, and **Lock the period after importing** (for past months).

7

Click **Import**. A results table shows how many rows were added or updated per sheet, and any row that could not be read with the reason.

The screenshot shows the 'Import monthly workbook' interface. At the top, there are filters for 'PROGRAMME' (1TB01031 · Marina Villag...), 'ASSET' (1TB01031.01 · The Marina), and 'REPORTING PERIOD' (Monthly Report No 51 - ...). The sidebar on the left lists various modules, with 'Monthly Report' highlighted. The main content area has a heading 'Import monthly workbook' and a sub-heading 'MODULE 12'. Below this, there is a section titled '1 Choose the workbook and the month it belongs to' with instructions: 'Upload one of your Excel monthly reports and the app records it against a reporting period. Import past months in date order, locking each one, to build the history; then each new month shows its movement against the last.' The interface includes an 'Excel file' section with a 'Choose File' button and a 'Read the workbook' button. A dropdown menu shows 'Monthly Report No 51 - Sep'26 · Open'. A note at the bottom states: 'Nothing is saved at this step; you review the app's reading first.'

The import page after the workbook was read: one block per sheet, with the columns it recognised.

What happens to your numbers

- Rows are matched by their key (cost code, item number, claim number, IPC number). Uploading the next month **updates** the existing rows and adds the new ones. Nothing is duplicated.
- The cost report reproduces Schedule B: DVOs feed column H, live PVO/VOs feed J, early warnings feed L. The totals for E, F, G, H, J and L tie to the Excel exactly.
- Certified to date (P) is taken from the IPC logs, which are more up to date than the certified column in Schedule B.
- Contractor names are tidied to one spelling each (for example "Al Saad", "ALSAAD GENERAL CONTRACTING" and "ALS - Prelims" all become Al Saad General Contracting Co. Ltd.).

What is special about the VBH workbook

- Cost lines come from **SCHD B**; the sub-asset of each line (Branded Condos .01, Branded Residence .02, Hotel .03, Project Wide .99) is read from the block the line sits in. The **DATA** sheet supplies the contractor, PO number and asset for every ACC reference, so the packages are named "ACC ref – package or contractor" (for example 006C05 – DEPA).
- Contracts are one per PO number (one architect PO can cover several cost lines), valued at the awarded contracts / budget of those lines. The IPC logs come from the "Schedule H ..." sheets; each is matched to its contract by the ACC code or PO number in its heading.

- The change tracker (SCHD C) numbers its items per package, so the dashboard numbers them **CH-<ACC ref>-<item>** (for example CH-006C05-8). Only the ACTIVE amount of each stage feeds the cost report, as in the Excel.
- Allowances that SCHD B carries in its Early Warning column without a row on the Early Warning sheet (the Nammos operator allowances, for example) are imported as early warnings named "EW <ACC ref>", so column L ties to the Excel.
- The green box after reading the file quotes SCHD A's grand totals (budget, DVO, PVO, RFC, early warnings, anticipated final account, certified) so you can compare them with Level 2 after the import. Two differences are expected: the dashboard counts one PVO column where the Excel splits committed and potential PVOs, and **Certified to date** is the gross cumulative certified amount from the IPC sheets, whereas SCHD B shows it net of advance recovery and retention.
- Bonds without an expiry date and FA Status rows for contracts that belong to another project are listed in the green box and not imported.

How each report's data is kept. Every monthly report has its own stored copy of all the registers and of the calculated cost report. The copy is taken when the report's workbook is imported, when the report is locked, and when the next month is started. The **latest** report (highest number) is the live one: the registers you edit belong to it. Every earlier report is shown from its stored copy, read-only, whether or not it is locked. So the movement between two months always compares two stored reports, and you can import the months in any order: importing an older month never disturbs the latest month – the older month is rebuilt from its own workbook (on top of the nearest earlier stored report, or from nothing), stored as its own report, and the latest month's live figures are put back automatically. A stand-alone import into an earlier report updates that report's own stored copy.

Reports that show the same figures month after month (for example 48, 49 and 50 all with the same anticipated final account) were locked with older versions of the dashboard, which froze whatever the live data was at the time. Fix them once: open Monthly Report → All reports (library) and **Re-upload** each report with its own workbook, oldest first, ticking "Lock the period after importing". Each re-upload stores that month on its own; the latest month is never affected.

Locking issues a report. The latest report is frozen from the live registers; an earlier report is issued with the copy stored when it was imported. If an earlier report has no stored copy (it was created before this version and never imported), the dashboard asks you to re-upload its workbook before locking, so another month's figures are never frozen under its name.

Stand-alone imports: update one part of the current report

The screenshot shows the Commercial Dashboard interface. The top bar includes filters for Programme (1TB01031 - Marina Villag...), Asset (1TB01031.01 - The Marina), and Reporting Period (Monthly Report No 51 - ...). The left sidebar lists modules, with 'Bonds & Insurance' highlighted under 'STAND-ALONE IMPORTS'. The main content area is titled 'STAND-ALONE IMPORTS' and 'Import Bonds & Insurance'. It contains instructions to update the bonds and insurance log from Excel. A message states: 'Updating **Monthly Report No 51 – Sep'26** only (the report selected in the top bar). To update another month, change the period in the top bar first.' Below this is a section '1 Choose the Excel file' with instructions to upload a Schedule G (bonds & Insurance) sheet. A file upload button shows 'Choose File No file chosen'. A 'Read the workbook' button is also present. A note indicates: 'Nothing is saved at this step; you review the app's reading first.'

The **Stand-alone imports** section of the left menu: Monthly report workbook, Bonds & Insurance, Invoices & Payments, Final Account Status and Claims Tracker. Each page says which report it will update.

Between monthly reports you often get a fresh Excel for just one thing: a new bonds schedule, the latest IPC logs, an updated FA Status, or the programme-wide Claims Tracker. The stand-alone import pages take that one file and update **only that part** of the report selected in the top bar. Nothing else changes.

- 1 Check the top bar first: the import goes into the reporting period shown there. If that month is locked (issued) the page tells you so and refuses; switch to the open month.
- 2 Open **Stand-alone imports** and pick the page: **Bonds & Insurance**, **Invoices & Payments** (contracts and IPC logs), **Final Account Status** or **Claims Tracker**.
- 3 Choose the file. You can upload the single sheet, the Excel you downloaded from that module's page (a handy way to edit in Excel and re-upload), or even the whole monthly workbook: the page only uses the sheets that belong to it and skips the rest.
- 4 Click **Read the workbook**, check the columns, then **Import**. Rows are matched by their reference (bond ref, PO number and IPC number, ACC code, claim number): existing rows are updated, new rows are added, nothing is duplicated.

The Claims Tracker

Commercial Dashboard | PROGRAMME: 1TB01031 · Marina Villag... | ASSET: 1TB01031.01 · The Marina | REPORTING PERIOD: Monthly Report No 51 - ... | CM: Commercial Manager Admin

STAND-ALONE IMPORTS

Import Claims Tracker

Pick our claims out of the AMAALA Claims Tracker workbook and update Claims & Disputes for the current report.

Updating **Monthly Report No 51 – Sep'26** only (the report selected in the top bar). To update another month, change the period in the top bar first.

[Executive Summary](#)

1 Choose the Excel file

Upload the Claims Tracker workbook (AMA-CM-FRM-0018, the file with the Program_01 sheet). Only the claims whose contract number or asset code belongs to the programme and asset in the top bar are kept; each is linked to our cost report line by its contract code (e.g. 1TB01031C02 → 031C02). Claims already in the dashboard are matched by their letter references and updated; the others are added as CT-###.

Excel file – Claims Tracker (Program_01 sheet)

Choose File claims.xlsx

Read the workbook | Nothing is saved at this step; you review the app's reading first.

2 Check how each sheet was read

The file layout was recognised and converted automatically.

- Claims Tracker as of 2025-09-04: 158 claim(s) in the file, 13 belong to 1TB01031 / 1TB01031.01 and were kept; the rest (other assets) were ignored.
- 13 linked to a cost report line by contract code; 12 matched an existing claim by letter reference (updated), 1 new (numbered CT-###).

For each sheet, confirm which register it is and which column goes to which field. Columns left as "– not used –" are ignored (calculated columns like Latest Budget or Anticipated Final Account should stay unused; the app calculates them). Your choices are remembered for next month.

▼ **Claims Tracker** 13 row(s) | Claims & Disputes (Schedule E) | **48 column(s) mapped**

Column in your sheet	Example values
Claim No (claim no.)	CT-008, CT-009

The AMAALA Claims Tracker workbook after reading: the green box says how many of its claims belong to your programme and how many matched claims already in the dashboard.

The Claims Tracker (form AMA-CM-FRM-0018, the file with the **Program_01** sheet) lists every claim on the whole programme. The dashboard keeps only the rows whose contract number or asset code belongs to the programme and asset in the top bar, for example 1TB01031C02 or 1.TB.01.031.01. Each claim is linked to the right cost report line by its contract code (1TB01031C02 → line 031C02), so the claimed and determined amounts flow into column M of the cost report. Claims already in the dashboard are recognised by their letter references or their description and are updated; claims that are new get the number **CT-** followed by the tracker's item number, so you can always find them again in the tracker.

Time claims and cost claims are separate lines in the tracker (FULL TIA EAR and COST EAR). They stay separate in the dashboard too, marked [Time claim] and [Cost claim] in the description.

Every column of the tracker is kept. Besides the notice, particulars and the four assessments, each claim now carries the tracker's assessment type, the (B–A) and (C–A) business-day counts and compliance flags as the tracker has them, the high-level EAR RFA, the last action / type of discussion, the EAR / HLEAR timetable (trigger date, days allowed and completion date of the draft, the TIA assessment and the finalisation), the assessment-report and EI / DVO status, who the action is with, the remark, rejection ("on merit" or "revise & resubmit"), Notice of Dissatisfaction and Notice of Dispute flags, the KPI closure months and the project dates. Open a claim to see them grouped in their own sections.

The Claims Status Report is correspondingly fuller. After the headline figures, narrative, movement and the register table it adds: ageing of the open claims in the tracker's response-time bands (1–7, 8–14, 15–21, over 21 days), the open claims by action holder, the EAR / HLEAR progress of every claim against the tracker timetable (with overdue steps flagged), a table of rejections, notices of dissatisfaction and disputes, and a claim-by-claim detail section that prints every tracker column for each claim. The Excel version adds a "Claims detail (all columns)" sheet with one row per claim and every field.

Village Boutique Hotel: the monthly workbook is the single source. One upload of the VBH Commercial Report records everything the workbook holds: the cost lines (SCHD B), the change tracker (SCHD C), the early warnings, the bonds & insurance log (SCHD G), the contracts (Schedule H) with every contractor's payment sheet (all of the "Schedule H – contractor" tabs, including sheets with several service or call-off orders, whose cumulative figures are carried across the blocks), the Final Account Status sheet, the project team and distribution list (Report Data), the report reference (kept as the period's Aconex ref), the report checklist ticks, the Stage 2 contract conversion tracker (carried as each contract's final account adjustment) and the "Key period movements" list from the Executive Summary, which becomes the period's key issues narrative. Only the Claims Tracker stays a stand-alone import. The Marina keeps its arrangement.

Invoice & Payment Status Report. Module 8 has its own executive report, next to the Claims and Final Account ones. It opens with the headline position (contracts, revised value, certified, paid, balance still to certify, cash awaiting payment, retention held, average days to certify and to pay), then a written commercial narrative: the position at cut-off, the movement since the previous report, performance against the contractual certification and payment periods, the cash outstanding by age, and the recommended actions. Tables follow: every contract with its certified percentage, amounts awaiting certification and payment and retention held; a summary by contractor; the ageing of certified but unpaid certificates; and every application or certificate that is past its contractual date. Press **Payment status report** on the Invoices & Payments page for the PDF or Excel, or pick it in Reports.

Every schedule now has an executive status report, not just a raw table. Change Management, Early Warnings & Risks / Opportunities, Provisional Sums, Bonds & Insurance and Budget Transfers each get the same treatment as Claims, Final Account Status and Invoice & Payment Tracking: headline KPI tiles, a written commercial narrative (position at cut-off, movement since the previous report, ageing or compliance, outlook), an items-requiring-attention list, and full tables – as PDF or Excel, from a "Status report" button on the module page or from Reports. The module pages themselves also gained interactive charts (hover a bar for the exact figure): an ageing chart for open changes, a value-by-category chart for changes, cover-by-type for bonds & insurance, largest items by budget for provisional sums, and net movement by package for budget transfers. Colour is used only where it carries real meaning – the ageing bars run from good to critical with the age band, never with the item itself – and every chart is a plain bar so a length is compared exactly, not guessed from a wedge.

Which registers the monthly workbook may write. Claims & Disputes come only from the stand-alone Claims Tracker import, for every project and whichever month it is for; the workbook's Schedule E sheet is read but skipped. Bonds & Insurance and Final Account Status depend on the project: for Village Boutique Hotel the monthly workbook carries SCHD G and the FA Status sheet, so both are recorded with every monthly import; for The Marina they come only from their stand-alone imports (Bonds & Insurance, Final Account Status). The switch is in Settings → Programmes → "Monthly workbook feeds Bonds & Insurance and Final Account Status". When an earlier month is rebuilt from

its workbook, the project's stand-alone registers stay exactly as that report holds them, and every other row the workbook does not contain is removed from that report.

8. The modules, one by one

Module 1 – Project Setup & Report Control

TM

The Marina

Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

All reports (library)

New month (manual entry)

STAND-ALONE IMPORTS

Monthly report workbook

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 51 – ...

Open

CM

Commercial Manager

Admin

MODULE 1

Project Setup & Report Control

The cover, index and data-input sheet of the monthly report: who, what and which period.

Project particulars

Edit

Programme name

Marina Village (Programme 1 – Triple Bay)

Programme code

1TB01031

Asset name

The Marina

Asset code

1TB01031.01

Client

The AMAALA Company

Location

Triple Bay, AMAALA

Shown for the Programme and Asset selected in the top bar. Other programmes / assets are managed under Settings.

Report control

Open

Lock period

Report No

51

Reporting period

Monthly

Period

01-Sep-26 – 30-Sep-26

Locked

—

Report number and dates come from the period selected in the top bar.

Manage reporting periods

Aconex reference

e.g. RSG-1TB01031-MCR-049

Document / transmittal reference for this month's report.

PREPARED BY

Name

mm/dd/yy

REVIEWED BY

Name

mm/dd/yy

APPROVED BY

Name

mm/dd/yy

Save report control

Report checklist

0 of 12 done

Tick each module once its section of Monthly Report No 51 – Sep'26 is complete. The checklist is kept per reporting period.

#	Module	Status	Done by	Comment
---	--------	--------	---------	---------

Project particulars, the report checklist, the distribution list and the sign-off names for the current period.

Use it once a month: tick the checklist as the report comes together and fill in Prepared by / Reviewed by / Approved by with the dates. These print on the cover of the report.

Page 27 of 73

Module 2 – Cost Report Level 1 & 2

Level 1 – Executive	Level 2 – Detailed	Line setup			
Cost Report – Executive	Professional Services SAR	Early Works SAR	Construction Works SAR	Management Supervision SAR	Commercial Management SAR
DEVELOPMENT BUDGET					
Previous Approved Budget	28,037,904.00	8,996,107.00	825,126,893.00	17,523,690.00	1,168,246.00
Approved Budget Transfers	52,544.33	0.00	-98,007,197.06	0.00	0.00
Development Budget (currently approved)	28,090,448.33	8,996,107.00	727,119,695.94	17,523,690.00	1,168,246.00
COMMITMENTS					
Contract Awards	18,514,917.11	8,996,107.00	699,877,014.48	0.00	0.00
DVO's (Determined Variation Orders)	1,243,492.42	-139,500.00	6,903,282.44	0.00	0.00
Committed	19,758,409.53	8,856,607.00	706,780,296.92	0.00	0.00
POTENTIAL OUT-TURN COSTS					
PVO's (Potential Variation Orders)	290,000.00	0.00	5,414,361.81	0.00	0.00
RFC's (Requests for Change)	0.00	0.00	640,000.00	0.00	0.00
Early Warnings	0.00	0.00	7,105,062.89	0.00	0.00
Claims	0.00	0.00	0.00	0.00	0.00
BALANCE TO PROCURE					
Uncommitted Packages	0.00	0.00	0.00	0.00	0.00
Anticipated Final Account	20,048,409.53	8,856,607.00	719,939,721.62	0.00	0.00
Variance to Budget	-8,042,038.80	-139,500.00	-7,179,974.32	-17,523,690.00	-1,168,246.00
Previous Report (Monthly Report No 50 – Aug'26)	-8,042,038.80	-139,500.00	-2,419,974.32	-17,523,690.00	-1,168,246.00
Difference	0.00	0.00	-4,760,000.00	0.00	0.00
CASH POSITION					
Certified to Date	16,005,999.23	8,856,607.00	710,764,628.75	0.00	0.00

Level 1 – Executive, laid out exactly like the **Level 01** sheet of your Excel report: one column per cost category (Professional Services, Early Works, Construction Works, Management Supervision, Commercial Management ...), then **Total**, **Previous** (the previous issued report) and **Movement**. Down the side: Development Budget, Commitments (Contract Awards, DVO's, Committed), Potential Out-Turn Costs (PVO's, RFC's, Early Warnings, Claims), Balance to Procure, Anticipated Final Account, Variance to Budget with the previous report and the difference, the cash position, and the comparison with last month's anticipated final account. Below the table, **Reasons for variance – this month** lists every item that moved the anticipated final account, with its amount and remark, and the NET movement. The order of the category columns is the order of Settings → Cost Categories.

Executive view. As on the Excel sheet: Contract Awards, DVOs and the **Remaining Budget Hold** (what is left of each category's hold after it has absorbed that category's changes) make up the commitments; PVOs, RFCs, early warnings, claims and uncommitted packages are added to reach the Anticipated Final Account; Variance to Budget is the difference to the Development Budget. Green is under budget or a decrease; red is over budget or an increase.

Every column is calculated by the dashboard; you never type into the cost report itself except on the Line setup tab. Column letters follow the Excel:

Column	Comes from
E Approved Baseline Budget	Line setup (typed once)
F Budget Transfers	Budget Transfers module (plus transfers brought forward from the Excel)
G Latest Budget	E + F
H Determined VO's	Change Management: approved DVO's
I Committed	G + H
J Potential VO's, K RFC's	Change Management: live PVO / VO and RFC amounts
L Early Warnings	Early Warnings module (open items)
M Claims	Claims module (claims linked to a cost line)
N Anticipated Final Account	I + J + K + L + M
O Variance	N – G
P Certified to Date	Invoices & Payments: latest cumulative certified per contract
Q Works to Complete	N – P
R Previous, S Movement	Last month's locked report and N – R

PROFESSIONAL SERVICES				
PS.031D03	WSP Consultants	WSP Consultants - Employers ...	WSP Middle East	1TB01031.0
PS.031D04	Becon - Marine Relocation	Becon Developments Co - Co...	Beacon Development Company	1TB01031.0
PS.031D01	5 Ocean - Marine Survey 2210091	Five Oceans Marine Survey - ...	Five Oceans Environmental Services LLC	1TB01031.0
PS.031D06	Sydney SeaPlane	Sydney Seaplane - Seaplane ...	Sydney Seaplanes Asia Limited	1TB01031.0
PS.031F03	Haskoning - Navigation Simulation	Haskoning - Navigation Simulat...	Haskoning DHV Saudia	1TB01031.0
PS.031F02	Kaust-King Abdullah University of Science	Kaust-King Abdullah University...	KAUST – King Abdullah University of Science & Technology	1TB01031.0
<i>PS.98</i>	<i>Budget Hold</i>	<i>Remaining budget - Profession...</i>	—	<i>1TB01031.0</i>
Sub-Total Professional Services				
EARLY WORKS				
CN.031C01	ALS - Early Works	Al Saad - Early Works Package	Al Saad General Contracting Co. Ltd.	1TB01031.0
CN.031C03	JVD Early Works	JVD - Early Works	Dredging International Saudi Arabia (JVD)	1TB01031.0
Sub-Total Early Works				
CONSTRUCTION WORKS				
CN.031C02	Al Saad Prelims	Preliminaries and General	Al Saad General Contracting Co. Ltd.	1TB01031.0

Level 2 – Detailed, laid out like the **Level 02** sheet: the lines grouped by cost category, each block ending with its **Sub-Total**, then the GRAND TOTAL, the total excluding the budget hold (the executive view) and the Level 1 – Level 2 check. "Remaining budget" lines are shown in italics. Scroll sideways to see all columns E to S.

Budget hold lines. The "Remaining budget" lines of each category (Professional Services, Construction Works...) are marked as budget hold. They absorb the changes, early warnings and claims of their category up to their own budget, so the category total stays at the approved budget until the hold is used

up; beyond that the excess shows as over budget in the variance, exactly like the Excel Schedule B and Level 1.

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

User guide (PDF)

Change history

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 51 – ...

Open

CM Commercial ManagerAdmin

MODULE 2

Cost Report Level 1 & 2

Schedule A (Level 1, by asset and cost category) and Schedule B (Level 2, by package / contractor). All formulas are calculated by the app.

PDFExcel

Monthly Report No 51 – Sep'26Previous: Monthly Report No 50 – Aug'26Level 1 – Level 2 check OK

RecalculateExport Level 1 & 2 (Excel)

Level 1 – ExecutiveLevel 2 – DetailedLine setup

Set up one line per package / contractor with its approved baseline budget (columns A–E). Packages and contractors come from Settings. Use Import to load them from your Schedule B in one go.

Search cost report lines...

FiltersExportImportAdd Cost line

Asset	Code	Package	Name / description
The Marina	PS.031D03	WSP Consultants	WSP Consultants - Employers Representative
The Marina	PS.031D04	Becon - Marine Relocation	Becon Developments Co - Coastal Conservation Management Plan and C
The Marina	PS.031D01	5 Ocean - Marine Survey 2210091	Five Oceans Marine Survey - Coral Ecology Surveys - 2210091
The Marina	PS.031D06	Sydney SeaPlane	Sydney Seaplane - Seaplane Consultant - 1250665
The Marina	PS.031F03	Haskoning - Navigation Simulation	Haskoning - Navigation Simulation Study
The Marina	PS.031F02	Kaust-King Abdullah University of Science	Kaust-King Abdullah University of Science 2250235
The Marina	CN031C01	ALS - Early Works	Al Saad - Early Works Package
The Marina	CN031C03	JVD Early Works	JVD - Early Works
The Marina	CN031C02	Al Saad Prelims	Preliminaries and General

Line setup: the cost lines with their code, package, contractor, category and baseline budget.

Module 3 – Change Management Tracker

CD Commercial Dashboard

MODULES

Project Setup

Cost Report

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

User guide (PDF)

Change history

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 51 – ...

Open

CM Commercial Manager

Admin

MODULE 3

Change Management Tracker

Every change in one record, followed from Early Warning → RFC → PVO → VO → EI → DVO → Funding. Approved DVOs, live PVO / VOs and RFCs feed the cost report automatically.

PDF Excel

CHANGES

162

121 open

PENDING OVER 30 / 60 DAYS

0 / 106

open items by days since raised

COST REPORT – DVO (H)

8,007,274.86

PVO / VO (J) 5,704,361.81

COST REPORT – RFC (K)

640,000.00

all changes linked to a cost line

Status matrix

Number of changes at each stage by that stage's status

Stage	Cancelled	Approved	Pending	Superseded	Transferred	Review Complete	Other	Total
RFC	50	101	1	2	0	1	0	155
PVO	21	100	1	1	0	0	1	124
VO	15	96	0	0	0	0	1	112
DVO	10	97	2	0	0	0	0	109
Total	96	394	4	3	0	1	2	500

Days open > 30

Days open > 60

Highlighting applies to open changes only. Link each change to its cost report line so its value flows into columns H, J and K.

Q Search change management tracker...

Filters

Refresh

Export

Import

+ Add Change

Contractor / Consultant	Project stage	Change category	Initiated by	Action pending by	Actions
Al Saad General Contracting Co. Ltd.	Post-Contract Variation	Design Dev	Employer	None	🕒 ✎ 🗑
Al Saad General Contracting Co. Ltd.	Post-Contract Variation	Design Dev	Employer	None	🕒 ✎ 🗑

Cards with the totals, the status matrix (how many changes at each stage and status) and the list of changes.

One row per change, followed from Early Warning → RFC → PVO → VO → EI → DVO → Funding. Open the row and fill in each stage as it happens (reference, date, status, amount). The dashboard works out the **current stage**, the **days open** (amber over 30, red over 60) and feeds columns H, J and K of the cost report. Link every change to its **cost report line** in the form, otherwise its value cannot flow into the cost report.

Module 4 – Claims & Disputes

CD Commercial Dashboard | PROGRAMME: 1TB01031 · Marina Villag... | ASSET: 1TB01031.01 · The Marina | REPORTING PERIOD: Monthly Report No 51 - ... | CM Commercial Manager Admin

MODULE 4
Claims & Disputes
 Schedule E: every claim with its notice compliance, detailed claim, assessment by each party and the determination.

CLAIMS
7
 6 pending · 1 Approved

EOT DAYS CLAIMED VS GRANTED
820 → 384
 47% of days claimed granted

SAR CLAIMED VS DETERMINED
46,455,401.69 → 14,631,530.80
 31% of value claimed determined

COST REPORT – CLAIMS (M)
19,471,955.92
 7 claim(s) not linked to a cost line

Assessment ladder
 Totals across all claims at each step of the assessment.

Party	Claims	EOT days	Compensable days	Cost (SAR)
Contractor's Claim	7	820	465	46,455,401.69
Engineer's Recommendation	3	324	147	4,840,425.12
Employer's Assessment	1	324	177	0.00
Determination / Agreement	2	384	0	14,631,530.80

Notice compliance
 Business days use the Sunday–Thursday working week. Public holidays are not excluded.

Notice later than 28 business days: **0**

Detailed claim later than 42 business days: **0**

Column M of the [cost report](#) carries, per claim: the Determination, else the Employer's assessment, else the Engineer's recommendation, else the Contractor's claim. Rejected claims and claims already included in the lump sum carry zero.

Search claims & disputes... | Filters | Export | Import | + Add Claim

Claim No	Description	Status	Claim type	Asset code	Contractor / Consultant
CL-001	Notice of Disatisfaction - Engineer's Instruction N...	Pending	EOT	The Marina	AlSaad General Contracting Co. Ltd.
CL-002	Notice of Disatisfaction - Engineer's Instruction N...	Pending	Prolongation	The Marina	AlSaad General Contracting Co. Ltd.
CL-003	Notice of Dissatisfaction on Engineer's Determina...	Pending	Other	The Marina	AlSaad General Contracting Co. Ltd.
CL-004	Extension of time - Precast Elements for fixed jetti...	Pending	EOT	The Marina	AlSaad General Contracting Co. Ltd.

Summary cards and the claims register.

Type the dates of the notice and of the detailed claim; the dashboard counts business days (Sunday to Thursday) and shows whether the 28-day and 42-day limits were met. Record the contractor's claim, the engineer's recommendation, the employer's assessment and the determination in their own sections.

The Claims Status Report

TM The Marina Commercial Dashboard | PROGRAMME: 1TB01031 · Marina Villag... | ASSET: 1TB01031.01 · The Marina | REPORTING PERIOD: Monthly Report No 51 - ... | CM Commercial Manager Admin

MODULE 4
Claims & Disputes
 Schedule E: every claim with its notice compliance, detailed claim, assessment by each party and the determination.

CLAIMS
14
 8 pending · 4 Approved · 2 Rejected

EOT DAYS CLAIMED VS GRANTED
1,818 → 381
 21% of days claimed granted

SAR CLAIMED VS DETERMINED
52,412,068.79 → 29,263,061.60
 56% of value claimed determined

COST REPORT – CLAIMS (M)
14,631,530.80
 1 claim(s) not linked to a cost line

Claims status report | PDF | Excel | Email claim status report

The **Claims status report** buttons in the page header (PDF and Excel) produce the executive claims report for the month selected in the top bar.

Claims Status Report

1TB01031 · Marina Village (Programme 1 – Triple Bay) · Monthly Report No 51 – Sep'26 · DRAFT (period not locked) · generated 10-Sep-26 15:47

CLAIMS RECORDED 14 8 pending · 4 determined · 2 rejected	CONTRACTORS WITH CLAIMS 3	CLAIMED (SAR) 52,412,068.79 1818 EOT days claimed	DETERMINED (SAR) 29,263,061.60 56% of value · 381 days granted
OPEN EXPOSURE (SAR) 52,412,068.79 gross value of pending claims	CARRIED IN COST REPORT (M) 14,631,530.80 determined / assessed amounts	LATE NOTICES / PARTICULARS 0 / 0 later than 28 / 42 business days	DISPUTES 2 Notice of Dissatisfaction / Dispute

Commercial narrative

Position at cut-off

As at 30-Sep-26, 14 claims are recorded against 1TB01031.01 The Marina from 3 contractors: 8 pending, 4 determined or approved and 2 rejected. Contractors have claimed SAR 52,412,068.79 and 1818 days of extension of time; determinations to date total SAR 29,263,061.60 and 381 days, i.e. 56% of the value and 21% of the time claimed. The open claims carry a gross exposure of SAR 52,412,068.79, of which SAR 14,631,530.80 is carried in the cost report (column M); the balance is reported through the early warnings until determined.

Movement since Monthly Report No 50 – Aug'26

7 new claims were received (CT-008, CT-061, CT-069, CT-084 and 3 more). 5 claims changed status or value (CL-002, CL-004, CL-005, CL-006 and 1 more). The claims column of the cost report moved by nil.

Exposure and status of open claims

The largest open item is CT-008 (Al Saad General Contracting Co. Ltd., Prolongation) at SAR 46,455,401.69, currently at the stage "Employer's assessment issued – awaiting determination" with action resting with Employer's Representative. Across the 8 open claims: 3 employer's assessment issued – awaiting determination; 2 resubmitted – under assessment; 3 detailed claim received – under assessment. Where an assessment exists, the assessed value totals SAR 14,631,530.80 against SAR 46,455,401.69 claimed for the same items.

Compliance and risk

All claims were notified and particularised within the contractual time limits. 2 claims have escalated to a Notice of Dissatisfaction or Dispute and are being managed with legal support.

Outlook and recommended actions

The commercial team's priorities for the coming period are to complete the assessment of the claims under review and issue the Engineer's recommendations, close out the determinations issued and agree final values with the contractors. Determined amounts will be carried into the cost report and, where budget is not available, funded through the change management process.

Since Monthly Report No 50 – Aug'26

- New: CT-008 EOT 1 Prolongation
Engineer's Instruction No. 5, 7, 9 & 10 [Cost claim] (SAR 46,455,401.69)
- New: CT-061 EOT-02 TB Marina Project - Request for Extension of Time [Time claim]
- New: CT-069 Costs Claim Requests associated with EOT-2 (cost claim related to item 61 above) [Cost cla (SAR 5,155,062.34)]

1TB01031 · Monthly Report No 51 – Sep'26 · DRAFT (period not locked)

Page 1 of 3

Page 1 of the report: headline figures, the written narrative and the items requiring attention. The claims table and the by-contractor summary follow.

Once the month's claims are in (typed in, imported from the monthly workbook or picked out of the Claims Tracker), press **Claims status report** → **PDF**. The dashboard writes the report itself: the position at cut-off (how many claims, claimed versus determined value and time), the movement since the last issued report, the exposure and stage of every open claim, compliance with the notice periods and any disputes, and the recommended actions. Nothing is typed by hand, so the words always match the numbers. The Excel version carries the same content for editing. The blue **Email claim status report** button next to it works exactly like "Email the Report" on the Executive Summary: it writes a short email with the headline table and narrative and opens it in Outlook with the Claims Status Report PDF attached.

Module 5 – Early Warnings and Risks & Opportunities

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

User guide (PDF)

Change history

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 51 – ...

Open

CM Commercial ManagerAdmin

MODULE 5

Early Warnings & Risks / Opportunities

Early warning notices (feeding column L of the cost report) and the commercial risk & opportunity register with its heat map.

PDF

Excel

Early Warnings (7)

Risks & Opportunities (2)

EARLY WARNINGS

7

6 open · 1 converted to RFC · 0 closed

OPEN – POTENTIAL COST (L)

7,105,062.89

all open items linked to a cost line

OPEN – POTENTIAL TIME

0 days

sum of potential time impact

OPEN BY LIKELIHOOD

Low 0

Med 3

High 3

Open early warnings feed column L of the [cost report](#). When one becomes an RFC, set its status to *Converted to RFC* and link the change item so the value moves to the change tracker instead.

Q Search early warnings...

Filters

Export

Import

+ Add Early Warning

EW No ^	Date raised ^	Raised by ^	Package ^	Contractor / Consultant ^	Description ^
EW	31-Aug-26	Contractor	Elmar-Hijaz Boardwalk and Jetties	Elmar Marinas Khaleej LLC	Additional Slipway at Nabateen S
EW-07	06-Sep-26	Contractor	Al Saad Main Works	Al Saad General Contracting Co. Ltd.	Dredge spoil disposal site nearing
EW-22	31-Aug-26	Contractor	Al Saad Prelims	Al Saad General Contracting Co. Ltd.	Non Provision of Employer's Faci
EW-22-2	31-Aug-26	Contractor	Elmar-Hijaz Boardwalk and Jetties	Elmar Marinas Khaleej LLC	Elmar EOT-01 Cost Claim
EW-23	31-Aug-26	Contractor	MME-MME Marine Engg	MME – Majestic Marine Engineering LLC	EOT-02 COST – MME – Eextensio
EW-23-2	31-Aug-26	Contractor	MME-MME Marine Engg	MME – Majestic Marine Engineering LLC	Additional scope of Tographic Su
EW-23-3	31-Aug-26	Contractor	Elmar-Hijaz Boardwalk and Jetties	Elmar Marinas Khaleej LLC	MEP works, Aerodrom Installation,

7 of 7 early warnings · double-click a row to edit

Two registers on one page, with the heat map of risks and opportunities.

Open early warnings feed column L of the cost report. When an early warning becomes an RFC, set its status to "Converted to RFC" and it drops out of column L (the RFC takes over in column K/J).

Page 34 of 73

Module 6 – Provisional Sums

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

User guide (PDF)

Change history

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 51 – ...

Open

CM Commercial Manager

Admin

MODULE 6

Provisional Sums

Provisional sum allowances, what has been instructed against each, and the saving or extra that results.

TOTAL BUDGET

124,000,000.00

16 provisional sum(s)

TOTAL INSTRUCTED

50,477,392.65

5 of 16 item(s) with a contract value

TOTAL SAVING

28,522,607.35

Instructed value below budget

BY STATUS

Pending 15

Approved 1

(Saving) / Extra = Contract value – Budget. Savings show in green with a minus sign, extras in red. The totals row at the bottom of the table follows your search and filters. Statuses are managed under Settings → Provisional Sum Statuses.

Q Search provisional sums...

Filters

Export

Import

+ Add Provisional Sum

Item	Description	Status	Contractor	Budget	Contract value
PS-01	Allowance for Marine furniture steel support	Pending	Al Saad General Contracting Co. Ltd.	5,000,000.00	520,531.00
PS-02	Allowance for coordination with utilities	Pending	Al Saad General Contracting Co. Ltd.	2,500,000.00	—
PS-03	Dry stack access ramp	Pending	Al Saad General Contracting Co. Ltd.	1,000,000.00	—
PS-04	ECO Marine habitat to promote marine environment	Pending	Al Saad General Contracting Co. Ltd.	15,000,000.00	—
PS-05	Archl finish coordinated with external public realm	Pending	Al Saad General Contracting Co. Ltd.	2,000,000.00	1,059,783.36
PS-06	Bridge interface	Pending	Al Saad General Contracting Co. Ltd.	5,000,000.00	—
PS-07	Porous edge treatment following wave study	Approved	Al Saad General Contracting Co. Ltd.	12,000,000.00	621,261.23
PS-08	shoring to quay wall due to reduced set back	Pending	Al Saad General Contracting Co. Ltd.	48,000,000.00	48,000,000.00
PS-09	Labs & testing requirements	Pending	Al Saad General Contracting Co. Ltd.	1,000,000.00	—

Budget, instructed value and the (saving) / extra, worked out for you.

Page 35 of 73

Module 7 – Bonds & Insurance

Commercial Dashboard | PROGRAMME: 1TB01031 · Marina Villag... | ASSET: 1TB01031.01 · The Marina | REPORTING PERIOD: Monthly Report No 51 - ... | CM Commercial Manager Admin

MODULE 7
Bonds & Insurance
 Every bond and insurance policy: what the contract requires, what has been provided, and when it expires.

BONDS & POLICIES
38
 29 expired · 0 within 30 days · 0 with...

PROVIDED VS REQUIRED
683,882,463.51 / 314,714,52...
 total face value held vs total contrac...

SHORT FALLS
2
 0.06 below requirement in total

CHECKS OUT STANDING
 Not approved **10**
 Bank not verified **5**

Bonds & insurance expiring soon
29 already expired.
29 within 60 days

expired 679d	G-10b · Professional Indemnity · WSP Middle East	31-Oct-24
expired 649d	G-12 · Workmen's Compensation · WSP Middle East	30-Nov-24
expired 618d	G-05 · Advance Payment Bond · Al Saad General Contracting Co. Ltd.	31-Dec-24
expired 537d	G-03 · Public/Third Party Liability · Al Saad General Contracting Co. Ltd.	22-Mar-25
expired 537d	G-11 · Public/Third Party Liability · WSP Middle East	22-Mar-25
expired 528d	G-04 · Contractors All Risks · Al Saad General Contracting Co. Ltd.	31-Mar-25
expired 511d	G-02 · Professional Indemnity · Al Saad General Contracting Co. Ltd.	17-Apr-25
expired 467d	G-20 · Advance Payment Bond · Al Saad General Contracting Co. Ltd.	31-May-25

Open the Bonds & Insurance log →

Rows turn amber within 60 days of expiry and red within 30 days or once expired. Contract requirement = the % entered × revised contract value (or the original sum if no cost line is linked), or the fixed SAR amount. Types are managed under Settings → Insurance / Bond Types.

Search bonds & insurance... | Filters | Export | Import | + Add Bond / Insurance

Ref | Contractor / Consultant | Package | Type of bond / Insurance | Policy /

Every bond and policy with its expiry. Rows turn amber 60 days before expiry and red 30 days before or once expired.

Contract requirement is either a percentage of the contract value or a fixed SAR amount; the variance to what was provided is calculated. Bonds expiring soon also appear on the Executive Summary.

Filter Expiring within 30 days | Clear | Report on this filter | PDF | Excel

EXPIRY
 All 69 | Expired or within 30 days 38 | Expired 34 | Expiring within 15 days 2 | **Expiring within 30 days 4** | Expiring within 60 days 8 | Active (over 60 days) 24

Released or superseded 3

TYPE
Bonds & insurance 4 | Bonds only 1 | Insurance only 3 | Other 0

Showing 4 of 69 item(s). The figures, the chart, the log below and the PDF / Excel report all follow this filter.

FILTERED BONDS & POLICIES
4
 0 expired · 4 within 30 days · 0 within 60 days

PROVIDED VS REQUIRED
3,802,917.50 / 3,802,917.50
 total face value held vs total contract requir...

SHORTFALLS
0
 every item meets its requirement

CHECKS OUTSTANDING
 Not approved **0** | Bank not verified **4**

The filter at the top of the page. Every chip shows how many items it holds, and the whole page – figures, expiring list, chart, log and the PDF / Excel report – follows whatever you pick.

Filtering the page and the report. The filter sits above the figures and has two rows of chips. **Expiry:** All, Expired or within 30 days (the chase list), Expired, Expiring within 15 days, Expiring within 30 days, Expiring within 60 days, Active (over 60 days), and Released or superseded. The windows are cumulative, so "within 30 days" also holds everything in "within 15 days"; each chip carries its own count, and the counts update as you pick on the other row. **Type:** Bonds & insurance (everything), Bonds only, Insurance only or Other. Each bond type is sorted into one of the three from its name – anything with "bond" or "guarantee" in it is a bond, indemnity / liability / all-risks / compensation / marine / motor / plant

policies are insurance, and the rest (a trade licence, for example) is "other". Change the type names under Settings → Insurance / Bond Types and the sorting follows.

The downloads follow the filter. Press **Report on this filter** → **PDF** or **Excel** in the filter card and you get the Bonds & Insurance Status Report for exactly what is on screen: the filter is printed at the top, the headline figures count only the filtered items, and the report lists every one of them in full (ref, contractor, package, type, category, required, provided, expiry, days and status) instead of only the 60-day window. The file name says which filter it was, for example *Bonds_and_Insurance_Status_Report_Expiring_within_15_days_insurance_only_...*. The **Export** button in the log's own toolbar downloads the same filtered rows as a plain Excel table. Clear the filter and everything goes back to the whole register.

Each row has a **Status: Active, Expiring, Expired, Released or Superseded**. A policy is **Released** when its contract is finished, so an old expiry date is not a problem and it is not counted as expired. The dashboard works this out for you from the **Final Account Status** (Closed, Not required or Direct payment), which decides first, and from the contract status in Invoices & Payments (Closed, Completed, Terminated) where a contract has no final account row. Contracts are recognised by their code (031C02), so closing one contract releases the bonds on all of its cost lines (CN.031C02 and CN.031C02-2 alike). When you import the Excel report the FA Status sheet and the CLOSED contracts in Schedule H are read the same way. You can also tick **Contract closed – bond released** on the row yourself. **Superseded** means a newer policy of the same type is held for the same contract, so the old one is ignored too.

Customise my reports

REPORTS

Customise my reports

Build the report you want: pick the records, filter on any field, choose the columns, group and total them, and take it away as a PDF, an Excel workbook or a written Word summary.

WHAT DO YOU WANT TO REPORT ON?

Payments due & ageing

▼

Everything certified and not yet paid, bucketed into overdue, due within 14 / 30 days, due later, and certified with no invoice – with VAT added or withholding tax deducted, and what is owed in total.

· 221 record(s) before filtering

1 filter(s) set. Nothing is built until you click Generate.

Generate report

PDF

Excel

Word summary

Title and note

What the report is called and anything you want printed under the title.

REPORT TITLE (OPTIONAL)

Payments due & ageing

YOUR NOTE, PRINTED UNDER THE TITLE

e.g. For the commercial review on 3 October.

Filters

Every field can be filtered, and you can add as many conditions as you like.

FILL THE FILTERS IN FOR ME

Overdue only

Overdue or due within 14 days

Certified, no invoice

A starting point only – it fills in the filters below, which you can then change. Nothing is built until you click Generate.

Records must match

all of these

Payment status

is any of

Certified – invoice not yet raised

Due later

Due within 14 days

Due within 30 days

Choose the records at the top, set as many filters as you want, pick the columns and grouping, then click Generate report. Nothing is built until you ask for it.

Build the report you want, rather than the one the dashboard happens to print. Reports & downloads

→ **Customise my reports** (also in the left menu) opens a set-up page, not a list of ready-made reports. Pick what to report on in the box at the top – any register the project keeps – cost lines, changes, claims, early warnings, provisional sums, bonds, contracts, the IPC log, final accounts, budget transfers, meeting actions – or from one of five purpose-built reports the dashboard works out across several modules at once:

- **Payments due & ageing.** Everything certified and not yet paid, put into the bucket that says what to do with it: already overdue, due within 14 days, due within 30 days, due later, or certified with no invoice raised yet. VAT is added to the certified amount and withholding tax is deducted, so the "total due" is what actually leaves the bank. Set which applies to each contract under Invoices & Payments → the contract's form → Contract settings → **Tax on payment**; the rate is the VAT % on the same form. Ageing counts from the date each payment falls due, not from the certificate date.
- **EOT & claims action tracker.** Every claim as an action list: who it is pending with, the owner, what the last action was and how many days ago, the target date for the next step, and a flag – On track (14 days or less), Watch (15–30) or Stuck (over 30). Three fields on the claim feed it: **Owner**, **Date of last action** and **Target date for the next step**, under the claim's Actions section. Leave the date of last action empty and the tracker counts from when the row was last edited.
- **What needs attention (whole project).** One list of everything late, expiring or stuck, pulled from every module at once – bonds about to lapse, payments past their date, claims that have gone quiet, changes going nowhere, overdue meeting actions, final accounts past their forecast closure, contracts certified beyond their value. It is built as a decision queue: every line says what happens if nothing is done, and the list is ranked by what is at stake weighted by how long it has been waiting, not by which module it came from.
- **Contract performance scorecard.** One line per contract drawing on every module: value, certified, paid, what is certified and unpaid, payments overdue, average days late, open changes and claims, bond cover and the final account position.
- **Contract value bridge.** What each contract was let for, what moved it – approved variations, approved claims and the final account or Stage 2 remeasure adjustment – and what it is worth now, with the movement as a percentage of the original price.

Filter on anything. Add as many conditions as you like; every column of the chosen report is offered, and the test on offer follows the kind of column it is. Text columns take contains / does not contain / is exactly / is empty; numbers take between / at least / at most; dates take between / before / after / in the last N days / in the next N days / in the past (overdue); and any column with a fixed set of values (a status, a contractor, a package, a bond type) is offered as a tick-list – "is any of" / "is none of". Records can be made to match *all* of the conditions or *any* of them. Each report also offers one-click starting points ("Overdue only", "Stuck – over 30 days", "Expiring within 30 days"), which simply fill the filter in for you and can then be changed.

Choose what is printed. Tick the columns and put them in the order you want with the arrows, group the records by any field (each group gets its own subtotal, and the report gets a grand total), sort by up to two columns, and trim to the first N records.

How much do you want in it?

REPORTS

Customise my reports

Build the report you want: pick the records, filter on any field, choose the columns, group and total them, and take it away as a PDF, an Excel workbook or a written Word summary.

WHAT DO YOU WANT TO REPORT ON?

Payments due & ageing

Everything certified and not yet paid, bucketed into overdue, due within 14 / 30 days, due later, and certified with no invoice – with VAT added or withholding tax deducted, and what is owed in total.

· 221 record(s) before filtering

1 filter(s) set. Nothing is built until you click Generate.

[Generate report](#) [PDF](#) [Excel](#) [Word summary](#)

Title and note

What the report is called and anything you want printed under the title.

REPORT TITLE (OPTIONAL)

Payments due & ageing

YOUR NOTE, PRINTED UNDER THE TITLE

e.g. For the commercial review on 3 October.

Filters

Every field can be filtered, and you can add as many conditions as you like.

FILL THE FILTERS IN FOR ME

[Overdue only](#) [Overdue or due within 14 days](#) [Certified, no invoice](#)

A starting point only – it fills in the filters below, which you can then change. Nothing is built until you click Generate.

Records must match [all of these](#)

Payment status

is any of

Certified – invoice not yet raised
Due later
Due within 14 days
Due within 30 days
Overdue

[+ Add a filter](#)

Columns

Choose what is printed, and the order it is printed in.

Payment status

Contract code

Contractor / consultant

IPA / IPC reference

Group, sort and trim

GROUP BY (WITH A SUBTOTAL PER GROUP)

Contractor / consultant

SORT BY

Days overdue / remaining

A → Z / low

How much do you want in it?

Pick the shape of the report. Each one is a starting point – the ticks underneath can still be changed.

One-pager [PDF or Word](#)

The answer on a single page: the headline figures, the written position and what needs attention. No tables.

Detailed summary [PDF or Word](#)

The answer on a single page: the headline figures, the written position and what needs attention. No tables.

Full report [PDF or Word](#)

The answer on a single page: the headline figures, the written position and what needs attention. No tables.

Records only [Excel](#)

Just the records and their totals, with nothing written – for when you want to work on the figures yourself in Excel.

Four shapes of report, from a single page to the records on their own. Each one is a starting point – the ticks underneath still change any individual part.

Under **How much do you want in it?** the same records can be turned into four different documents:

- **One-pager.** The answer on a single page: the headline figures, the written position and what needs attention, with no tables at all. For the PDF this really is one page – the sort of thing that goes to a director or in front of a meeting.
- **Detailed summary.** The figures and the commentary with the breakdown and the ageing behind them, but not the full list of records. Usually two or three pages.
- **Full report.** Everything: the figures, the commentary, the breakdown, the ageing and every record with its subtotals.
- **Records only.** Just the records and their totals, with nothing written – for when you want to work on the figures yourself in Excel.

The label on each says which file it is meant for, but the choice is the *shape* of the report, not the format: whichever you pick, all three downloads stay available, so a one-pager can come out as a PDF, a Word document or an Excel workbook. Under the styles, **What to include** lets you tick or untick any single part – the headline figures, the commentary, the "needs attention" list, the breakdown, the ageing analysis or the records – and the style then shows as your own mix.

Nothing is built until you ask for it. Choosing the records, adding filters and changing the columns builds nothing: the page waits until you click **Generate report**. Once it has run, the report appears underneath the set-up and the PDF, Excel and Word buttons come to life. Change anything afterwards and the page says the set-up has changed and the downloads are held back until you generate it again, so a file can never be a different report from the one on screen.

A filter you have added but not yet given a value to is ignored rather than treated as "matches nothing", and is marked in amber so you can see it is not doing anything yet. With no filters at all the report simply covers every record.

Three files, one set of figures. What is on screen is the report; the three buttons at the top give you the same thing as a file.

- **PDF** – the printed report: the answer in one sentence at the top, the headline figures, the commentary, what needs attention, the analysis and the records, with the filter and a basis-of-preparation note printed so the reader knows exactly what they are looking at.
- **Excel** – two sheets. *Report* is the presented version with subtotals; *Data* is the same records flat, one header row, no merged cells, filters on and numbers written as real numbers, so you can pivot it without unpicking anything.
- **Word summary** – the report written up as a document: a one-page executive summary (the bottom line in a sentence, the points that carry it with their figures, and what is needed and from whom), then the position in detail, the analysis, the records and the basis of preparation. It is the dashboard's own writing, worked out from the same figures the tables print, so the words can never disagree with the numbers.


Amounts in all three are shown in whole SAR with negatives in brackets, a dash where there is nothing to show, and the unit named in the column heading rather than repeated in every cell.

How the reports are coloured. The palette is deliberately restrained: the colours sit at about a third to a half of full strength, in the range the financial press prints with, because a fully saturated colour is what makes a page look cheap. Colour is used to separate one part of the page from another – a rule under the title, a tinted band behind each section heading, a warm panel around the headline sentence, a tinted callout around each point that needs action – and to mark the exceptions in a table. It is never spread across a whole row or a whole column, so an exception still stands out.


Nothing depends on seeing the colour. Every status carries three things at once: its colour, its own shape (a triangle for something adverse, a square for something to watch, a circle for something in order) and the word itself. That matters because these reports get photocopied and forwarded: muted colours are the first thing to disappear in greyscale, and red against green is the pair that colour-blind readers cannot separate. The bars beside the breakdown and ageing tables step through one colour from dark to light rather than changing colour, so they stay in order in a photocopy, and each carries its own figure.

Save a report you will want again. Give the set-up a name and it is kept in the **Saved reports** box at the top of the page; pick it next month and the whole set-up comes back, ready to generate against that month's figures.

Module 8 – Invoices & Payments

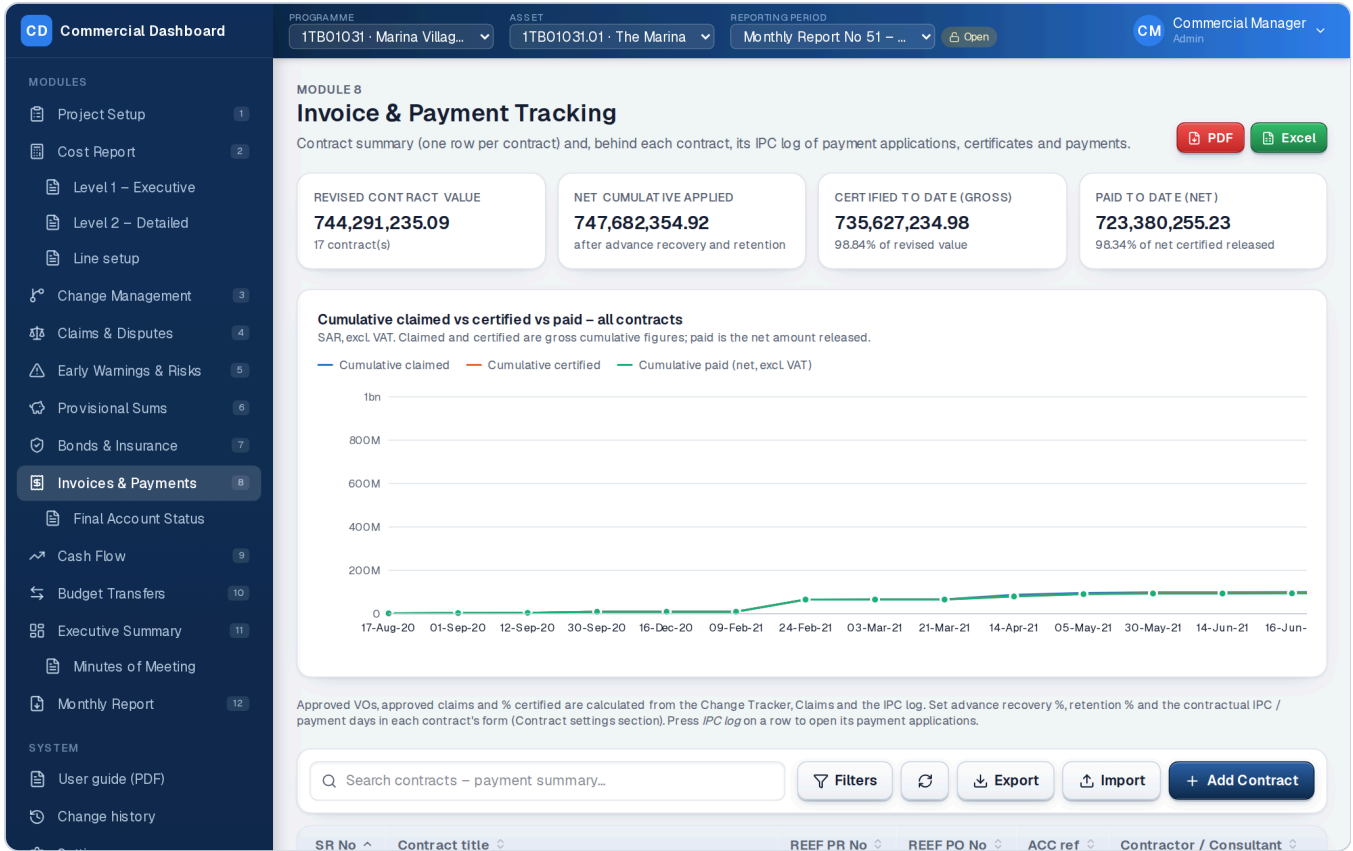

The contract summary (one row per contract) with cumulative applied, certified and paid, and the % certified.

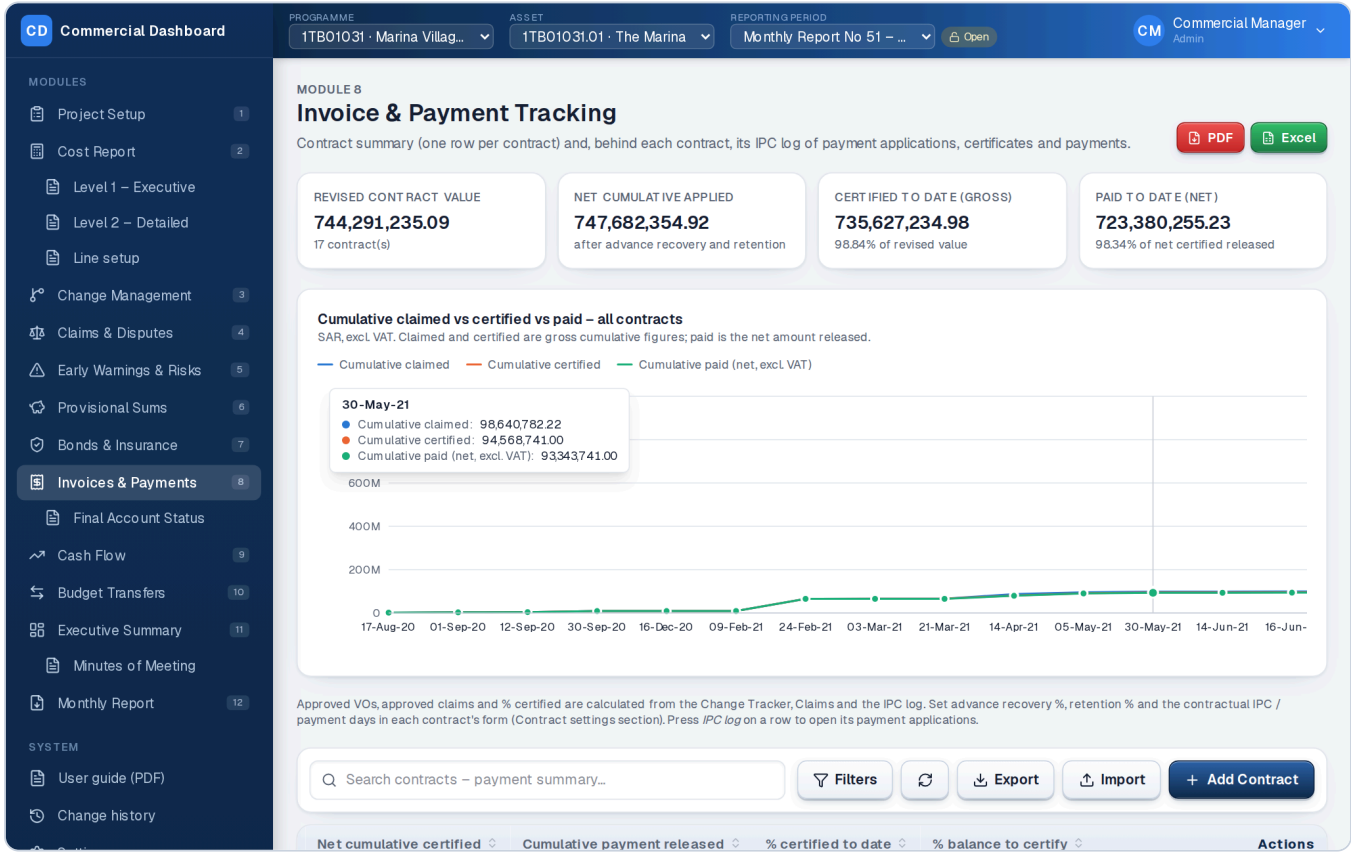

Click a contract to open its IPC log. Add one row per payment application. Due dates for the IPC and the payment are worked out from the contract settings (days to issue IPC, days to pay).

Module 8 – Final Account Status

CD Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 51 - ... [Open](#)

CM Commercial Manager Admin

MODULE 8

Final Account Status

One row per contract: is the final account statement open, signed or not required, and when is closure expected. Committed cost and the anticipated final account are read from the cost report line, so the totals tie to Schedule B.

[PDF](#) [Excel](#)

OPEN	CLOSED (FAS SIGNED)	NOT REQUIRED / DIRECT PAYMENT	TOTAL PACKAGES
6 161,839,134.63 anticipated final account - 2 past forecast date	5 228,091,410.28 anticipated final account	6 8,907,406.57 anticipated final account	17 398,837,951.48 total anticipated final account

Days remaining turn amber within 60 days of the forecast closure date and red once it has passed (open final accounts only). Link each row to its cost report line so the values stay in step with Schedule B.

Q Search final account status... [Filters](#) [Export](#) [Import](#) [+ Add Final Account](#)

ACC code	Package / description	Contractor / Consultant
PS.031D01	Five Oceans Marine Survey - Coral Ecology Surveys - 2210091	Five Oceans Environmental Services LLC
PS.031D03	WSP Consultants - Employers Representative	WSP Middle East
PS.031D04	Becon Developments Co - Coastal Conservation Management Plan and Coral Relocation	Beacon Development Company
PS.031D06	Sydney Seaplane - Seaplane Consultant - 1250665	Sydney Seaplanes Asia Limited
PS.031F02	Kaust- King Abdullah University of Science 2250235	KAUST – King Abdullah University of Science & Technol
PS.031F03	Haskoning - Navigation Simulation Study	Haskoning DHV Saudia
CN.031C01	AlSaad - Early Works Package	Al Saad General Contracting Co. Ltd.
CN.031C02	AlSaad-Marina Basin	Al Saad General Contracting Co. Ltd.

One row per contract: is the final account open, signed (closed) or not required, and when closure is expected. The committed cost and anticipated final account come from the cost report line.

The Final Account Status Report

TM The Marina Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 51 - ... [Open](#)

CM Commercial Manager Admin

MODULE 8

Final Account Status

One row per contract: is the final account statement open, signed or not required, and when is closure expected. Committed cost and the anticipated final account are read from the cost report line, so the totals tie to Schedule B.

[Final account status report](#) [PDF](#) [Excel](#) [Email final account status report](#)

[PDF](#) [Excel](#)

OPEN	CLOSED (FAS SIGNED)	NOT REQUIRED / DIRECT PAYMENT	TOTAL PACKAGES
6 161,839,134.63 anticipated final account - 2 past forecast date	5 228,091,410.28 anticipated final account	6 8,907,406.57 anticipated final account	17 398,837,951.48 total anticipated final account

On the Final Account Status page: **Final account status report** (PDF and Excel) and **Email final account status report**.

Final Account Status Report

1TB01031 · Marina Village (Programme 1 – Triple Bay) · Monthly Report No 51 – Sep'26 · DRAFT (period not locked) · generated 10-Sep-26 15:52

PACKAGES TRACKED 17 6 open · 5 closed · 6 not required	OPEN (SAR) 161,839,134.63 anticipated final account of open packages	CLOSED – FAS SIGNED (SAR) 228,091,410.28	NOT REQUIRED / DIRECT PAYMENT (SAR) 8,907,406.57
TOTAL ANTICIPATED FINAL ACCOUNT 398,837,951.48 all tracked packages	UNCOMMITTED ON OPEN PACKAGES 12,849,424.70 still to be agreed	PAST FORECAST CLOSURE DATE 2 0 due within 60 days	NO FORECAST DATE 0 open packages

Commercial narrative

Position at cut-off

As at 30-Sep-26, 17 contract packages are tracked for final account on 1TB01031.01 The Marina: 6 open (SAR 161,839,134.63 anticipated final account), 5 closed with the final account statement signed (SAR 228,091,410.28) and 6 not requiring a final account or paid directly (SAR 8,907,406.57). The anticipated final account across all packages is SAR 398,837,951.48, of which SAR 12,849,424.70 on the open packages is not yet committed and remains to be agreed.

Movement since Monthly Report No 50 – Aug'26

2 packages changed status or anticipated final account (CN.031C10, CN.031C15). The anticipated final account of the tracked packages moved by -5,360,000.00.

Closure programme

2 packages are beyond the forecast closure date and need a revised programme or escalation. The next closure is forecast for 30-Jul-26 (CN.031C12 Al Saad General Contracting Co. Ltd.). Every open package has a forecast closure date.

Outlook and recommended actions

The commercial team's priorities are to close out the overdue final accounts and agree revised dates where the statement cannot be signed this period, agree the SAR 12,849,424.70 of uncommitted value through the change and claims processes so it can be committed before closure. Signed final account statements release the retention and bonds held for each package.

Since Monthly Report No 50 – Aug'26

- CN.031C10 MME Marine Engineering: Open -> Open (AFA +640,000.00)
- CN.031C15 Elmar-Hijaz Boardwalk and Jetties: Open -> Open (AFA -6,000,000.00)

Items requiring attention

- 2 final accounts past the forecast closure date (CN.031C12 Al Saad General Contracting Co. Ltd., PS.031F02 KAUST – King Abdullah University of Science & Technology) – revise the forecast or escalate the closure.
- Largest uncommitted balances still to be agreed: CN.031C10 SAR 6,295,062.89; CN.031C15 SAR 6,264,361.81; PS.031F03 SAR 290,000.00.

Final account status by package

Open packages first, earliest forecast closure first. Committed and anticipated final account are read from the cost report.

Page 1 of the report: headline figures, the narrative (position, movement, closure programme, actions) and the items requiring attention, followed by the package table.

The report reads the Final Account Status register for the month in the top bar and writes the narrative itself: how many packages are open, closed or not required and their anticipated final account, what changed since the last issued report, which closures are overdue or due within 60 days, the uncommitted value still to be agreed, and the recommended actions. The email button opens the same summary in Outlook with the PDF attached, addressed to the distribution list.

Module 9 – Cash Flow

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

User guide (PDF)

Change history

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 51 – ...

Open

CM Commercial ManagerAdmin

MODULE 9

Cash Flow

Monthly forecast per contract against the actual payments made, with the cumulative picture and what has been certified but not yet paid.

PDF

Excel

Monthly grid

Cumulative chart

Accruals (6)

Months: Sep'20 – Apr'26

Refresh

Export (Excel)

Type a forecast in any month and press Tab or click away to save. Actuals = net payments (excl. VAT) by paid date from Payment Tracking, unless overridden. Click an actual to override it; clear the box to go back to the automatic value. Difference = Actual – Forecast (red = more than forecast).

Transaction No	Supplier	Line Description	Coding	CBS	Programme	
—	Five Oceans Environmental Services LLC	Coral Ecology Surveys	—	—	1TB01031	
—	Beacon Development Company	Coastal Conservation Manage...	—	—	1TB01031	
—	Al Saad General Contracting Co. Ltd.	Triple Bay Marina Basin – Early...	—	—	1TB01031	
—	Dredging International Saudi Arabia (JVD)	Triple Bay Marina Basin – Early...	—	—	1TB01031	
—	Five Oceans Environmental Services LLC	Marina Ecological Coral Surveys	—	—	1TB01031	
—	WSP Middle East	Marina Basin Supervision Con...	—	—	1TB01031	
—	Al Saad General Contracting Co. Ltd.	Triple Bay Marina Basin – Desl...	—	—	1TB01031	
—	Five Oceans Environmental Services LLC	Marina Ecological Coral Reloc...	—	—	1TB01031	
—	MME – Majestic Marine Engineering LLC	Design and Construction of FL...	—	—	1TB01031	
—	Al Saad General Contracting Co. Ltd.	Construction of Fixed Jetty for...	—	—	1TB01031	
—	Supreme Rubber LLC	Supply of Marine Furniture	—	—	1TB01031	
—	Etmar Marinas Khaleej LLC	Constructing Boardwalks & Je...	—	—	1TB01031	
—	Al Rajhi Takaful (Insurance)	Al Rajhi Takaful-Insurance – C...	—	—	1TB01031	

Forecast, actual and difference per contract per month, with the cumulative chart. Actuals come from the paid dates in the IPC logs; you can overwrite a cell if needed.

Module 10 – Budget Transfers

CD Commercial Dashboard

MODULES

Project Setup

Cost Report

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

User guide (PDF)

Change history

PROGRAMME

ASSET

REPORTING PERIOD

CM Commercial Manager

Admin

1TB01031 · Marina Villag...

1TB01031.01 · The Marina

Monthly Report No 51 – ...

Open

MODULE 10

Budget Transfers

Budget moved between packages. Approved transfers reduce the From package and increase the To package in column F of the cost report.

PDF

Excel

TRANSFERS

30

30 approved

APPROVED AMOUNT MOVED

711,697,476.18

total leaving From packages = total ...

PENDING APPROVAL

0.00

not yet in the cost report

COST REPORT CHECK

Column F nets to zero

30 approved not applied

⚠

These approved transfers are not in the cost report yet: BT-01(From package has no cost report line); BT-02(From package has no cost report line); BT-03(From package has no cost report line); BT-04(From package has no cost report line); BT-05(From package has no cost report line); BT-06(From package has no cost report line); BT-07(From package has no cost report line); BT-09(From package has no cost report line); BT-10(From package has no cost report line); BT-11(From package has no cost report line); BT-12(From package has no cost report line); BT-13(To package has no cost report line); BT-14(From package has no cost report line); BT-15(From package has no cost report line); BT-16(From package has no cost report line); BT-17(From package has no cost report line); BT-18(From package has no cost report line); BT-19(From package has no cost report line); BT-21(From package has no cost report line); BT-23(From package has no cost report line); BT-24(From package has no cost report line); BT-25(From package has no cost report line); BT-26(From package has no cost report line); BT-27(From package has no cost report line); BT-28(From package has no cost report line); BT-29(From package has no cost report line); BT-30(From package has no cost report line); BT-31(From package has no cost report line); BT-31b(From package has no cost report line); BT-32(From package has no cost report line). Open the transfer and choose the From / To cost line, or add the missing line on the Cost Report Line setup tab.

Net movement by package (as applied to cost report column F)

Package	Out	In	Net
No approved transfers applied yet.			

A transfer lands on the package's Level 2 line automatically. If a package has more than one line (several contractors), pick the line in the form. The *In cost report* column shows whether each transfer is currently applied. Column F on the Cost Report is now live.

Q Search budget transfers...

Filters

Refresh

Export

Import

+ Add Budget transfer

Item	Description	Status	From package	To package
------	-------------	--------	--------------	------------

Transfers between packages. Approved transfers linked to cost lines feed column F.

Module 11 – Minutes of Meeting

CD Commercial Dashboard

MODULES

Project Setup

Cost Report

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

User guide (PDF)

Change history

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 51 – ...

Open

CM Commercial Manager

Admin

< Executive Summary

MODULE 11

Minutes of Meeting

One row per meeting. Open the minutes to record items and actions; anything still open is carried forward to the next meeting automatically.

PDFExcel

Q Search minutes of meeting...

Filters

Export

Import

+ Add Meeting

Meeting No	Title	Meeting date	Reporting period	Chair	Attendees
MCM-50	Monthly Commercial Meeting – August 2026	02-Sep-26	Monthly Report No 50 – Aug'26	Michael Hansen	M. Hansen, B. Lombard

1 of 1 minutes of meeting · double-click a row to edit

One meeting per month. Open items are carried forward automatically to the next meeting.

CD Commercial Dashboard

MODULES

Project Setup

Cost Report

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

User guide (PDF)

Change history

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 51 – ...

Open

CM Commercial Manager

Admin

< Executive Summary

MODULE 11

Minutes of Meeting

One row per meeting. Open the minutes to record items and actions; anything still open is carried forward to the next meeting automatically.

PDFExcel

Q Search minutes of meeting...

Filters

Export

Import

+ Add Meeting

Meeting date	Reporting period	Chair	Attendees	Actions
p-26	Monthly Report No 50 – Aug'26	Michael Hansen	M. Hansen, B. Lombard, N. Chintawar, S. Fairfield (p...	Open minutes

1 of 1 minutes of meeting · double-click a row to edit

Inside a meeting: attendees, discussion items and actions with owner, due date and status.

9. Locking a month and generating the report

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 51 - ... [Open](#)

CM Commercial Manager Admin

< Settings

REPORT CONTROL

Reporting Periods

One row per monthly report. Lock a period at month end to take a snapshot of every register.

Month-end: press *Lock* on a period to freeze it. The app stores a copy (snapshot) of every module register at that moment so later reports can show *This Period* vs *Previous Period*. Unlock only if you need to correct something.

Search reporting periods...

Filters Export Import + Add Reporting Period

Label	Status	Locked at	Locked by	Aconex ref	Actions
Report No 51 - Sep'26	Open	—	—	—	Lock Refresh Edit Delete
Report No 50 - Aug'26	Locked	10-Sep-26	Commercial Manager	AMAALA/THE MARINA/MONTHLY REPORT 50	Unlock Refresh Edit Delete

2 of 2 reporting periods · double-click a row to edit

Settings → Reporting Periods. **1** Lock or Unlock a period (Admin). **2** Add the next month.

Locking takes a snapshot of every register and of the cost report. From then on the month is read-only and the next month compares itself against it ("previous period" and "movement" columns).

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina PROJECT/REPORT: Monthly Report No 51 – ... Open

MODULES

- Project Setup 1
- Cost Report 2
 - Level 1 – Executive
 - Level 2 – Detailed
 - Line setup
- Change Management 3
- Claims & Disputes 4
- Early Warnings & Risks 5
- Provisional Sums 6
- Bonds & Insurance 7
- Invoices & Payments 8
 - Final Account Status
- Cash Flow 9
- Budget Transfers 10
- Executive Summary 11
 - Minutes of Meeting
- Monthly Report 12**

SYSTEM

- User guide (PDF)
- Change history

MODULE 12

Generate Monthly Report

Cover, index, minutes of meeting, executive summary and Schedules A to J as PDF or Excel, built from the locked snapshot of the chosen period.

Reporting period: Monthly Report No 51 – Sep'26 · Open Generate PDF Generate Excel

Open – report is a DRAFT from live data Lock the period under Settings → Reporting Periods (or on Project Setup) to freeze the figures before issuing.

Have the month in Excel already?
Upload your existing monthly report workbook and the app records it against a period. Import past months in order to build the history, then each new month shows its movement. Import monthly workbook

Contents

- Cover page with project particulars and the Prepared / Reviewed / Approved block
- Index with checklist status and distribution list
- Minutes of Meeting for the period (carried-forward and new items)
- Executive Summary: KPIs, open items, key issues, actions, cost chart
- Schedule A** Cost Report – Level 1 (Executive) ○
- Schedule B** Cost Report – Level 2 (Detailed) ○
- Schedule C** Change Management Tracker ○
- Schedule D** Early Warnings & Risks / Opportunities ○
- Schedule E** Claims & Disputes ○
- Schedule F** Provisional Sums ○
- Schedule G** Bonds & Insurance ○
- Schedule H** Invoice & Payment Tracking and Final Account Status ○
- Schedule I** Cash Flow ○
- Schedule J** Budget Transfers ○

Sign-off block (current period)

PREPARED BY	REVIEWED BY	APPROVED BY
no date	no date	no date

Fill these in on [Project Setup](#) → [Report control](#). Aconex reference and key issues come from the same place.

Monthly Report. **1** Choose the period. **2** Generate PDF. **3** Generate Excel.

The PDF contains the cover page with the sign-off block, the index, the minutes of meeting, the executive summary and Schedules A to J. The Excel has one sheet per schedule. If the period is still open the report is marked as a **draft from live data**; lock the period to issue the final version.

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 51 - ... Open

MODULE 12

Generate Monthly Report

Cover, index, minutes of meeting, executive summary and Schedules A to J as PDF or Excel, built from the locked snapshot of the chosen period.

Reporting period: Monthly Report No 51 – Sep'26 · Open

[Open – report is a DRAFT from live data](#) Lock the period under Settings → Reporting Periods (or on Project Setup) to freeze the figures before issuing.

[Generate PDF](#) [Generate Excel](#)

Have the month in Excel already?
Upload your existing monthly report workbook and the app records it against a period. Import past months in order to build the history, then each new month shows its movement.

[Import monthly workbook](#)

Contents

- Cover page with project particulars and the Prepared / Reviewed / Approved block
- Index with checklist status and distribution list
- Minutes of Meeting for the period (carried-forward and new items)
- Executive Summary: KPIs, open items, key issues, actions, cost chart
- Schedule A** Cost Report – Level 1 (Executive)
- Schedule B** Cost Report – Level 2 (Detailed)
- Schedule C** Change Management Tracker
- Schedule D** Early Warnings & Risks / Opportunities
- Schedule E** Claims & Disputes
- Schedule F** Provisional Sums
- Schedule G** Bonds & Insurance
- Schedule H** Invoice & Payment Tracking and Final Account Status
- Schedule I** Cash Flow
- Schedule J** Budget Transfers

Sign-off block (current period)

PREPARED BY: no date REVIEWED BY: no date APPROVED BY: no date

Fill these in on [Project Setup](#) → [Report control](#). Aconex reference and key issues come from the same place.

The contents of the report and the sign-off block for the current period.

All reports (library): change, re-upload or delete a report

< Monthly Report

MODULE 12

All reports (library)

Every monthly report the dashboard holds: where it came from, whether it is issued, and the tools to open, change, re-upload, lock, unlock or delete it.

Report	Cut-off	Status	Source	Issued snapshot	Last change
Monthly Report No 51 – Sep'26 Report No 51	30-Sep-26	Open	Manual entry	live data	10-Sep-26
Report No 51: Open Downloads Re-upload Change Lock Delete					
Monthly Report No 50 – Aug'26 Report No 50	31-Aug-26	Issued (locked)	Workbook import	530 records · 47 cost lines	10-Sep-26
Report No 50: Open Downloads Re-upload Change Unlock Delete					

Re-upload opens the monthly workbook import with this report pre-selected; the workbook's rows update the existing ones by their references. A locked report is unlocked first (Admin) and should be locked again after the import. **Delete** removes the report, its issued snapshot and its checklist only; the live registers are not touched.

Monthly Report → **All reports (library)** (also in the left menu). One row per report with its cut-off, status, where it came from (the workbook file, when and by whom, or "Manual entry"), the data it holds (Live for the latest report, Stored copy or Issued copy for the others) and the tools: **Open** (select it in the top bar), **Downloads**, **Re-upload**, **Change**, **Lock / Unlock** and the bin.

- **Re-upload** opens the monthly workbook import with that report pre-selected, so you can load a corrected or newer version of the same month. Rows are matched by their references: the report is refreshed, not duplicated, and stored as that report's own data. A locked report is unlocked first (Admin,

after a confirmation); tick "Lock the period after importing" to issue it again. For a month older than the latest report, the latest report's live figures are put back automatically when the import finishes.

- **Change** edits the report number, the cut-off date or the label. Leave the label blank to rebuild it from the number and date. The number decides the order of the reports and therefore which report the movement is measured against.
- **Delete** (Admin) removes the report, its issued snapshot and its checklist after you type the report number to confirm. The live registers – cost lines, changes, claims, payments – are never touched by a delete, so deleting a wrongly created period is safe.
- **Lock / Unlock** work as on the Project Setup page; locking an older report while a newer one exists asks for a confirmation.

10. Settings, users and backups

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 51 - ...

Settings

Dropdown lists, project structure, reporting periods and users. Every list supports add / edit / delete, search, Excel import & export and change history.

Database backup [Download database](#)

Cloud backup is off (no BACKUP_GITHUB_* or BACKUP_S3_* settings). The database is the file data/commercial.db; use *Download database* to keep a copy. On a hosting service, set the backup settings so the database survives restarts.

Changes are uploaded within about 20 seconds, plus one dated copy per day. To restore, place the downloaded file at data/commercial.db (or upload it to the backup storage as backups/commercial.db) and restart the app.

PROJECT STRUCTURE

Programmes 1 → Top-level programmes (e.g. 1TB01031).

Assets 3 → Assets within a programme (e.g. 1TB01031.01).

Clients 1 → The employer / client organisations.

Locations 1 → Where the programmes / assets are located.

REPORT CONTROL

Reporting Periods 2 → One row per monthly report. Lock a period at month end to take a snapshot of every register.

COMMERCIAL LISTS

Packages 50 → Work packages / contracts that the cost report is broken down by.

Contractors & Consultants 13 → Every party you hold a contract or purchase order with.

DROPDOWN LISTS

Settings: every dropdown list, the project structure, reporting periods, users, the database backup and the Start over card (Admin only).

- **Dropdown lists** (packages, contractors, statuses, bond types, cost categories...): add or rename values here. The forms pick them up immediately.
- **Programmes and Assets**: the projects and their sub-assets shown in the top bar. A programme row is a stand-alone project (1TB01031 The Marina, 1TB01006 Village Boutique Hotel); to add another project, add a programme and at least one asset under it – it starts with an empty library and empty registers.
- **Reporting Periods**: add the next month, lock and unlock (chapter 9).
- **Users**: add colleagues and choose their role (chapter 11).
- **Database backup**: the data is backed up automatically to a private GitHub repository within 20 seconds of every change. "Download database" gives you a copy to keep.
- **Start over**: wipes all project data (not users or settings). Only for a fresh start after a test import. It asks you to type DELETE.

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 51 - ...

Settings

ACCESS

Users

People who can log in. Admin = full control, Editor = can add and change records, Viewer = read-only.

Search users... Filters Export Import **+ Add User**

Full name ^	Email (login) ^	Role ^	Active ^	Actions
Commercial Manager	admin@commercial.local	admin	Yes	

1 of 1 users · double-click a row to edit

Settings → Users. **1** Add a user: name, email, role and a first password. They can change the password later.

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 51 - ...

Change history

The latest 300 changes across every register: who changed what, and when.

- 10-Sep-26 13:28 · Commercial Manager login auth
Commercial Manager logged in
- 10-Sep-26 13:24 · Commercial Manager login auth
Commercial Manager logged in
- 10-Sep-26 13:18 · Commercial Manager context context
Changed the current programme / asset / period in the top bar
period: Monthly Report No 50 – Aug'26 → Monthly Report No 51 – Sep'26
- 10-Sep-26 13:18 · Commercial Manager context context
Changed the current programme / asset / period in the top bar
period: Monthly Report No 51 – Sep'26 → Monthly Report No 50 – Aug'26
- 10-Sep-26 13:18 · Commercial Manager login auth
Commercial Manager logged in
- 10-Sep-26 13:17 · Commercial Manager update claims
Changed Claim "CL-005": Status, EOT days, Cost (SAR), Letter / VO ref, Date
status: Pending → Approved
determination eot days: (blank) → 60
determination cost: (blank) → 0
determination ref: (blank) → AMA01031-GENCORR-001204
determination date: (blank) → 2026-09-15
- 10-Sep-26 13:17 · Commercial Manager update bonds
Changed Bond / Insurance "G-13": Expiry date, Comments
expiry date: 2026-02-28 → 2027-06-30
comments: Approval status: Under process MME01031-TRANSMIT-000259 1TB01031-03IC10-MME-BND-CM-0001[C4] → Extended to 30-Jun-27
- 10-Sep-26 13:17 · Commercial Manager create payment applications

Change history (System → Change history) lists every change made by anyone, newest first.

11. Who can do what

Role	Can see	Can add / edit / delete	Can lock periods, manage users, back up, start over
Viewer	Everything	No	No
Reports only (download)	Only the Reports & downloads page	No. Can pick a month and download every report as PDF or Excel, and open the user guide. Every other page and button is hidden and blocked.	No
Data entry (add only)	Everything	Can add new rows in every module (a new change, claim, IPC, bond, meeting action, cost line...) and run every PDF, Excel and "Email the Report". Cannot edit or delete existing rows, enter cash flow, change report control or key issues, or import a workbook.	No
Editor	Everything	Yes, in every module	No
Admin	Everything	Yes, in every module	Yes

Give Viewer to people who only read the report, Data entry to colleagues who log new items for you, Editor to the commercial team, and Admin to one or two people who issue the report.

Two accounts are created for you the first time the dashboard starts: **User-1** (login **user1@commercial.local**) and **User-2** (login **user2@commercial.local**). They are **Reports only** users: when they log in they land on the Reports & downloads page and can do nothing else. Ask the Admin for the starting password and change it under Settings → Users as soon as possible. The Admin can give them another role there at any time.

The cost report as a presentation (PowerPoint and PDF slides)

Executive Summary, top right. **1 PowerPoint** downloads the monthly cost report as a short (10–13 slides), colourful, animated and fully editable presentation. **2 PDF slides** is the same presentation as a PDF. **3 Excel dashboard** downloads the whole dashboard as one Excel workbook (see below). The Reports & downloads page has the same buttons, for any month.

The presentation is built from the report selected in the top bar and carries its status (Issued or Draft) in the footer of every slide. Each slide has its own colour band, coloured headline tiles and either charts or tables that fill the page. Only sections with something to show are included: a month with no claims, no cash-flow figures or no earlier report to compare with simply has no claims, cash-flow or movement slide, and tiles that would show zero are left out. The slides that can appear are: title; executive summary with headline tiles, a written summary and the anticipated-final-account build-up; cost report Level 1 in the Excel "Level 01" layout with a budget-against-forecast chart; the largest packages and the lines driving the variance; movement since the previous report; change management with the status of every stage; early warnings and risks; claims and disputes; invoices and payments with the cumulative claimed / certified / paid curve; cash flow (monthly and cumulative); bonds and insurance; provisional sums and budget transfers; and key issues and open actions.

The dashboard as an Excel workbook

The **Excel dashboard** button (and "Commercial Dashboard (Excel)" on the Reports & downloads page) gives you the whole dashboard for the selected month in one workbook, laid out like the website: a **Dashboard** sheet with the six headline tiles, the six open-item tiles, links to every module, six native Excel charts, the headlines, key issues and open actions; then one sheet per module – Level 1, Level 2, Movement, Change Management, Claims & Disputes, Early Warnings & Risks, Provisional Sums, Bonds & Insurance, Invoices & Payments, Final Account Status, Cash Flow, Budget Transfers and Minutes & Actions. Each module sheet starts with the summary figures and a chart, exactly as the dashboard page does, followed by the full register.

The workbook is live: Level 1 is built by formula from Level 2, the Dashboard tiles read Level 1, and the module summaries are COUNTIF / SUMIF formulas over the register on the same sheet. Change a figure in a register and the summary, the tile and the chart follow. The charts are ordinary Excel charts (right-click → Select Data to change them). Figures that the dashboard works out from several registers together – open change items, expired bonds, the package ranking and the payment curve – are written as values for that month.

The Excel edition – the whole dashboard inside Excel

On the Reports & downloads page, **Commercial Dashboard – Excel edition (.xlsm)** downloads the dashboard as a stand-alone Excel application loaded with today's data. It is meant for working entirely in Excel, without the website: you sign in with the same users and roles, the modules are Excel tables, the cost report is formulas, and the imports, period lock and PDF export are buttons. Only an admin or editor can download it.

First time you open it

1. Save the file somewhere on your PC, right-click it → **Properties** → tick **Unblock** → OK. (Windows blocks macros in files downloaded from the internet until you do this.)
2. Open the file. Click **Enable Content** in the yellow bar if Excel shows one. On a Mac there is no Unblock step: Excel asks once whether to enable macros – choose **Enable Macros**.
3. The **Login** sheet appears. Type your email and password and click **Sign in**. Starting passwords: the administrator uses **Admin@123**, everyone else **Welcome@123**. You are asked to choose your own password the first time.

How it looks

The Login sheet is a full-colour welcome page: a white sign-in card on a navy-to-teal background with the programme name, what the workbook can do and the first-sign-in passwords. Inside, every sheet has a gradient title band, the Home sheet has raised colour tiles and glossy buttons (each with a small icon), the module links are colour-coded cards, and the charts sit in rounded panels with a soft shadow. The buttons are ordinary Excel shapes: they are part of the file, so they are there even before you sign in, and the workbook wires each one to its action on the first sign in.

The website's passwords cannot be copied into Excel (they are stored as one-way hashes), which is why everyone starts with the standard password. Passwords in the Excel edition are hashed too, but Excel is not a secure system: anyone who can open the file with macros switched off can see the sheets. Keep the file where only the commercial team can reach it.

Moving around

The workbook behaves like the website: the sheet tabs are hidden and every page carries the same navigation bar at the top – **Home** (the executive summary), **Level 1**, **Level 2**, **Movement**, **Registers**, **Periods**, **Reports**, **Setup**, **Users** and **Sign out**. The current page is highlighted in gold. **Registers** is a menu of tiles, one per module, each showing how many open items it holds; click a tile to open that register.

The Commercial Dashboard folder

The workbook creates a folder called **Commercial Dashboard** on your Desktop the first time it needs it, with three sub-folders: **Reports** (every PDF, Excel copy, PowerPoint and Claim EAR it produces – saved there automatically, no file window), **Imported reports** (a copy of every file you import, named with its report number) and **Backups** (the copies kept before each step). **Open reports folder** on Home and **Reports folder** on the Library page open it.

Autosave and undo

The workbook saves itself after every step – an import, a new month, a lock or unlock, a deleted report, a user change, a switch of the report shown – and a few seconds after every cell you type. Before each step it also keeps a copy of itself in the Backups sub-folder of the Commercial Dashboard folder on your Desktop (the last 15 are kept). Two buttons sit in the navigation bar on every page: **Undo entry** takes back the last cell you typed (Excel's own undo), and **Undo step** brings back the copy kept before the last step, after asking you to confirm – the workbook then reopens as it was and you sign in again.

Every report kept on its own

As on the website, each report keeps its own data. The pages show the report chosen in the gold box on Home (or on the Periods page); an issued report is read only, the current report is live. Switching reports saves the current report's rows and loads the other report's rows into every page – cost report, registers, tiles and charts alike. On the **Periods** page, **Delete report** removes a report and everything stored for it (an editor or admin only).

Periods – choosing the report shown

The quickest way is the gold **Report shown** box at the top right of Home: pick a report from its dropdown and the summary tiles, charts, Level 1 and Level 2 switch to that issued report at once. The **Periods** page lists every report. Click the row of an issued (locked) report and press **Show this report**: Home, Level 1 and Level 2 then show that report's stored copy, read only, and the Previous column compares it with the report before it – the same as choosing a period on the website. A banner on each of those pages says which report is shown. **Back to current report** returns to the live data. The registers always show the current data. **New month**, **Lock period** and **Unlock period** are on this page as well as on Home.

Imports

The **Imports** page (also the Imports button on Home) holds the five imports with a note on what each one loads: the monthly report, the claims tracker, bonds & insurance, payment tracking and final accounts. Every monthly import asks for the report number and the cut-off date first (pre-filled from the file). A later number becomes the new current report; the same number replaces the current data; an earlier number is stored as an issued report on its own, ready to be shown or reported on, while the current report stays live. **New month** asks for the report number and cut-off date in the same way.

Reports – the library

The **Library** page (also the Report library button on Home) lists every report the workbook holds – number, label, cut-off, status, source file and how many files have been produced for it. Click a report, then a button: produce the cost report PDF, the Excel copy or the PowerPoint from it; **Replace from file** re-imports it from a monthly report workbook; **Edit No / cut-off** changes its report number and cut-off date (everything stored follows the new number); **Delete report** removes it and everything stored for it. It also keeps a list of everything produced: **Cost report (PDF)**, **Issued copy (Excel)**, **PowerPoint presentation** and **Claim EAR (Word)**. Each file is saved where you choose and listed in the library with its report number, date and author. Select a row and press **Open selected file** to open it again, or **Open the reports folder** to see them all. To produce a report for an earlier period, choose that period on the Periods page first.

What is inside

- **Home** – the headline tiles, open-item tiles, six live charts and the buttons: New month, Lock / Unlock period, Recalculate, Export PDF report, Sign out, the five imports, Change my password, **PowerPoint presentation** and **Claim EAR (Word)**.
- **Setup** – programme, asset, client, location, the current report number and the rules (bond expiry days).
- **Level 1, Level 2, Movement** – Level 2 holds the cost lines; columns F to S are formulas over the other tables exactly as on the website (transfers → F, changes → H/J/K, early warnings → L, claims → M, contracts → P, the stored copy of the previous report → R and S). Level 1 sums Level 2 by category in the Excel "Level 01" layout, with the previous report and the movement.
- **Changes, Claims, Early Warnings, Risks, Provisional Sums, Bonds, Contracts, IPCs, Final Accounts, Cash Flow, Transfers, Actions** – one table each, with dropdowns for the status columns and calculated columns (feed column and amount, cost report amount, bond status, revised contract value, payment due dates ...). Edit the rows directly; everything recalculates.
- **Periods and Snapshots** – the reporting periods and the stored copies of each issued cost report. **Lock period** stores the current Level 2 as the issued copy; **New month** stores it and starts the next report number, so the movement columns compare with it.
- **Users** (admin only) – add users, set roles (admin, editor, contributor, viewer, reporter) and reset passwords with the buttons. Viewers see read-only sheets; reporters see Home, Level 1, Level 2 and Movement only.

Imports

Import monthly report reads your monthly cost report workbook (The Marina CM Report layout: Schedule B, C, D, F, H and the per-contract Schedule H sheets, Early Warning, Schedule J, Data Input). It replaces the cost lines, changes, early warnings, risks, provisional sums, contracts, IPC log and transfers of the current report; claims, bonds and final accounts are never touched by it. A workbook with a higher report number starts the next month (the current report is stored first); the same report number is a re-import; an older month cannot be imported in Excel – use the website for that. **Import claims tracker** reads the AMAALA Claims Tracker and keeps only the claims of your programme / asset. **Import bonds & insurance, Import payment tracking** and **Import final accounts** recognise the columns of any workbook by their headings, as the website does, and update rows by their reference.

PowerPoint presentation and Claim EAR in Excel

PowerPoint presentation builds the same short deck as the website – title, executive summary, Level 1, movement, changes, early warnings, claims, payments and cash flow, bonds, provisional sums, key issues – directly in PowerPoint on your PC, with the charts copied from the Home sheet as editable charts, the tables as editable PowerPoint tables, a fade transition and staggered fade-in animations. It asks where to save the .pptx and saves the same slides as a PDF next to it. PowerPoint must be installed.

Claim EAR (Word) drafts the Employer's Assessment Report exactly as the website does: it asks for the claim title, the folder with the contractor's submission, the EAR template (Word, optional), a folder of contract documents (optional) and, for a revision, the previous EAR and previous submission. It reads the files (PDFs and photographs are sent as they are; Word, Excel and text files as text), sends them with the same drafting instructions to the Claude drafting engine, and writes the report as a Word document from

your template's styles into the submission folder. A revision is compared with the previous report in Word, so every change appears as a tracked change by "Commercial Manager". Word must be installed, the PC needs internet access, and an administrator must first paste the Anthropic API key into the "API key" cell on the Setup sheet (the same key the website uses). Drafting takes 3–10 minutes; Excel stays busy meanwhile.

Excel for Mac

The Excel edition works in Excel for Mac (Microsoft 365) as well as Excel for Windows: sign in, the tables, the cost report, imports, period lock, PDF export, PowerPoint and the Claim EAR. Two small differences: file-open windows on the Mac do not filter by file type, so pick the right file yourself; and the Claim EAR sends its request through the Mac's built-in network tool, so the first time you run it macOS may ask you to allow Excel to run a script – allow it. If Excel for Mac ever shows a Visual Basic message, note the exact wording (or take a screenshot) and send it to the administrator; it tells them which step to fix.

The website and the Excel edition are separate copies. Data entered in Excel does not flow back to the website. Download a fresh Excel edition whenever you want Excel to start from the website's latest data.

When you present the PowerPoint, every slide fades in and its tiles, charts and tables appear one after the other automatically – no clicks are needed. The animations are ordinary PowerPoint animations: open the Animations tab → Animation Pane to change or remove them.

Everything in the PowerPoint is editable. The charts are native PowerPoint charts (right-click → Edit Data), the tables are real tables, and the text is text. Change a number, a colour or a wording, add your own slide, and present. The PDF version is for e-mailing or printing; the layout and colours are the same as the PowerPoint.

The Reports & downloads page

The screenshot shows the 'Reports & downloads' page in the The Marina Commercial Dashboard. The interface includes a top navigation bar with filters for Programme (1TB01031 - Marina Villag...), Asset (1TB01031.01 - The Marina), and Reporting Period (Monthly Report No 51 - ...). A user profile 'User-1' is logged in. The left sidebar contains a 'REPORTS' section with 'Reports & downloads' and 'User guide (PDF)'. The main content area is titled '1TB01031 - 1TB01031.01 Reports & downloads' and instructs users to 'Choose the month, then download any report as a print-ready PDF or a formatted Excel file.' Below this, the 'REPORTING PERIOD' section shows 'Monthly Report No 51 - Sep'26' as the selected period, with a 'Draft - live data' status and a 'cut-off 30-Sep-26' date. A 'Full monthly report - Monthly Report No 51 - Sep'26' is available for download as PDF or Excel. The 'SUMMARIES' section lists five reports: 'Executive Summary', 'Movement since the previous report', 'Claims Status Report', 'Final Account Status Report', and 'Minutes of Meeting', each with PDF and Excel download options. The 'SCHEDULES' section lists four reports: 'Schedule A - Cost Report - Level 1 (Executive)', 'Schedule B - Cost Report - Level 2 (Detailed)', 'Schedule C - Change Management Tracker', and 'Schedule D - Early Warnings & Risks / Opportunities', also with PDF and Excel download options.

1TB01031 - 1TB01031.01 Reports & downloads

Choose the month, then download any report as a print-ready PDF or a formatted Excel file.

REPORTING PERIOD

Monthly Report No 51 - Sep'26 Monthly Report No 50 - Aug'26

Draft - live data cut-off 30-Sep-26

Full monthly report - Monthly Report No 51 - Sep'26 PDF Excel

Cover, index, minutes, executive summary, movement and Schedules A to J in one file.

SUMMARIES

Executive Summary Headline figures, open items, payment tracker, key issues and actions	PDF Excel
Movement since the previous report Cost report movement, key period movements, status counts, register changes	PDF Excel
Claims Status Report Executive claims report with narrative	PDF Excel
Final Account Status Report Executive final account report with narrative	PDF Excel
Minutes of Meeting Meetings and actions of the period	PDF Excel

SCHEDULES

Schedule A - Cost Report - Level 1 (Executive) Asset x category summary	PDF Excel
Schedule B - Cost Report - Level 2 (Detailed) Line by line cost report	PDF Excel
Schedule C - Change Management Tracker Register as printed in the monthly report	PDF Excel
Schedule D - Early Warnings & Risks / Opportunities	PDF Excel

Everyone has it under **System** → **Reports & downloads**; for a Reports-only user it is the whole dashboard. Pick the month at the top, then download the full monthly report or any single report as PDF or Excel.

12. Security: how the dashboard and its documents are protected

Everything in the dashboard sits behind a login, and the protection works in layers. Nothing is public: even the user guide PDF needs a login.

Layer	What it does
Encrypted connection	The site is only served over HTTPS. The browser is told to always use HTTPS (HSTS), never to show the dashboard inside another website (no framing), and search engines are told not to index it.
Login and sessions	Passwords are stored as salted bcrypt hashes; nobody, not even the Admin, can read them. A login lasts 7 days on that browser, in a cookie the page scripts cannot read and that is never sent to other websites. Sessions are signed with a secret key that exists only on the server.
Password rules	At least 10 characters with letters and numbers, not your name, not a common word. Accounts created with a starting password must choose their own password at the first login before they can see anything. Anyone can change their own password from the menu under their name.
Brute-force protection	After 5 wrong passwords an email address or a network address is locked for 15 minutes; 30 attempts from one address in 15 minutes are refused. Every failed and successful login is written to the Change history with the network address.
Roles	Every page and every server call checks the role from the database, not just the login token, so a change under Settings → Users applies immediately. Reports-only users cannot reach anything but the Reports page.
Cross-site protection	Requests that change data are accepted only when they come from the dashboard's own address, so a malicious website you happen to visit cannot act on the dashboard with your login. Browser security headers (content security policy, no MIME sniffing, no referrer leakage) are sent with every page.
Uploads	Workbook imports accept only genuine .xlsx files up to 40 MB; they are parsed in a separate process with a memory cap and deleted after 30 minutes. Claim EAR documents (any file type, up to 60 MB each) are kept on the server's private disk under the case, are never served to anyone but logged-in Editors and Admins, and are deleted with the case.
Data and backups	The database lives on the server's private disk. Backups go to your own private GitHub repository with a token that only the server holds. The database download is Admin-only.

What you and your colleagues must do

- Use a strong, unique password and never share it; never write it in an email or chat.
- Give each person their own account; use **Viewer** or **Reports only** for anyone who does not need to enter data, and set accounts to **Inactive** as soon as someone leaves.
- Log out on shared or public computers (menu under your name → Log out).
- Keep the backup GitHub repository private and do not share the backup token.

- The PDF and Excel files you download are your copies: store them in your company's document system, not on personal devices or public drives.
- If you suspect a leaked password, change it at once and ask the Admin to review the Change history for unfamiliar logins.

13. Automation: Claim EAR (Employer's Assessment Report)

When a contractor submits an extension of time or cost claim, the Employer answers with an **Employer's Assessment Report (EAR)**. Writing one by hand means reading the whole claim folder, checking the contract, and drafting twenty or more pages in the house template. The **Automation** → **Claim EAR** page does the reading and the first draft for you: you upload the documents, press one button, and download a print-ready Word file laid out on your own template. For a **revised** submission it writes the new report on top of the previous EAR, with every difference shown as a tracked change by **Commercial Manager**, so the reviewer sees exactly what moved.

Who can use it. Editors and Admins. Viewers, Data entry and Reports-only accounts do not see the Automation menu. The drafting engine needs a key set by the administrator in the hosting settings (`ANTHROPIC_API_KEY` on Render); until it is set, the page shows an orange banner and Create EAR produces a skeleton laid out from your template instead of the full report.

Step 1: create a case

Claim EAR – Employer's Assessment Report

Upload the contractor's claim folder, your EAR template and the contract documents; the dashboard writes the Employer's Assessment Report as a print-ready Word file. For a revised submission it also takes the previous EAR and previous submission, and writes the new report with tracked changes.

Drafting engine not configured. Add `ANTHROPIC_API_KEY` in the hosting settings (Render → Environment) to have the full report written; until then Create EAR produces a skeleton laid out from your template.

Start a new assessment
One case per contractor claim. Give it a name, then upload the claim folder, your EAR template and the contract folder on the next screen.

1 Case title: e.g. EOT Claim No 3 – Quay wall drawings

Contractor: [input field]

Claim ref: [input field]

2 Revised submission

3 Create case

Contractor	Claim ref	Submission	Documents	Status	Report	Last change
Marina Marine Works Co	CL-003	Revision 1	4 files · 24 KB	Generated	Word	2026-09-10 · Commercial Manager
Marina Marine Works Co	CL-003	Original	6 files · 24 KB	Generated	Word	2026-09-10 · Commercial Manager

4 Open →

Automation → Claim EAR. 1 Name the case (one per contractor claim). 2 Tick **Revised submission** when the contractor has re-submitted and you already issued an EAR. 3 Create case. 4 Open an existing case. The list shows how many documents each case holds, its status and a link to the last Word report.

Step 2: upload the documents

TM The Marina
Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031C01 · The Marina REPORTING PERIOD: Monthly Report No 51 – ... **CM Commercial Manager** Admin

< Claim EAR cases

AUTOMATION · CLAIM EAR

EOT Claim No 3 – Quay wall drawings

Marina Marine Works Co · Contract 1TB01031C02 · Claim CL-003

Drafting engine not configured. Documents can be uploaded and a skeleton EAR laid out from your template, but the full assessment is written only when the server has an ANTHROPIC_API_KEY (Render → Environment). Ask the administrator to add it, then press Create EAR again.

Case details Original submission Save details

Case title: EOT Claim No 3 – Quay wall dra Contractor: Marina Marine Works Co Contract No: 1TB01031C02 Claim reference: CL-003

Contractor's submission ref: MMW-RSG-L-0412 Submission date: 08/20/2026 ☐ This is a revised submission

1 Contractor's claim & supporting documents 4 Upload folder Add files

The whole claim folder: narrative, notices, programmes (XER), delay analysis, cost build-ups, correspondence, photos – any file type.

File Type	File Name	Size	Status
PDF	01 Narrative/claim.pdf	2 KB	✓
Excel	02 Analysis/events.xlsx	6 KB	✓
Text	03 Programme/programme.xer	1 KB	✓
Image	04 Photos/site-photo.png	6 KB	⚠

Files marked with a warning could not be read fully (scanned PDF, image or a format the engine cannot open). Hover to see why.

2 EAR template (Word or PDF) 1 Choose file

Your Employer's Assessment Report template. Its headings, order and wording drive the structure of the report.

File Type	File Name	Size	Status
Word	template.docx	8 KB	✓

3 Contract documents 1 Upload folder Add files

The whole contract folder: conditions of contract, particular conditions, specifications, programme requirements – any file type.

File Type	File Name	Size	Status
PDF	Conditions/particular-conditions.pdf	2 KB	✓

Create EAR (Word)


6 documents · 24 KB. The engine reads the whole submission and the contract, follows your template, and writes a print-ready report.

Download EAR (Word) Create again

✓ **EAR - EOT Claim No 3 Quay wall drawings.docx** created 2026-09-10 18:20. Skeleton only – the drafting engine is not configured (add ANTHROPIC_API_KEY on the server). 6 documents received. Not readable: 1 file.

All amounts in SAR. Dates DD-MMM-YY

A case. **1** Case details: contractor, contract number, claim and submission references (they go on the report's cover block) – Save. **2** **Upload folder** sends the contractor's whole claim folder, sub-folders included. **3** Choose your EAR template (Word or PDF). **4** Upload the contract folder. **5** Create EAR. **6** Download the Word file.



Once a group holds documents, a red **Remove all** button appears beside Upload folder and Add files. One click (and a confirmation) empties that group so you can upload a corrected folder.

- 1 **Contractor's claim & supporting documents.** Click **Upload folder** and pick the folder you received from the contractor: the narrative, notices and letters, the delay analysis, the programmes (XER), cost build-ups, photographs. Every file type is accepted (PDF, Word, Excel, images, XER, e-mails, anything). Sub-folder names are kept, and the report cites documents by them. Use **Add files** to add single files later.
- 2 **EAR template.** One Word file (a PDF also works, see below): your Employer's Assessment Report template. The report is written **into a copy of that file**, so its fonts, colours, heading styles, cover page, revision-history block, header and footer, page size and margins are exactly those of the template; nothing about its look is changed. Its headings, in their order, are the headings of the report (the engine may add sub-headings under them, one per delay event for example). Only the numbering (1.0, 1.1, 1.1.1, Table 1, Table 2 ...) is regenerated to fit the new content, in the template's own style. A previously issued EAR is an ideal template. With a PDF template the headings are still followed, but the file is laid out in the dashboard's standard Word style because a PDF's fonts and styles cannot be copied.
- 3 **Contract documents.** Upload the contract folder: conditions of contract, particular conditions, specifications, programme requirements, key letters. The report quotes the clause numbers from here.
- 4 **Remove all** next to the upload buttons empties a group in one click (after a confirmation), for example to replace a whole claim folder with a newer one; the bin icon on a row removes a single document.
- 5 Each document gets a badge for its type and a green tick when its text could be read. An orange triangle means the engine cannot see inside it: a scanned PDF without text (run OCR in Acrobat and upload it again), an image (kept as evidence and named in the report), or a format such as .msg, .zip or .dwg. Hover the triangle for the reason.

Large folders. Files go up one at a time in small pieces, so a 300 MB claim folder simply takes a few minutes; keep the page open until the counter finishes. Each file may be up to 60 MB and a case up to 800 MB.

Step 3: create the report

Press **Create EAR**. The engine reads the whole submission, the contract and the template, then writes the report: entitlement and notice compliance, the delay analysis (critical path, concurrency, float, mitigation), quantum (rates, prolongation, duplication with variations), with claimed-against-assessed tables, the Employer's position for each delay event, a conclusion and recommendation, the documents relied upon and a list of information gaps to request from the contractor. Every finding cites the clause and the file it comes from. Writing takes a few minutes for a large claim; the green box then names the file and how many documents were read. Click **Download EAR (Word)**.

The Word file is fully editable and looks like your template: same fonts and heading colours, the cover page filled with the contract number, contractor, claim reference and date, the revision-history block, the table of contents, the numbered paragraphs, the tables in the template's table style with numbered captions, and an "Assessment at a glance" table at the start of the first section. Read it, adjust what you want, and issue it. Press **Create again** after adding documents to rewrite it.

"This document contains fields that may refer to other files. Update?" Word asks this the first time you open the report. Answer **Yes**: it fills in the page numbers of the table of contents.

Revised submissions: tracked changes

The screenshot displays the 'Claim EAR cases' interface in The Marina Commercial Dashboard. The top navigation bar shows the programme '1TB01031 · Marina Villag...', asset '1TB01031.01 · The Marina', and reporting period 'Monthly Report No 51'. The user is logged in as 'CM Commercial Manager Admin'.

The left sidebar lists various modules, with 'Claim EAR' highlighted under the 'AUTOMATION' section.

The main content area shows the details for 'EOT Claim No 3 – Quay wall drawings (Rev 1)' under 'Marina Marine Works Co · Claim CL-003'. A warning message states: 'Drafting engine not configured. Documents can be uploaded and a skeleton EAR laid out from your template, but the full assessment is written only when the server has an ANTHROPIC_API_KEY (Render → Environment). Ask the administrator to add it, then press Create EAR again.'

The 'Case details' section includes the following information:

- Case title: EOT Claim No 3 – Quay wall dra
- Contractor: Marina Marine Works Co
- Contract No: [Redacted]
- Claim reference: CL-003
- Contractor's submission ref: [Redacted]
- Submission date: mm/dd/yyyy
- Revision number: 1

A red box highlights the checkbox 'This is a revised submission', which is checked. A red circle with the number '1' is placed next to this checkbox.

Below the case details, there are sections for uploading documents:

- 1 Contractor's claim & supporting documents**: Includes a 'Upload folder' button and a list of files, including '01 Narrative/claim-rev1.pdf' (2 KB).
- 2 EAR template (Word or PDF)**: Includes a 'Choose file' button and a list of files, including 'template.docx' (8 KB).
- 3 Contract documents**: Includes a 'Upload folder' button and a message: 'No documents yet – upload the whole folder; sub-folders are kept.'
- 4 Previous EAR issued by the Employer**: Includes a 'Choose file' button and a list of files, including 'EAR-original.docx' (12 KB).
- 5 Contractor's previous submission**: Includes a 'Upload folder' button and a list of files, including 'claim.pdf' (2 KB).

At the bottom, the 'Create revised EAR (Word, tracked changes)' section includes a 'Download EAR (Word)' button and a 'Create again' button. A green notification bar at the bottom states: 'EAR - EOT Claim No 3 Quay wall drawings Rev 1 - Rev 1.docx created 2026-09-10 18:20. Skeleton only - the drafting engine is not configured (add ANTHROPIC_API_KEY on the server). 4 documents received.'

A revised case. **1** Tick **This is a revised submission** and enter the revision number; two more groups appear. **2** Upload the previous EAR you issued (Word or PDF). **3** Upload the contractor's previous submission. **4** Create revised EAR.

When the contractor re-submits, create a new case (or untick and re-tick the box on the old one), tick **revised submission**, upload the new claim folder as usual, and add the **previous EAR** and the **previous submission**. The engine keeps the previous report's structure and wording wherever it is still right, changes only what the new evidence justifies, and adds a section "Changes in the revised submission". The Word file is written on top of the previous EAR with **Track Changes switched on**: every insertion and deletion is a tracked change by **Commercial Manager**, dated the day it was written. Open it in Word, use

Review → **Next** to walk through the differences, and Accept or Reject each one as you would with a colleague's mark-up.

The previous EAR can be the Word file the dashboard produced last time or any Word/PDF you wrote yourself; a Word file gives the cleanest comparison because its paragraphs and tables line up exactly.

Good practice

- Name the case after the claim and the letter reference; fill the contract number and submission date so the cover block is right first time.
- The report is a draft prepared for you, not a determination. Check every figure against the submission before it is issued; the "Information gaps" list at the end is a ready-made request letter to the contractor.
- Delete a case (the bin icon on the list, Admin only) when the claim is closed; that removes its documents from the server.

14. Libraries: EOT Library and Contract Library

Document	Type	Date	EOT (days)	Read	
▾ Arab Company for Laboratories and Soil Branch (ACES) 006D01 Arab Company for Laboratories and Soil Branch (ACES) - ...				3 documents · latest 16-May-26	🗑️ Remove all
^ Contemporain Studio, S.L. 006D12 Design Consultancy Services (3 lines)				3 documents · latest 16-May-26	🗑️ Remove all
▾ Contractor claim submission – adverse weather EAR/2026/SHOT-3.pdf · 242 KB	Claim submission	16-May-26	0 assessed 60 claimed	High match Read	🔗 Open ✎ Change 🔄 🗑️
▾ Employer Assessment Report – Design change, MEP risers EAR/2026/SHOT-2.pdf · 242 KB	EAR – Combined (Time & Cost)	15-Apr-26	14 assessed 28 claimed	High match Read	🔗 Open ✎ Change 🔄 🗑️
▾ Employer Assessment Report – Access to Zone 3 EAR/2026/SHOT-1.pdf · 242 KB	EAR – Extension of Time	14-Mar-26	21 assessed 45 claimed	High match Read	🔗 Open ✎ Change 🔄 🗑️
▾ Foster + Partners Limited 006D06 Executive Architect Services (3 lines)				3 documents · latest 16-May-26	🗑️ Remove all
▾ National Center for Environmental Compliance 006D08 National Center for Environmental Compliance - 220531...				3 documents · latest 16-May-26	🗑️ Remove all
▾ Shapoorji Pallonji Mideast LLC 006C15 Shapoorji Pallonji Mideast LLC - 2230262				1 document	🗑️ Remove all

The EOT Library: the documents sit folded away under the contract they belong to, so the page opens as a short list of contracts rather than one long list of files.

Two document libraries sit in the left menu under **Libraries**, one per project (switch the project in the top bar to see the other project's documents):

- **EOT Library (EARs)** – the Employer's Assessment Reports for extension of time and prolongation claims, with the claim submissions, notices and determination letters that go with them.
- **Contract Library** – the contract documents of every contract: agreement, letter of award, conditions, specifications, pricing schedules, amendments, variation orders, bonds.

Adding documents

- 1 Open the library and click **Add files** (pick one or more PDF or Word files) or **Add a folder** (the whole folder, sub-folders included – each document keeps its folder as its location).
- 2 **To stop part-way, click Stop** in the blue bar that shows the progress. Every document is read as it arrives and reading uses the AI allowance, so a folder picked by mistake does not have to run to the end. The documents already added stay; nothing after them is uploaded or read.
- 3 Each document is uploaded, its text is read, and the dashboard works out **who it is for**: it looks for the ACC contract codes (006C15, 031C10 ...), PO numbers and contractor names in the document and matches them with the Contracts, Cost report lines and Contractors of the project. The list shows the match as **High**, **Medium** or **Low**, or **Not filed** when nothing was found.
- 4 With the reading engine switched on (the same ANTHROPIC_API_KEY as the Claim EAR automation), each document is also **read**: its type (EAR – Extension of Time, Contract Agreement, Letter of Award ...), title, reference, date, claim reference, the days claimed and assessed, the amounts claimed and assessed, a professional summary and the key points are recorded. Without the engine the document is filed from its references only and marked **Partly read**.
- 5 Click a document's name to open its summary and key points; **Open** shows the original file; **Change** corrects the contractor, contract code, type, date or figures when the automatic filing is wrong; the

circular arrow reads the document again; the bin removes it. Uploading a file with the same name from the same folder replaces the earlier copy.

How the list is organised

The documents are grouped under the contract they are filed against: one heading per contract, showing the contractor, the ACC contract code, how many documents there are and the date of the most recent one. A heading is closed until you click it, so a library of several hundred documents opens as a short index of contracts. Searching or setting a filter opens what matched, and you can still close a heading while a filter is running. Anything that could not be filed against a contract sits at the bottom under **Not yet filed under a contract**.

Remove all on a heading clears out that whole contract in one go – useful when a folder was picked by mistake and filled a contract with documents that do not belong there. It asks first and cannot be undone, and it removes only the documents the heading is showing, so setting a filter first narrows what goes. Every removal is recorded in Change history.

Finding a document

Use the filters above the list: **contractor**, **contract code**, **document type**, **filed / not yet filed**, and the search box, which looks through the titles, references, summaries and the full text of every document. The EOT Library also shows the days assessed and claimed per report, so the extension-of-time position per contractor is visible at a glance. Everything in both libraries is also read by ASK ME (chapter 15).

Scanned PDFs. A PDF that is only a picture of the pages has no readable text: the document is stored but shows **Unread**. Run OCR (Adobe Acrobat → Scan & OCR → Recognize Text) and upload it again, or file it by hand with Change.

15. ASK ME: questions in plain English

Village Boutique Hotel
Commercial Dashboard

PROJECT / ASSET: 1TBO1006 - Village Bouti...
SUB-ASSET: 1TBO1006.03 - Village B...

ASK ME
Village Boutique Hotel (VBH) - Monthly Report No 47 - Aug'26 - searches every register, report and library

ASK ME is not switched on for this server. Ask the administrator to add ANTHROPIC_API_KEY in the hosting settings (Render → Environment) and redeploy. Until then questions cannot be answered.

Ask a question in plain English about the project and reporting period selected in the top bar. The assistant reads the cost report, the movement, every register, the report library and the EOT and contract libraries, and answers with the figures and references, ending with a professional summary you can copy and paste.

- What is the anticipated final account and how has it moved since the last report?
- List every open early warning with its value and who raised it.
- Which bonds or insurances expire in the next 60 days?
- Summarise the EOT assessments issued to date and the days granted per contractor.
- Which contracts have late IPCs or late payments this period?
- Draft a short note for the client on the change management position this month.

Type your question in English...

Enter to send · Shift+Enter for a new line. Answers use the project and period in the top bar.

Executive Summary
Monthly Report No 47 - Aug'26 - cut-off 31-Aug-26 - all amounts SAR

APPROVED BUDGET
854,010,655.25

LATEST BUDGET
1,520,599,588.4
incl. transfers 666,588.93

VARIANCE TO LATEST BUDGET
-18,077,034.09
under budget

CERTIFIED TO DATE
1,456,666,271.5
97% of anticipated final

OPEN CHANGES BY STAGE

RFC	PVO	VO	DVO
25	37	28	80

74 change(s) open in total

OPEN CLAIMS
0
0.00 claimed and pending

Movement since Monthly Report No 46 - Jul'26

Monthly Report No 46 - Jul'26 holds exactly the same figures as Monthly Report No 46 - Jul'26 was locked after this month's data was loaded, or when this imports → Monthly report workbook, choose Monthly Report No 47 - Aug'26 then re-import Monthly Report No 47 - Aug'26.

Cost report

- Approved Budget
- Budget Transfers
- Latest Budget
- Determined VOs

The ASK ME panel opens from the coloured button in the top bar. Type a question, or click one of the examples.

The **ASK ME** button in the top bar opens an assistant that knows everything on the dashboard for the project and reporting period selected in the top bar: the cost report (Level 1 and Level 2), the movement since the previous report, every register (changes, claims, early warnings, risks, provisional sums, bonds, contracts, IPC logs, final accounts, budget transfers, meetings and actions), the report library, the month-end checklist, and the EOT and Contract libraries. Ask in ordinary English, for example:

- "What is the anticipated final account and how has it moved since the last report?"
- "List every open early warning above SAR 1 million with its contractor."
- "Which bonds expire in the next 60 days?"
- "Summarise the EOT assessments issued to Shapoorji and the days granted."
- "Draft a note for the client on the change management position this month."

- 1 Click **ASK ME** in the top bar (every role except report-only accounts).
- 2 Type the question and press **Enter** (Shift+Enter for a new line), or click an example. The assistant reads the whole project and answers in a minute or so; long questions on a big project can take longer.
- 3 The answer quotes the figures, references, dates and statuses from the dashboard and shows its working. Below it, the green **Summary for copy-paste** box holds a self-contained professional summary – press **Copy** and paste it into an email, a report or the minutes.

4

Ask follow-up questions in the same panel; the conversation is kept until you close it or press the eraser to start again.

What it will and will not do. The assistant only uses what is on the dashboard; it says when something is not recorded and where it would normally be. It never changes any data. Every question is noted in the Change history with the name of the person who asked.

Switching it on. ASK ME, the library reading engine and the Claim EAR drafting all use the same ANTHROPIC_API_KEY in the hosting settings (Render → Environment). Until it is added, the ASK ME panel shows a notice and questions cannot be answered.

16. If something goes wrong

What you see	What to do
"Login failed" on the office laptop	Try your phone or another browser. If the phone works, the office network is blocking the site; ask IT to allow the address.
The page takes a long time or shows a 502 message	The free hosting sleeps after 15 minutes without visitors and needs up to a minute to wake up. Wait, then reload once.
A field turns red when saving	Read the message under the field. Usually a required field is empty or a value is not in the dropdown list.
"This period is locked"	You are trying to change an issued month. Switch the top bar to the open month, or ask an Admin to unlock.
A dropdown does not have the package / contractor you need	Ask an Admin to add it under Settings, or tick "create missing values" when importing a workbook.
The import lists rows with errors	The rest of the file was imported. Fix the cells named in the message in Excel, then import the same file again choosing the same period; fixed rows are updated, nothing is duplicated.
The Level 1 – Level 2 check is red	A cost line is missing an asset or category. Open Cost Report → Line setup and complete the line.
Claim EAR shows "Drafting engine not configured"	The administrator must add ANTHROPIC_API_KEY in the hosting settings (Render → Environment) and redeploy. Until then Create EAR gives a skeleton only.
A claim document has an orange triangle	The engine cannot read inside it: a scanned PDF (run OCR and upload again), an image (fine, it is kept as evidence) or a .msg / .zip / .dwg file (save the content as PDF).
"Writing the report" runs for a long time or the connection drops	A big claim takes several minutes. Wait, then reload the case page: if the green box shows the file, it was saved; otherwise press Create EAR again.
A report was imported into the wrong month, or twice	Open Monthly Report → All reports (library). Use Change to correct its number or cut-off, Re-upload to load the right workbook into it, or the bin to delete a period created by mistake.
Period movement shows 0.00 and the "previous" figures equal this report's	Both reports hold the same stored figures (this happened with older versions when a report was locked after the next month's data was loaded). Open Monthly Report → All reports and use Re-upload on the month that is wrong: each report is stored on import and the latest month's live figures are put back automatically.
"... has no stored data of its own" when locking	The report was created before its data was stored and a newer report exists. Re-upload its workbook from All reports (library); it is stored on import and can then be locked.

Numbers on the Executive Summary look wrong	Check the top bar period, then the source module (a change not linked to a cost line, an early warning left Open, an IPC with a wrong cumulative value).
---	--

Health check for support: <https://commercial-dashboard-kkz4.onrender.com/api/health> shows whether the database and the backup are working.

Questions or ideas for the dashboard? Note them in the minutes of meeting under "Dashboard" so they are not forgotten.
