

The Marina Commercial Dashboard User Guide

The Marina – Marina Village (Programme 1, Triple Bay)

A simple, step-by-step guide with pictures

Website: <https://commercial-dashboard-kkz4.onrender.com>

Version 2.16 · September 2026 · Prepared for the Commercial team

What is in this guide

1. What the dashboard is, in one minute
2. Logging in (on a computer or a phone)
3. Finding your way around the screen
4. The home page: Executive Summary
5. How every list works (search, filter, add, edit, export, history)
6. The monthly routine, step by step
7. Importing your Excel monthly report
8. The modules, one by one
9. Locking a month and generating the report
10. Settings, users and backups
11. Who can do what (roles)
12. If something goes wrong

Reading tip. Every picture has red numbered circles. The text under the picture explains what each number is. You can jump straight to the chapter you need; each one stands on its own.

1. What the dashboard is, in one minute

The Marina Commercial Dashboard is a website that replaces the monthly commercial report you used to build in Excel. Everything that used to live in the Excel schedules now lives in the dashboard:

- **Cost Report** (Schedules A and B) – budget, committed cost, changes, final account, certified to date.
- **Change Management Tracker** (Schedule C) – every RFC, PVO, VO, EI and DVO.
- **Early Warnings, Risks, Provisional Sums, Bonds & Insurance** (Schedules D, F and G). Claims & Disputes (Schedule E) come from the Claims Tracker import, not from the monthly workbook.
- **Invoices & Payments** with the IPC log per contract and the **Final Account Status** (Schedule H).
- **Cash Flow** (Schedule I) and **Budget Transfers** (Schedule J).
- **Executive Summary** and **Minutes of Meeting**.


The big difference from Excel: **you only type the facts** (a new change, an IPC, a bond expiry date). The dashboard does all the sums, colours the warnings, and prints the monthly report as a PDF or an Excel file. Every month is **locked** when it is issued, so the next month can show what moved.

Golden rule: type each fact once, in the right list. The cost report and the executive summary update themselves.

You do not need to install anything. It works in any web browser, on a laptop or on a phone.

2. Logging in

- 1 Open your browser (Edge, Chrome or Safari) and go to **https://commercial-dashboard-kkz4.onrender.com**.
- 2 Type your **email** 1 and your **password** 2 .
- 3 Click **Sign in** 3 .



The login page. An Admin creates your login under Settings → Users (see chapter 10).

First time? The site may take up to a minute to wake up if nobody has used it for a while. Just wait; do not refresh many times.

Office laptop says "Login failed"? Some company networks block the login. Try your phone, or another browser. If it works on the phone, ask IT to allow the site address.

On a phone

The same address works on a phone. The menu is hidden behind the **three lines** button at the top left. Tap it to open the list of pages.

1TB01031 · Marina Villag...

1TB01031CM

1TB01031 · 1TB01031.01 · MODULE 11

Executive Summary

Monthly Report No 51 – Sep'26 · cut-off 30-Sep-26 · all amounts SAR

Open

Checklist 0/12

L1 – L2 check OK

PDF

Excel

APPROVED BUDGET

E

880,852,840.00

LATEST BUDGET

G

782,898,187.27

incl. transfers -97,954,652.73

COMMITTED

I

735,395,313.45

incl. DVOs 8,007,274.86

ANTICIPATED FINAL ACCOUNT

N

748,844,738.15

PVO/RFC/EW/claims 13,449,424.70

VARIANCE TO LATEST BUDGET

O

-34,053,449.12

under budget

N

CERTIFIED TO DATE

P

CDCommercial DashboardX1TB01031CM

MODULES

Project Setup1

Cost Report2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

N

All amounts in SAR · Dates DD-MMM-YY

P

3. Finding your way around the screen

Commercial Dashboard

1TB01031 · Marina Villag... 1TB01031.01 · The Marina Monthly Report No 51 - ... Open

Executive Summary

Monthly Report No 51 - Sep'26 · cut-off 30-Sep-26 · all amounts SAR

APPROVED BUDGET **880,852,840.00**

LATEST BUDGET **782,898,187.27**
incl transfers -97,954,652.73

COMMITTED **735,395,313.45**
incl DVOs 8,007,274.86

ANTICIPATED FINAL ACCOUNT **748,844,738.15**
PVO/RFC/EW/claims 13,449,424.70

VARIANCE TO LATEST BUDGET **-34,053,449.12**
under budget

CERTIFIED TO DATE **735,627,234.98**
98% of anticipated final account

WORKS TO COMPLETE **13,217,503.17**

PERIOD MOVEMENT **-4,760,000.00**
vs Monthly Report No 50 - Aug'26

OPEN CHANGES BY STAGE

1	1	0	2
RFC	PVO	VO	DVO

121 change(s) open in total

OPEN CLAIMS **6**
46,455,401.69 claimed and pending

OPEN EARLY WARNINGS **6**
7,105,062.89 potential cost · 2 open ri...

BONDS & INSURANCE EXPIRING **29**
29 expired · 0 within 30 days · 0 with...

Movement since Monthly Report No 50 - Aug'26

Cost report	Previous (Monthly Report No 50 - Aug'26)	This report	Movement
Approved Budget	880,852,840.00	880,852,840.00	-
Budget Transfers	-97,954,652.73	-97,954,652.73	-
Latest Budget	782,898,187.27	782,898,187.27	-
Determined VO's	7,917,459.86	8,007,274.86	+89,815.00
Committed	735,305,498.45	735,395,313.45	+89,815.00
Potential VO's	5,794,176.81	5,704,361.81	-89,815.00

The screen has three parts: the menu on the left, the blue bar at the top, and the page in the middle.

- **1 Menu.** One line per module, numbered 1 to 12 like the Excel schedules. Click a line to open that page. Under **Cost Report** there are three direct buttons: **Level 1 – Executive**, **Level 2 – Detailed** and **Line setup**. Under Invoices & Payments sits **Final Account Status**. "User guide", "Change history" and "Settings" are at the bottom.
- **2 Programme.** Which programme you are looking at (1TB01031 Marina Village).
- **3 Asset.** The asset inside the programme (1TB01031.01 The Marina).
- **4 Reporting period.** The month you are working in, for example "Monthly Report No 50 – Aug'26". The little padlock tells you if the month is **Locked** (issued, read-only) or **Open** (you can still type).
- **5 You.** Your name and role. Click it to sign out.
- **6 The page.** Whatever you chose in the menu.

The period matters. Everything you see and type belongs to the period shown in the top bar. Before you start a new month, make sure the top bar shows the new month (chapter 6 explains how to create it).

Looking back at an issued month. Choose any locked month in the top bar (for example "Monthly Report No 50 – Aug'26"). The badge changes to **Issued · viewing** and every page, from the Executive Summary to the IPC logs, shows that month exactly as it was issued. Nothing can be edited while you

look at an issued month; a green note on each list reminds you. Switch back to the open month to continue working.

4. The home page: Executive Summary

When you log in you land on the Executive Summary. It is the one-page picture of the month, the same numbers that go on the first pages of the monthly report.

Executive Summary
Monthly Report No 51 – Sep'26 · cut-off 30-Sep-26 · all amounts SAR

APPROVED BUDGET (E)
880,852,840.00

LATEST BUDGET (G)
782,898,187.27
incl transfers -97,954,652.73

COMMITTED (I)
735,395,313.45
incl DVOs 8,007,274.86

ANTICIPATED FINAL ACCOUNT (N)
748,844,738.15
PVO/RFC/EW/claims 13,449,424.70

VARIANCE TO LATEST BUDGET (O)
-34,053,449.12
under budget

CERTIFIED TO DATE (P)
735,627,234.98
98% of anticipated final account

WORKS TO COMPLETE (Q)
13,217,503.17

PERIOD MOVEMENT (S)
-4,760,000.00
vs Monthly Report No 50 – Aug'26

OPEN CHANGES BY STAGE
RFC: 1, PVO: 1, VO: 0, DVO: 2
121 change(s) open in total

OPEN CLAIMS
6
46,455,401.69 claimed and pending

OPEN EARLY WARNINGS
6
7,105,062.89 potential cost · 2 open r.l.

BONDS & INSURANCE EXPIRING
29
29 expired · 0 within 30 days · 0 with...

Movement since Monthly Report No 50 – Aug'26

Cost report	Previous (Monthly Report No 50 – Aug'26)	This report	Movement
E Approved Budget	880,852,840.00	880,852,840.00	–
F Budget Transfers	-97,954,652.73	-97,954,652.73	–
G Latest Budget	782,898,187.27	782,898,187.27	–
H Determined VOs	7,917,459.86	8,007,274.86	+89,815.00
I Committed	735,305,498.45	735,395,313.45	+89,815.00
J Potential VOs	5,794,176.81	5,704,361.81	-89,815.00

The Executive Summary for Monthly Report No 50 – Aug'26.

What the eight big numbers mean

Card	In plain words
Approved Budget (E)	The budget as originally approved, all lines added up.
Latest Budget (G)	Approved budget plus or minus budget transfers.
Committed (I)	Latest budget plus approved (determined) variation orders. What we are contractually bound to.
Anticipated Final Account (N)	Committed, plus potential changes, RFCs, early warnings and claims. Our best estimate of the final bill.
Variance to Latest Budget (O)	Anticipated final account minus latest budget. Green = under budget, red = over.
Certified to Date (P)	The value certified so far in the IPC logs.
Works to Complete (Q)	Anticipated final account minus certified to date.
Period Movement (S)	How much the anticipated final account moved since last month's locked report.

Below the numbers you see the **open items** (changes by stage, open claims, early warnings, bonds expiring), the **Key issues** box (type the month's headline issues here; they print on the report), and the **Actions** list from the minutes of meeting.

The three chips at the top right tell you at a glance: is the period **Locked**, how many **checklist** items are done, and whether the **Level 1 – Level 2 check** of the cost report is OK. The red **PDF** and green **Excel** buttons download this page as a print-ready file.

Movement since the last issued report

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

User guide (PDF)

Change history

Settings

Movement since Monthly Report No 50 – Aug'26

Monthly Report No 50 – Aug'26 → Monthly Report No 51 – Sep'26

PDFExcel

Cost report	Previous (Monthly Report No 50 – Aug'26)	This report	Movement
E Approved Budget	880,852,840.00	880,852,840.00	–
F Budget Transfers	-97,954,652.73	-97,954,652.73	–
G Latest Budget	782,898,187.27	782,898,187.27	–
H Determined VO's	7,917,459.86	8,007,274.86	+89,815.00
I Committed	735,305,498.45	735,395,313.45	+89,815.00
J Potential VO's	5,794,176.81	5,704,361.81	-89,815.00
K RFCs	0.00	640,000.00	+640,000.00
L Early Warnings	12,505,062.89	7,105,062.89	-5,400,000.00
M Claims	0.00	0.00	–
N Anticipated Final Account	753,604,738.15	748,844,738.15	-4,760,000.00
O Variance to Budget	-29,293,449.12	-34,053,449.12	-4,760,000.00
P Certified to Date	733,924,921.33	735,627,234.98	+1,702,313.65
Q Works to Complete	19,679,816.82	13,217,503.17	-6,462,313.65

Changes by stage

Open changes at each stage and the cost-report amount they carry, previous report vs this one.

RFC

12 → 13

640,000.00

was 0.00 +640,000.00

PVO

7 → 7

0.00

was 0.00 --

VO

7 → 7

2,029,260.00

was 2,029,260.00 --

DVO

89 → 88

24,148,878.74

was 24,148,878.74 --

Changes (RFC / PVO / VO / DVO)

161 → 162 rows +1 new 1 updated

cost-report amount: 36,826,671.86 → 37,556,486.86 (+729,815.00)

CH-162 Additional mooring bollards at the fuel dock

Claims & disputes

7 → 7 rows 1 updated

claimed (SAR): 46,455,401.69 → 46,455,401.69 (–)

CL-005 EOT-03 Extension of time - Precast Elements due to Delay in Utilities / Services related d


Pending → Approved

The comparison with the previous locked month: every cost report column (previous, this report, movement), open changes by stage, and then each register with its new, updated and removed rows and the amounts that moved.

This panel appears as soon as an earlier month has been locked. It answers the question "what changed since last month?" line by line: a new RFC, a PVO that became a DVO, a claim determined, an early warning converted, a bond renewed, a new IPC, a final account closed. Green means favourable, red means adverse. It is printed in the monthly report and can be downloaded on its own with the PDF and Excel buttons on the panel.

The eight big numbers follow the Excel "Level 01" convention: budget columns (E, F, G) include the budget hold; the change, forecast and certified columns exclude it, so the unallocated hold shows as "under budget" in the variance.

Key period movements

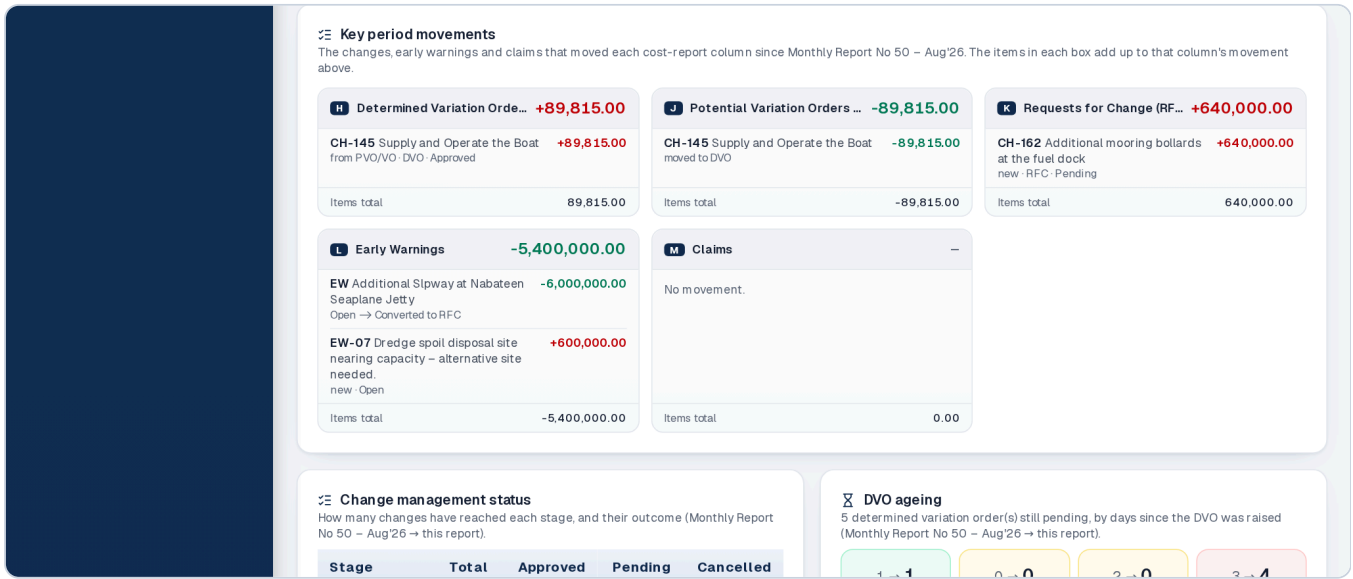

Payment status tracker

Payment status tracker							
			17 contract(s) - certified 99% of revised value		49 late IPC(s) / payment(s)		
Contract	Contractor	Revised value	Certified to date	This period	% certified	Paid (net)	% paid
2200571 Active Triple Bay Marina Basin - Design and Build	Al Saad General Contra...	557,833,437.06	567,098,629.26	0.00	101.7%	567,098,629.26	
2240167 Active Design and Construction of Floating Pontons	MME - Majestic Marine...	79,528,534.75	83,100,000.00	+1,702,313.65	104.5%	76,313,911.35	
2240276 Active Construction of Fixed Jetty for the Marina Ama...	Al Saad General Contra...	42,516,240.16	35,691,309.84	0.00	84.0%	35,691,309.84	
2250076 Active Constructing Boardwalks & Jetties for Hijaz Isl.	Elmar Marinas Khaleej...	28,247,178.71	19,809,003.40	0.00	70.1%	18,897,747.64	
2210172 Closed Marina Basin Supervision Consultant	WSP Middle East	13,900,878.64	12,617,276.95	0.00	90.8%	10,900,659.86	
2200593 Closed Marina Ecological Coral Relocation	Five Oceans Environme...	5,618,903.00	3,895,708.00	0.00	69.3%	3,895,708.00	
2200340 Closed Triple Bay Marina Basin - Early Contractor Inv...	Al Saad General Contra...	4,791,717.00	4,861,467.00	0.00	101.5%	4,861,467.00	
2200317 Closed Triple Bay Marina Basin - Early Contractor Inv...	Dredging International...	3,995,139.75	3,995,140.00	0.00	100.0%	3,995,140.00	
2210091 Closed Coral Ecology Surveys	Five Oceans Environme...	1,750,000.00	1,750,000.00	0.00	100.0%	0.00	
2250226 Active Sydney Seaplane - Seaplane Consultant - 12...	Sydney Seaplanes Asia...	1,694,211.00	1,178,947.70	0.00	69.6%	1,178,947.70	

One row per contract: revised value, certified to date, certified this period, % certified, net paid, % of certified already paid, and how many IPCs or payments were late against the contract dates.

The green table gives you the payment position of every contract without opening the IPC log. Percent bars fill up as the contract is certified and paid. A red number in the "Late" columns means the IPC was issued, or the payment made, after the contractual due date; open the contract's IPC log under Invoices & Payments to see which ones. All three new sections print in the Executive Summary and Movement PDFs and Excel files.

Email the Report

CD Commercial Dashboard

PROGRAMME
 1TB01031 · Marina Villag...

ASSET
 1TB01031.01 · The Marina

REPORTING PERIOD
 Monthly Report No 51 - ...

CM Commercial Manager
 Admin

MODULES
 Project Setup 1
 Cost Report 2

1TB01031 · 1TB01031.01 · MODULE 11
Executive Summary
 Monthly Report No 51 - Sep'26 · cut-off 30-Sep-26 · all amounts SAR

Open Checklist 0/12 L1 - L2 check OK

Email the Report

PDF Excel

The blue **Email the Report** button sits in the Executive Summary header next to the PDF and Excel buttons.

Email the Report

To: nobody yet – add email addresses to the distribution list under Project Setup, or type them in Outlook
 Subject: 1TB01031.1TB01031.01 The Marina · Monthly Report No 51 – Sep'26 – Commercial summary (draft)
 Attachments: Executive Summary.pdf · Cost Report Level 1.pdf · Cost Report Level 2.pdf

Dear all,
 Please find attached the **Executive Summary**, **Cost Report Level 1 (Executive)** and **Cost Report Level 2 (Detailed)** for **Monthly Report No 51 – Sep'26 – 1TB01031.01 The Marina** (cut-off 30-Sep-26, draft from live data). The headline position is:

Cost report (SAR)	Monthly Report No 50 – Aug'26	This report	Movement
E Approved Baseline Budget	880,852,840.00	880,852,840.00	–
G Latest Budget (incl. transfers)	782,898,187.27	782,898,187.27	–
I Committed Costs	735,305,498.45	735,395,313.45	+89,815.00
J Potential VOs	5,794,176.81	5,704,361.81	-89,815.00
K Requests for Change	0.00	640,000.00	+640,000.00
L Early Warnings	12,505,062.89	7,105,062.89	-5,400,000.00
M Claims	0.00	0.00	–
N Anticipated Final Account	753,604,738.15	748,844,738.15	-4,760,000.00
O Variance to Latest Budget	-29,293,449.12	-34,053,449.12	-4,760,000.00
P Certified to Date	733,924,921.33	735,627,234.98	+1,702,313.65
Q Works to Complete	19,679,816.82	13,217,503.17	-6,462,313.65

Budget columns include the budget hold; change and forecast columns exclude it. Variance to Latest Budget: negative = under budget.

Key movements since Monthly Report No 50 – Aug'26

- H Determined Variation Orders (DVO): +89,815.00**
 CH-145 Supply and Operate the Boat (from PVO/VO · DVO · Approved): +89,815.00
- J Potential Variation Orders (PVO / VO): -89,815.00**
 CH-145 Supply and Operate the Boat (moved to DVO): -89,815.00
- K Requests for Change (RFC): +640,000.00**
 CH-162 Additional mooring bollards at the fuel dock (new · RFC · Pending): +640,000.00
- L Early Warnings: -5,400,000.00**

Buttons: Copy summary, Open mail app (text only), Open in Outlook with PDFs attached

The dashboard writes a short email for you: who it goes to, the subject, the headline table (last month, this month, movement), the key movements, the open items and your key issues. Nothing to type.

Press the button and check the preview. Then choose one of the three buttons at the bottom:

1. **Open in Outlook with PDFs attached** (on your PC). A small draft file is downloaded. Open it from your Downloads folder and Outlook shows the email ready to send, with the Executive Summary, Level 1 and Level 2 PDFs already attached. Check it, add anyone missing in "To", and press Send.
2. **Open mail app (text only)** (on your phone). Your mail app opens with the text summary. A web page cannot attach files on a phone, so attach the PDFs yourself if you need them.
3. **Copy summary**. Puts the formatted table and text on the clipboard so you can paste it into any email or Teams message.

The "To" list is filled from the email addresses in **Project Setup** → **Distribution list & project team**. Add everyone's email there once and every month's email is addressed automatically. If the month is not yet locked the subject says "(draft)".

5. How every list works

Almost every page is a **list** (the app calls it a register): changes, claims, bonds, IPCs and so on. They all work the same way, so once you know one, you know them all.

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 51 - ...

MODULE 3

Change Management Tracker

Every change in one record, followed from Early Warning → RFC → PVO → VO → EI → DVO → Funding. Approved DVOs, live PVO / VOs and RFCs feed the cost report automatically.

CHANGES
162
121 open

PENDING OVER 30 / 60 DAYS
0 / 106
open items by days since raised

COST REPORT – DVO (H)
8,007,274.86
PVO / VO (J) 5,704,361.81

COST REPORT – RFC (K)
640,000.00
all changes linked to a cost line

Status matrix

Number of changes at each stage by that stage's status

Stage	Cancelled	Approved	Pending	Superseded	Transferred	Review Complete	Other	Total
RFC	50	101	1	2	0	1	0	155
PVO	21	100	1	1	0	0	1	124
VO	15	96	0	0	0	0	1	112
DVO	10	97	2	0	0	0	0	109
Total	96	394	4	3	0	1	2	500

Days open > 30 Days open > 60 Highlighting applies to open changes only. Link each change to its cost report line so its value flows into columns H, J and K.

1 Search change management tracker... 2 Filters 3 Export 4 Import 5 Add Change

Contractor / Consultant	Project stage	Change category	Initiated by	Action pending by	Actions
Al Saad General Contracting Co. Ltd.	Post-Contract Variation	Design Dev	Employer	None	History Edit Delete
Al Saad General Contracting Co. Ltd.	Post-Contract Variation	Design Dev	Employer	None	History Edit Delete

The Change Management Tracker. The tools above the table are the same on every list.

- 1 **Search.** Type a word or a number; the table shows only matching rows.
- 2 **Filters.** Narrow the list by status, package, contractor and so on.
- 3 **Export.** Downloads the list as a formatted Excel file. For the version laid out exactly as in the monthly report use the red **PDF** and green **Excel** buttons in the page header.
- 4 **Import.** Loads rows from an Excel file (for a single list). For the whole monthly report use chapter 7 instead.
- 5 **Add.** Opens an empty form to add a new row.
- 6 **Sort.** Click any column heading to sort by it. Click again to reverse.
- 7 **History.** Who changed this row, when, and what the old value was.
- 8 **Edit.** Opens the row in a form so you can change it.
- 9 **Delete.** Removes the row (it asks you to confirm).

Filters

CD Commercial Dashboard

PROGRAMME
1TB01031 · Marina Villag...
ASSET
1TB01031.01 · The Marina
REPORTING PERIOD
Monthly Report No 51 – ...
Open

CM Commercial Manager
Admin

MODULES

- Project Setup 1
- Cost Report 2
- Level 1 – Executive
- Level 2 – Detailed
- Line setup
- Change Management 3**
- Claims & Disputes 4
- Early Warnings & Risks 5
- Provisional Sums 6
- Bonds & Insurance 7
- Invoices & Payments 8
- Final Account Status
- Cash Flow 9
- Budget Transfers 10
- Executive Summary 11
- Minutes of Meeting
- Monthly Report 12

MODULE 3
Change Management Tracker
Every change in one record, followed from Early Warning → RFC → PVO → VO → EI → DVO → Funding. Approved DVOs, live PVO / VOs and RFCs feed the cost report automatically.

PDF Excel

CHANGES
162
121 open

PENDING OVER 30 / 60 DAYS
0 / 106
open items by days since raised

COST REPORT – DVO (H)
8,007,274.86
PVO / VO (J) 5,704,361.81

COST REPORT – RFC (K)
640,000.00
all changes linked to a cost line

Status matrix

Number of changes at each stage by that stage's status

Stage	Cancelled	Approved	Pending	Superseded	Transferred	Review Complete	Other	Total
RFC	50	101	1	2	0	1	0	155
PVO	21	100	1	1	0	0	1	124
VO	15	96	0	0	0	0	1	112
DVO	10	97	2	0	0	0	0	109
Total	96	394	4	3	0	1	2	500

Days open > 30 Days open > 60
Highlighting applies to open changes only. Link each change to its [cost report line](#) so its value flows into columns H, J and K.

1

Filters
Refresh
Export
Import
+ Add Change

Overall status
All

Project / Asset
All

Package
All

Contractor / Consultant
All

Project stage
All

Change category
All

Initiated by
All

Click Filters and choose values. "Clear" removes them again.

Page 14 of 57

Adding or editing a row

The form. Fields with a star are required. Sections can be opened and closed. **2** Save stores the row; **3** Cancel closes without saving.

- Money is typed as a plain number, for example 1250000 . The dashboard shows it as 1,250,000.00 SAR.
- Dates are picked from the calendar and shown as **DD-MMM-YY**, for example 31-Aug-26.
- Dropdowns (package, contractor, status) only offer values from Settings. If a value is missing, an Admin adds it under Settings.
- If something is wrong, the field turns red with a message. Fix it and click Save again.

Change history

Change history · CH-001

10-Sep-26 12:36 · Commercial Manager [import](#)

Imported Change "CH-001"

programme: (blank) → 1
 item no: (blank) → CH-001
 description: (blank) → Changes to Amaala BIM Requirements
 overall status: (blank) → 81
 date raised: (blank) → 2021-10-18
 asset: (blank) → 1
 package: (blank) → 563
 contractor: (blank) → 151
 cost line: (blank) → 483
 project stage: (blank) → 37
 change category: (blank) → 53
 initiated by: (blank) → 41
 action pending by: (blank) → None
 closed date: (blank) → 2022-08-21
 ew ref: (blank) → 0
 rfc ref: (blank) → 1
 rfc rev: (blank) → 0
 rfc date: (blank) → 2021-10-18
 rfc status: (blank) → 81
 rfc aconex ref: (blank) → AMA-WTRAN-000150
 rfc time impact: (blank) → 0
 rfc tracker amount: (blank) → 1750.00
 rfc cr amount: (blank) → 0
 pvo ref: (blank) → 1
 pvo rev: (blank) → 0
 pvo date: (blank) → 2021-10-18
 pvo status: (blank) → 81
 pvo aconex ref: (blank) → AMA-WTRAN-000150
 pvo time impact: (blank) → 0
 pvo tracker amount: (blank) → 1750.00
 pvo cr amount: (blank) → 1750.00
 vo ref: (blank) → VO 01
 vo date: (blank) → 2021-11-12
 vo status: (blank) → 81
 vo cr amount: (blank) → 1750.00
 vo contractor amount: (blank) → 0
 vo employer aconex ref: (blank) → AMA-WTRAN-000930
 vo employer date: (blank) → 2022-08-21

Every change is recorded: who, when, old value, new value. Nothing is ever lost silently.

Colours

Coloured chips carry the same meaning everywhere: **green = fine / approved / closed**

amber = attention soon

red = overdue / expired / rejected

What every Excel download looks like

Every Excel file the dashboard produces is a normal, fully editable workbook, formatted the same way: a navy title band with a link back to the dashboard, coloured column headers, alternating row shading, thin borders, real dates and money formats, a frozen header row with filters, coloured status cells (green for approved or closed, amber for pending or open, red for rejected, expired or overdue) and coloured sheet tabs. Totals are **live SUM formulas**, not typed numbers. The cost report goes further: on Level 2 the columns G, I, N, O, Q and S are formulas of the input columns, the category sub-totals and grand totals are SUMs, and on Level 1 every category figure is a SUMIFS formula over Level 2 while Development Budget, Committed, Anticipated Final Account and the variances are formulas of the rows above, so you can change a line in Excel and both sheets recalculate. Two check cells at the foot of Level 1 must read zero. The full monthly report has an Index sheet whose titles are links to each schedule, and each sheet has a "◀ Index" link in its title band. A file you downloaded can be edited and uploaded again through the Import buttons or the Stand-alone imports; the dashboard finds the header row below the title band by itself.

6. The monthly routine, step by step

This is the whole job for one month. It takes a few minutes of clicking plus the time you spend typing the month's facts.

- 1 Create the new month.** Open **Monthly Report** → **New month (manual entry)**. The next report number and month-end date are already filled in; press **Start**. The month is created, becomes the current period in the top bar and gets its checklist. (You can still add a period under Settings → Reporting Periods if you prefer.)
- 2 Record the month's facts** in each module: new changes and updates to their stages, new IPCs, new early warnings, bond renewals, budget transfers, provisional sum instructions, claim letters.
- 3 Check the cost report.** Open Cost Report → Level 2. The columns update themselves. The "Level 1 – Level 2 check" chip must be green.
- 4 Write the key issues** in the box on the Executive Summary, and add the minutes of the monthly meeting under Executive Summary → Minutes of Meeting.
- 5 Tick the checklist** on Project Setup and fill in Prepared by / Reviewed by / Approved by.
- 6 Lock the month** (Admin only): the **Lock & issue** button at the bottom of the New month page, or Settings → Reporting Periods → Lock. The month freezes; nothing can change by accident.
- 7 Generate the report:** Monthly Report → Generate PDF and Generate Excel. Send them out as usual. Any single page (Executive Summary, Level 1, Level 2, a schedule, the movement analysis) can also be downloaded on its own with the PDF / Excel buttons on that page.
- 8 Compare months:** pick any earlier locked month in the top bar to see that report; pick the current month to see the movement panel comparing it with the last issued one.

The New month page: manual entry without Excel

The screenshot shows the 'New monthly report – manual entry' page. The top navigation bar includes the 'The Marina' logo, programme and asset dropdowns, a reporting period dropdown, and a user profile. The left sidebar lists various modules, with 'Monthly Report' selected. The main content area has a title 'New monthly report – manual entry' and a description. It contains two main steps: 'Start the month' and 'Enter the month, module by module'. The second step lists 12 modules, each with a radio button, a column reference, a 'this month' status, and an 'Open' button.

Module	Column	Status	Action
Budget transfers	column F	0 this month	Open →
Cost report lines	column E-S	0 this month	Open →
Change management	column H, J, K	0 this month	Open →
Early warnings & risks	column L	0 this month	Open →
Claims & disputes	column M	0 this month	Open →
Provisional sums		0 this month	Open →
Bonds & insurance		0 this month	Open →
Invoices & payments	column P	0 this month	Open →
Cash flow		0 this month	Open →
Minutes, actions and key issues		0 this month	Open →
Report control		0 this month	Open →

Three steps on one page: start the month, enter it module by module (each row opens the module, shows how many rows were added or changed this month and which cost report column it feeds, and has a tick box), then review and Lock & issue.


A month entered by hand and a month imported from Excel produce exactly the same outputs: the Executive Summary, movement, Level 1 and Level 2, every schedule, the Claims and Final Account status reports, the emails and the full monthly report are all built from the registers, never from the Excel file. Import when you have the workbook; type when you do not; mix the two freely (for example, type the month and use a stand-alone import for the IPC logs).

Alternative for step 2: if you still prepare the month in your Excel workbook, upload it instead of typing. Chapter 7 shows how. The dashboard reads all the schedules in one go.

Locked months cannot be edited. If you really must correct an issued month, an Admin can Unlock it in Settings → Reporting Periods, make the correction, and Lock it again.


7. Importing your Excel monthly report

You can upload your monthly report workbook (the one with Schedule A to J, FA Status, Early Warning and the Schedule H sheets) exactly as it is. The dashboard recognises the layout, cleans it up and records everything against the reporting period.

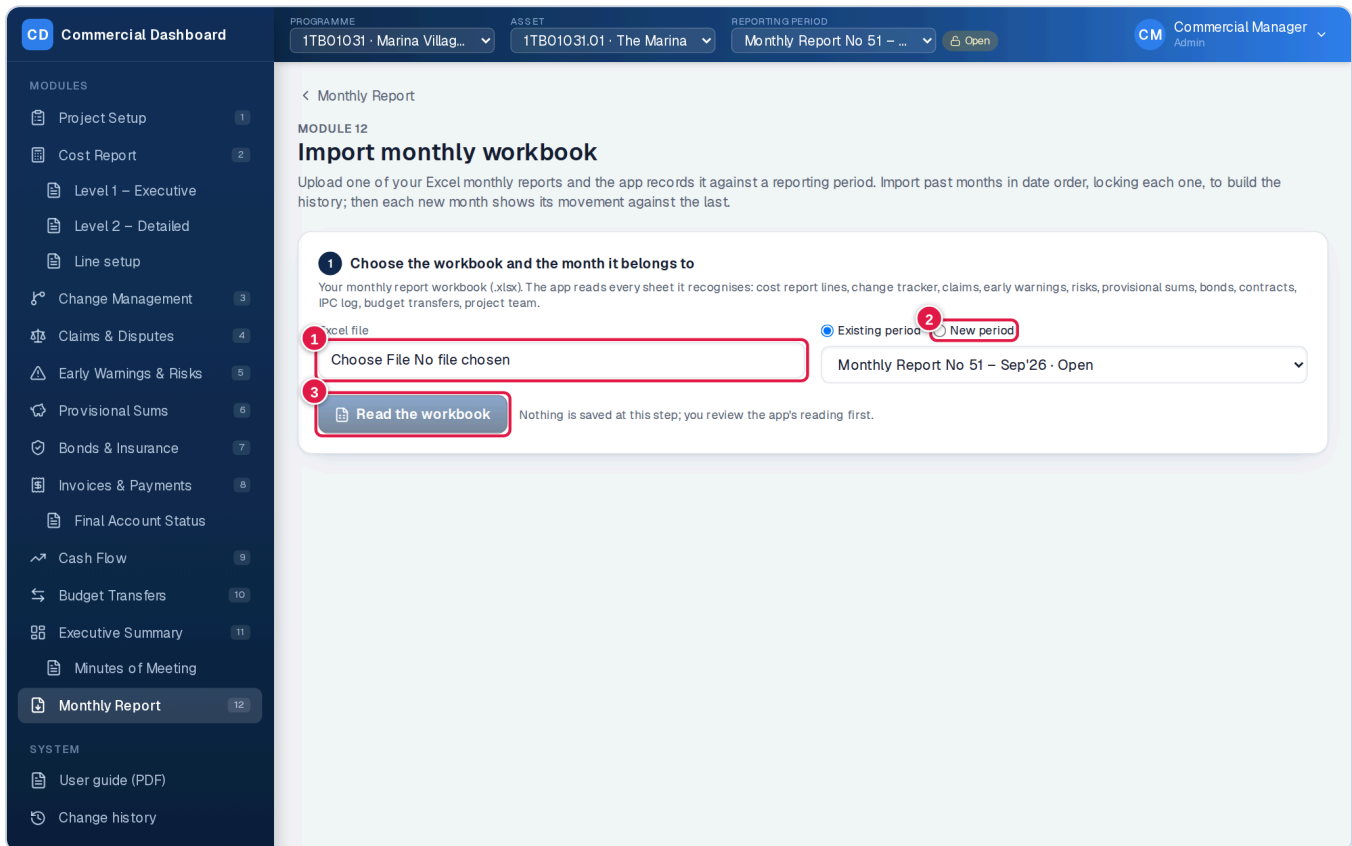

Stand-alone imports → Monthly report workbook. Step 1: choose the file and the period.

- 1 In the left menu, under **Stand-alone imports**, click **Monthly report workbook** (the Monthly Report page also has a button for it).
- 2 Click **Choose file** 1 and pick your Excel workbook (.xlsx).
- 3 Choose the period. For a month that does not exist yet choose **New period** 2 ; the report number and cut-off date are filled in from the workbook's Data Input sheet. Check them.
- 4 Click **Read the workbook** 3 . Nothing is saved yet. The upload takes a moment for a large file.
- 5 A green box confirms that your report layout was recognised. Below it, each sheet is listed with the register it goes to and the columns it read. Normally there is nothing to change.
- 6 Leave the two boxes ticked: **create missing packages, contractors and dropdown values**, and **Lock the period after importing** (for past months).
- 7 Click **Import**. A results table shows how many rows were added or updated per sheet, and any row that could not be read with the reason.

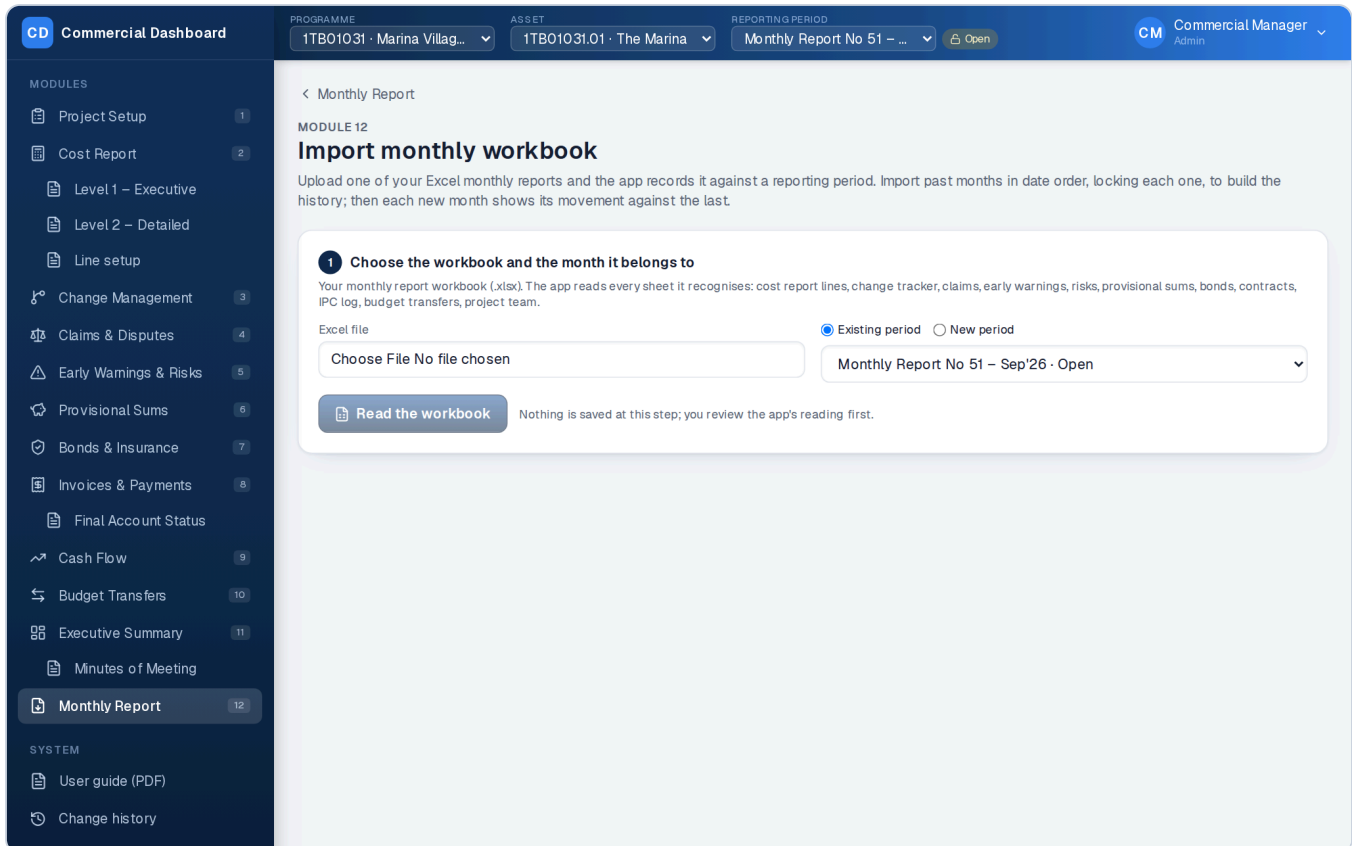

The import page after the workbook was read: one block per sheet, with the columns it recognised.

What happens to your numbers

- Rows are matched by their key (cost code, item number, claim number, IPC number). Uploading the next month **updates** the existing rows and adds the new ones. Nothing is duplicated.
- The cost report reproduces Schedule B: DVOs feed column H, live PVO/VOs feed J, early warnings feed L. The totals for E, F, G, H, J and L tie to the Excel exactly.
- Certified to date (P) is taken from the IPC logs, which are more up to date than the certified column in Schedule B.
- Contractor names are tidied to one spelling each (for example "Al Saad", "ALSAAD GENERAL CONTRACTING" and "ALS - Prelims" all become Al Saad General Contracting Co. Ltd.).

How each report's data is kept. Every monthly report has its own stored copy of all the registers and of the calculated cost report. The copy is taken when the report's workbook is imported, when the report is locked, and when the next month is started. The **latest** report (highest number) is the live one: the registers you edit belong to it. Every earlier report is shown from its stored copy, read-only, whether or not it is locked. So the movement between two months always compares two stored reports, and you can import the months in any order: importing an older month never disturbs the latest month – the older month is rebuilt from its own workbook (on top of the nearest earlier stored report, or from nothing), stored as its own report, and the latest month's live figures are put back automatically. A stand-alone import into an earlier report updates that report's own stored copy.

Reports that show the same figures month after month (for example 48, 49 and 50 all with the same anticipated final account) were locked with older versions of the dashboard, which froze whatever the live data was at the time. Fix them once: open Monthly Report → All reports (library) and **Re-upload** each report with its own workbook, oldest first, ticking "Lock the period after importing". Each re-upload stores that month on its own; the latest month is never affected.

Locking issues a report. The latest report is frozen from the live registers; an earlier report is issued with the copy stored when it was imported. If an earlier report has no stored copy (it was created before this version and never imported), the dashboard asks you to re-upload its workbook before locking, so another month's figures are never frozen under its name.

Stand-alone imports: update one part of the current report

The screenshot shows the 'Commercial Dashboard' interface. The top bar includes 'PROGRAMME' (1TB01031 · Marina Villag...), 'ASSET' (1TB01031.01 · The Marina), and 'REPORTING PERIOD' (Monthly Report No 51 - ...). The left sidebar lists modules, with 'Stand-alone imports' highlighted. The main content area is titled 'STAND-ALONE IMPORTS' and 'Import Bonds & Insurance'. It contains instructions to update the bonds and insurance log from Excel. A section titled '1 Choose the Excel file' prompts the user to upload a file, with a note that only the bonds sheet is used. A 'Read the workbook' button is visible, with a note that nothing is saved at this step.

The **Stand-alone imports** section of the left menu: Monthly report workbook, Bonds & Insurance, Invoices & Payments, Final Account Status and Claims Tracker. Each page says which report it will update.

Between monthly reports you often get a fresh Excel for just one thing: a new bonds schedule, the latest IPC logs, an updated FA Status, or the programme-wide Claims Tracker. The stand-alone import pages take that one file and update **only that part** of the report selected in the top bar. Nothing else changes.

- 1 Check the top bar first: the import goes into the reporting period shown there. If that month is locked (issued) the page tells you so and refuses; switch to the open month.
- 2 Open **Stand-alone imports** and pick the page: **Bonds & Insurance**, **Invoices & Payments** (contracts and IPC logs), **Final Account Status** or **Claims Tracker**.

- 3 Choose the file. You can upload the single sheet, the Excel you downloaded from that module's page (a handy way to edit in Excel and re-upload), or even the whole monthly workbook: the page only uses the sheets that belong to it and skips the rest.
- 4 Click **Read the workbook**, check the columns, then **Import**. Rows are matched by their reference (bond ref, PO number and IPC number, ACC code, claim number): existing rows are updated, new rows are added, nothing is duplicated.

The Claims Tracker

Commercial Dashboard

PROGRAMME: 1TB01031 - Marina Villag... ASSET: 1TB01031.01 - The Marina REPORTING PERIOD: Monthly Report No 51 - ...

STAND-ALONE IMPORTS

Import Claims Tracker

Pick our claims out of the AMAALA Claims Tracker workbook and update Claims & Disputes for the current report.

Updating **Monthly Report No 51 – Sep'26** only (the report selected in the top bar). To update another month, change the period in the top bar first.

[Executive Summary](#)

- 1 Choose the Excel file**

Upload the Claims Tracker workbook (AMA-CM-FRM-0018, the file with the Program_01 sheet). Only the claims whose contract number or asset code belongs to the programme and asset in the top bar are kept; each is linked to our cost report line by its contract code (e.g. 1TB01031C02 → 031C02). Claims already in the dashboard are matched by their letter references and updated; the others are added as CT-###.

Excel file – Claims Tracker (Program_01 sheet)

Choose File claims.xlsx

Read the workbook Nothing is saved at this step; you review the app's reading first.

Updates this report only
Monthly Report No 51 – Sep'26
 The report selected in the top bar. Rows are matched by their reference number: existing rows are updated, new ones added. Nothing else in the dashboard changes.
- 2 Check how each sheet was read**

The file layout was recognised and converted automatically.

 - Claims Tracker as of 2025-09-04: 158 claim(s) in the file, 13 belong to 1TB01031 / 1TB01031.01 and were kept; the rest (other assets) were ignored.
 - 13 linked to a cost report line by contract code; 12 matched an existing claim by letter reference (updated), 1 new (numbered CT-###).

For each sheet, confirm which register it is and which column goes to which field. Columns left as “— not used —” are ignored (calculated columns like Latest Budget or Anticipated Final Account should stay unused; the app calculates them). Your choices are remembered for next month.

▼ Claims Tracker 13 row(s) Claims & Disputes (Schedule E) 48 column(s) mapped

Column in your sheet	Example values
Claim No (claim ref)	CT-008-CT-008

The AMAALA Claims Tracker workbook after reading: the green box says how many of its claims belong to your programme and how many matched claims already in the dashboard.

The Claims Tracker (form AMA-CM-FRM-0018, the file with the **Program_01** sheet) lists every claim on the whole programme. The dashboard keeps only the rows whose contract number or asset code belongs to the programme and asset in the top bar, for example 1TB01031C02 or 1.TB.01.031.01. Each claim is linked to the right cost report line by its contract code (1TB01031C02 → line 031C02), so the claimed and determined amounts flow into column M of the cost report. Claims already in the dashboard are recognised by their letter references or their description and are updated; claims that are new get the number **CT-** followed by the tracker's item number, so you can always find them again in the tracker.

Time claims and cost claims are separate lines in the tracker (FULL TIA EAR and COST EAR). They stay separate in the dashboard too, marked [Time claim] and [Cost claim] in the description.

Three registers come only from their stand-alone imports. Claims & Disputes (Claims Tracker), Bonds & Insurance (Schedule G / bonds export) and Final Account Status (FA Status sheet) are never written by the monthly workbook import, whichever month it is for; the workbook's Schedule E, Schedule G and FA Status sheets are read but skipped. After each monthly import, run the three stand-alone imports with the latest files for that month. When an earlier month is rebuilt from its workbook, those three registers stay exactly as that report holds them, and every other row the workbook does not contain is removed from that report.

8. The modules, one by one

Module 1 – Project Setup & Report Control

TM

The Marina

Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

All reports (library)

New month (manual entry)

STAND-ALONE IMPORTS

Monthly report workbook

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 51 – ...Open

CMCommercial ManagerAdmin

MODULE 1

Project Setup & Report Control

The cover, index and data-input sheet of the monthly report: who, what and which period.

Project particulars

Edit

Programme nameMarina Village (Programme 1 – Triple Bay)

Programme code1TB01031

Asset nameThe Marina

Asset code1TB01031.01

ClientThe AMAALA Company

LocationTriple Bay, AMAALA

Shown for the Programme and Asset selected in the top bar. Other programmes / assets are managed under Settings.

Report control

OpenLock period

Report No51

Reporting periodMonthly

Period01-Sep-26 – 30-Sep-26

Locked—

Report number and dates come from the period selected in the top bar.
[Manage reporting periods](#)

Aconex reference
e.g. RSG-1TB01031-MCR-049

Document / transmittal reference for this month's report.

PREPARED BY
Name
mm/dd/yy

REVIEWED BY
Name
mm/dd/yy

APPROVED BY
Name
mm/dd/yy

Save report control

Report checklist

0 of 12 done

Tick each module once its section of Monthly Report No 51 – Sep'26 is complete. The checklist is kept per reporting period.

#	Module	Status	Done by	Comment
---	--------	--------	---------	---------

Project particulars, the report checklist, the distribution list and the sign-off names for the current period.

Use it once a month: tick the checklist as the report comes together and fill in Prepared by / Reviewed by / Approved by with the dates. These print on the cover of the report.

Page 24 of 57

Module 2 – Cost Report Level 1 & 2

Level 1 – Executive	Level 2 – Detailed	Line setup				
Cost Report – Executive		Professional Services	Early Works	Construction Works	Management Supervision	Commercial Management
		SAR	SAR	SAR	SAR	SAR
DEVELOPMENT BUDGET						
Previous Approved Budget		28,037,904.00	8,996,107.00	825,126,893.00	17,523,690.00	1,168,246.00
Approved Budget Transfers		52,544.33	0.00	-98,007,197.06	0.00	0.00
Development Budget (currently approved)		28,090,448.33	8,996,107.00	727,119,695.94	17,523,690.00	1,168,246.00
COMMITMENTS						
Contract Awards		18,514,917.11	8,996,107.00	699,877,014.48	0.00	0.00
DVO's (Determined Variation Orders)		1,243,492.42	-139,500.00	6,903,282.44	0.00	0.00
Committed		19,758,409.53	8,856,607.00	706,780,296.92	0.00	0.00
POTENTIAL OUT-TURN COSTS						
PVO's (Potential Variation Orders)		290,000.00	0.00	5,414,361.81	0.00	0.00
RFC's (Requests for Change)		0.00	0.00	640,000.00	0.00	0.00
Early Warnings		0.00	0.00	7,105,062.89	0.00	0.00
Claims		0.00	0.00	0.00	0.00	0.00
BALANCE TO PROCURE						
Uncommitted Packages		0.00	0.00	0.00	0.00	0.00
Anticipated Final Account		20,048,409.53	8,856,607.00	719,939,721.62	0.00	0.00
Variance to Budget		-8,042,038.80	-139,500.00	-7,179,974.32	-17,523,690.00	-1,168,246.00
Previous Report (Monthly Report No 50 – Aug'26)		-8,042,038.80	-139,500.00	-2,419,974.32	-17,523,690.00	-1,168,246.00
Difference		0.00	0.00	-4,760,000.00	0.00	0.00
CASH POSITION						
Certified to Date		16,005,999.23	8,856,607.00	710,764,628.75	0.00	0.00

Level 1 – Executive, laid out exactly like the **Level 01** sheet of your Excel report: one column per cost category (Professional Services, Early Works, Construction Works, Management Supervision, Commercial Management ...), then **Total**, **Previous** (the previous issued report) and **Movement**. Down the side: Development Budget, Commitments (Contract Awards, DVO's, Committed), Potential Out-Turn Costs (PVO's, RFC's, Early Warnings, Claims), Balance to Procure, Anticipated Final Account, Variance to Budget with the previous report and the difference, the cash position, and the comparison with last month's anticipated final account. Below the table, **Reasons for variance – this month** lists every item that moved the anticipated final account, with its amount and remark, and the NET movement. The order of the category columns is the order of Settings → Cost Categories.

Executive view. As on the Excel sheet, the budget rows include the unallocated "Remaining budget" lines (the budget hold) while every other row excludes them, so the unallocated budget shows in the variance as under budget. Green is under budget or a decrease; red is over budget or an increase.

Every column is calculated by the dashboard; you never type into the cost report itself except on the Line setup tab. Column letters follow the Excel:

Column	Comes from
E Approved Baseline Budget	Line setup (typed once)
F Budget Transfers	Budget Transfers module (plus transfers brought forward from the Excel)
G Latest Budget	E + F
H Determined VO's	Change Management: approved DVO's
I Committed	G + H
J Potential VO's, K RFC's	Change Management: live PVO / VO and RFC amounts
L Early Warnings	Early Warnings module (open items)
M Claims	Claims module (claims linked to a cost line)
N Anticipated Final Account	I + J + K + L + M
O Variance	N – G
P Certified to Date	Invoices & Payments: latest cumulative certified per contract
Q Works to Complete	N – P
R Previous, S Movement	Last month's locked report and N – R

PROFESSIONAL SERVICES				
PS.031D03	WSP Consultants	WSP Consultants - Employers ...	WSP Middle East	1TB01031.0
PS.031D04	Becon - Marine Relocation	Becon Developments Co - Co...	Beacon Development Company	1TB01031.0
PS.031D01	5 Ocean - Marine Survey 2210091	Five Oceans Marine Survey - ...	Five Oceans Environmental Services LLC	1TB01031.0
PS.031D06	Sydney SeaPlane	Sydney Seaplane - Seaplane ...	Sydney Seaplanes Asia Limited	1TB01031.0
PS.031F03	Haskoning - Navigation Simulation	Haskoning - Navigation Simulat...	Haskoning DHV Saudia	1TB01031.0
PS.031F02	Kaust-King Abdullah University of Science	Kaust-King Abdullah University...	KAUST – King Abdullah University of Science & Technology	1TB01031.0
<i>PS.98</i>	<i>Budget Hold</i>	<i>Remaining budget - Profession...</i>	—	<i>1TB01031.0</i>
Sub-Total Professional Services				
EARLY WORKS				
CN.031C01	ALS - Early Works	Al Saad - Early Works Package	Al Saad General Contracting Co. Ltd.	1TB01031.0
CN.031C03	JVD Early Works	JVD - Early Works	Dredging International Saudi Arabia (JVD)	1TB01031.0
Sub-Total Early Works				
CONSTRUCTION WORKS				
CN.031C02	Al Saad Prelims	Preliminaries and General	Al Saad General Contracting Co. Ltd.	1TB01031.0

Level 2 – Detailed, laid out like the **Level 02** sheet: the lines grouped by cost category, each block ending with its **Sub-Total**, then the GRAND TOTAL, the total excluding the budget hold (the executive view) and the Level 1 – Level 2 check. "Remaining budget" lines are shown in italics. Scroll sideways to see all columns E to S.

Budget hold lines. The "Remaining budget" lines of each category (Professional Services, Construction Works...) are marked as budget hold. They absorb the changes and early warnings of their category, so the category total stays at the approved budget until the hold is used up, exactly like the Excel Schedule A.

CD Commercial Dashboard

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 51 – ...

Open

CM Commercial Manager

Admin

MODULES

Project Setup

Cost Report

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

User guide (PDF)

Change history

MODULE 2

Cost Report Level 1 & 2

Schedule A (Level 1, by asset and cost category) and Schedule B (Level 2, by package / contractor). All formulas are calculated by the app.

PDF

Excel

Monthly Report No 51 – Sep'26

Previous: Monthly Report No 50 – Aug'26

Level 1 – Level 2 check OK

Recalculate

Export Level 1 & 2 (Excel)

Level 1 – Executive

Level 2 – Detailed

Line setup

Set up one line per package / contractor with its approved baseline budget (columns A–E). Packages and contractors come from Settings. Use Import to load them from your Schedule B in one go.

Search cost report lines...

Filters

Export

Import

Add Cost line

Asset	Code	Package	Name / description
The Marina	PS.031D03	WSP Consultants	WSP Consultants - Employers Representative
The Marina	PS.031D04	Becon - Marine Relocation	Becon Developments Co - Coastal Conservation Management Plan and C
The Marina	PS.031D01	5 Ocean - Marine Survey 2210091	Five Oceans Marine Survey - Coral Ecology Surveys - 2210091
The Marina	PS.031D06	Sydney SeaPlane	Sydney Seaplane - Seaplane Consultant - 1250665
The Marina	PS.031FO3	Haskoning - Navigation Simulation	Haskoning - Navigation Simulation Study
The Marina	PS.031FO2	Kaust-King Abdullah University of Science	Kaust-King Abdullah University of Science 2250235
The Marina	CN031C01	ALS - Early Works	AlSaad - Early Works Package
The Marina	CN031C03	JVD Early Works	JVD - Early Works
The Marina	CN031C02	AlSaad Prelims	Preliminaries and General

Line setup: the cost lines with their code, package, contractor, category and baseline budget.

Module 3 – Change Management Tracker

CD Commercial Dashboard

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 51 – ...

Open

CM Commercial Manager

Admin

MODULES

Project Setup

Cost Report

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

User guide (PDF)

Change history

MODULE 3

Change Management Tracker

Every change in one record, followed from Early Warning → RFC → PVO → VO → EI → DVO → Funding. Approved DVOs, live PVO / VOs and RFCs feed the cost report automatically.

PDF

Excel

CHANGES

162

121 open

PENDING OVER 30 / 60 DAYS

0 / 106

open items by days since raised

COST REPORT – DVO (H)

8,007,274.86

PVO / VO (J) 5,704,361.81

COST REPORT – RFC (K)

640,000.00

all changes linked to a cost line

Status matrix

Number of changes at each stage by that stage's status

Stage	Cancelled	Approved	Pending	Superseded	Transferred	Review Complete	Other	Total
RFC	50	101	1	2	0	1	0	155
PVO	21	100	1	1	0	0	1	124
VO	15	96	0	0	0	0	1	112
DVO	10	97	2	0	0	0	0	109
Total	96	394	4	3	0	1	2	500

Days open > 30

Days open > 60

Highlighting applies to open changes only. Link each change to its cost report line so its value flows into columns H, J and K.

Search change management tracker...

Filters

Export

Import

Add Change

Contractor / Consultant	Project stage	Change category	Initiated by	Action pending by	Actions
Al Saad General Contracting Co. Ltd.	Post-Contract Variation	Design Dev	Employer	None	🕒 ✎ 🗑
Al Saad General Contracting Co. Ltd.	Post-Contract Variation	Design Dev	Employer	None	🕒 ✎ 🗑

Cards with the totals, the status matrix (how many changes at each stage and status) and the list of changes.

One row per change, followed from Early Warning → RFC → PVO → VO → EI → DVO → Funding. Open the row and fill in each stage as it happens (reference, date, status, amount). The dashboard works out the **current stage**, the **days open** (amber over 30, red over 60) and feeds columns H, J and K of the cost report. Link every change to its **cost report line** in the form, otherwise its value cannot flow into the cost report.

Module 4 – Claims & Disputes

Commercial Dashboard | PROGRAMME: 1TB01031 · Marina Villag... | ASSET: 1TB01031.01 · The Marina | REPORTING PERIOD: Monthly Report No 51 - ... | CM Commercial Manager Admin

MODULE 4
Claims & Disputes
Schedule E: every claim with its notice compliance, detailed claim, assessment by each party and the determination.

CLAIMS
7
6 pending · 1 Approved

EOT DAYS CLAIMED VS GRANTED
820 → 384
47% of days claimed granted

SAR CLAIMED VS DET ERMINED
46,455,401.69 → 14,631,530.80
31% of value claimed determined

COST REPORT – CLAIMS (M)
19,471,955.92
7 claim(s) not linked to a cost line

Assessment ladder
Totals across all claims at each step of the assessment.

Party	Claims	EOT days	Compensable days	Cost (SAR)
Contractor's Claim	7	820	465	46,455,401.69
Engineer's Recommendation	3	324	147	4,840,425.12
Employer's Assessment	1	324	177	0.00
Determination / Agreement	2	384	0	14,631,530.80

Notice compliance
Business days use the Sunday–Thursday working week. Public holidays are not excluded.

Notice later than 28 business days: 0

Detailed claim later than 42 business days: 0

Column M of the [cost report](#) carries, per claim: the Determination, else the Employer's assessment, else the Engineer's recommendation, else the Contractor's claim. Rejected claims and claims already included in the lump sum carry zero.

Search claims & disputes... | Filters | Export | Import | + Add Claim

Claim No	Description	Status	Claim type	Asset code	Contractor / Consultant
CL-001	Notice of Disatisfaction - Engineer's Instruction N...	Pending	EOT	The Marina	AlSaad General Contracting Co. Ltd.
CL-002	Notice of Disatisfaction - Engineer's Instruction N...	Pending	Prolongation	The Marina	AlSaad General Contracting Co. Ltd.
CL-003	Notice of Dissatisfaction on Engineer's Determina...	Pending	Other	The Marina	AlSaad General Contracting Co. Ltd.
CL-004	Extension of time - Precast Elements for fixed jetti...	Pending	EOT	The Marina	AlSaad General Contracting Co. Ltd.

Summary cards and the claims register.

Type the dates of the notice and of the detailed claim; the dashboard counts business days (Sunday to Thursday) and shows whether the 28-day and 42-day limits were met. Record the contractor's claim, the engineer's recommendation, the employer's assessment and the determination in their own sections.

The Claims Status Report

The Marina Commercial Dashboard | PROGRAMME: 1TB01031 · Marina Villag... | ASSET: 1TB01031.01 · The Marina | REPORTING PERIOD: Monthly Report No 51 - ... | CM Commercial Manager Admin

MODULE 4
Claims & Disputes
Schedule E: every claim with its notice compliance, detailed claim, assessment by each party and the determination.

CLAIMS
14
8 pending · 4 Approved · 2 Rejected

EOT DAYS CLAIMED VS GRANTED
1,818 → 381
21% of days claimed granted

SAR CLAIMED VS DET ERMINED
52,412,068.79 → 29,263,061.60
56% of value claimed determined

COST REPORT – CLAIMS (M)
14,631,530.80
1 claim(s) not linked to a cost line

Claims status report | PDF | Excel | Email claim status report

The **Claims status report** buttons in the page header (PDF and Excel) produce the executive claims report for the month selected in the top bar.

Claims Status Report

1TB01031 · Marina Village (Programme 1 – Triple Bay) · Monthly Report No 51 – Sep'26 · DRAFT (period not locked) · generated 10-Sep-26 15:47

CLAIMS RECORDED 14 8 pending · 4 determined · 2 rejected	CONTRACTORS WITH CLAIMS 3	CLAIMED (SAR) 52,412,068.79 1818 EOT days claimed	DETERMINED (SAR) 29,263,061.60 56% of value · 381 days granted
OPEN EXPOSURE (SAR) 52,412,068.79 gross value of pending claims	CARRIED IN COST REPORT (M) 14,631,530.80 determined / assessed amounts	LATE NOTICES / PARTICULARS 0 / 0 later than 28 / 42 business days	DISPUTES 2 Notice of Dissatisfaction / Dispute

Commercial narrative

Position at cut-off

As at 30-Sep-26, 14 claims are recorded against 1TB01031.01 The Marina from 3 contractors: 8 pending, 4 determined or approved and 2 rejected. Contractors have claimed SAR 52,412,068.79 and 1818 days of extension of time; determinations to date total SAR 29,263,061.60 and 381 days, i.e. 56% of the value and 21% of the time claimed. The open claims carry a gross exposure of SAR 52,412,068.79, of which SAR 14,631,530.80 is carried in the cost report (column M); the balance is reported through the early warnings until determined.

Movement since Monthly Report No 50 – Aug'26

7 new claims were received (CT-008, CT-061, CT-069, CT-084 and 3 more). 5 claims changed status or value (CL-002, CL-004, CL-005, CL-006 and 1 more). The claims column of the cost report moved by nil.

Exposure and status of open claims

The largest open item is CT-008 (Al Saad General Contracting Co. Ltd., Prolongation) at SAR 46,455,401.69, currently at the stage "Employer's assessment issued – awaiting determination" with action resting with Employer's Representative. Across the 8 open claims: 3 employer's assessment issued – awaiting determination; 2 resubmitted – under assessment; 3 detailed claim received – under assessment. Where an assessment exists, the assessed value totals SAR 14,631,530.80 against SAR 46,455,401.69 claimed for the same items.

Compliance and risk

All claims were notified and particularised within the contractual time limits. 2 claims have escalated to a Notice of Dissatisfaction or Dispute and are being managed with legal support.

Outlook and recommended actions

The commercial team's priorities for the coming period are to complete the assessment of the claims under review and issue the Engineer's recommendations, close out the determinations issued and agree final values with the contractors. Determined amounts will be carried into the cost report and, where budget is not available, funded through the change management process.

Since Monthly Report No 50 – Aug'26

- New: CT-008 EOT 1 Prolongation
Engineer's Instruction No. 5, 7, 9 & 10 [Cost claim] (SAR 46,455,401.69)
- New: CT-061 EOT-02 TB Marina Project - Request for Extension of Time [Time claim]
- New: CT-069 Costs Claim Requests associated with EOT-2 (cost claim related to item 61 above) [Cost cla (SAR 5,155,062.34)]

Page 1 of the report: headline figures, the written narrative and the items requiring attention. The claims table and the by-contractor summary follow.

Once the month's claims are in (typed in, imported from the monthly workbook or picked out of the Claims Tracker), press **Claims status report** → **PDF**. The dashboard writes the report itself: the position at cut-off (how many claims, claimed versus determined value and time), the movement since the last issued report, the exposure and stage of every open claim, compliance with the notice periods and any disputes, and the recommended actions. Nothing is typed by hand, so the words always match the numbers. The Excel version carries the same content for editing. The blue **Email claim status report** button next to it works exactly like "Email the Report" on the Executive Summary: it writes a short email with the headline table and narrative and opens it in Outlook with the Claims Status Report PDF attached.

Module 5 – Early Warnings and Risks & Opportunities

CD Commercial Dashboard

MODULES

Project Setup

Cost Report

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

User guide (PDF)

Change history

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 51 – ...

Open

CM Commercial Manager

Admin

MODULE 5

Early Warnings & Risks / Opportunities

Early warning notices (feeding column L of the cost report) and the commercial risk & opportunity register with its heat map.

PDF Excel

Early Warnings (7)

Risks & Opportunities (2)

EARLY WARNINGS

7

6 open · 1 converted to RFC · 0 closed

OPEN – POTENTIAL COST (L)

7,105,062.89

all open items linked to a cost line

OPEN – POTENTIAL TIME

0 days

sum of potential time impact

OPEN BY LIKELIHOOD

Low 0 Med 3 High 3

Open early warnings feed column L of the [cost report](#). When one becomes an RFC, set its status to *Converted to RFC* and link the change item so the value moves to the change tracker instead.

Q Search early warnings...

Filters

Refresh

Export

Import

+ Add Early Warning

EW No ^	Date raised ^	Raised by ^	Package ^	Contractor / Consultant ^	Description ^
EW	31-Aug-26	Contractor	Elmar-Hijaz Boardwalk and Jetties	Elmar Marinas Khaleej LLC	Additional Slipway at Nabateen S
EW-07	06-Sep-26	Contractor	Al Saad Main Works	Al Saad General Contracting Co. Ltd.	Dredge spoil disposal site nearing
EW-22	31-Aug-26	Contractor	Al Saad Prelims	Al Saad General Contracting Co. Ltd.	Non Provision of Employer's Faci
EW-22-2	31-Aug-26	Contractor	Elmar-Hijaz Boardwalk and Jetties	Elmar Marinas Khaleej LLC	Elmar EOT-01 Cost Claim
EW-23	31-Aug-26	Contractor	MME-MME Marine Engg	MME – Majestic Marine Engineering LLC	EOT-02 COST – MME – Eextensio
EW-23-2	31-Aug-26	Contractor	MME-MME Marine Engg	MME – Majestic Marine Engineering LLC	Additional scope of Tograpic Su
EW-23-3	31-Aug-26	Contractor	Elmar-Hijaz Boardwalk and Jetties	Elmar Marinas Khaleej LLC	MEP works, Aerodrom Installation,

7 of 7 early warnings · double-click a row to edit

Two registers on one page, with the heat map of risks and opportunities.

Open early warnings feed column L of the cost report. When an early warning becomes an RFC, set its status to "Converted to RFC" and it drops out of column L (the RFC takes over in column K/J).

Module 6 – Provisional Sums

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

User guide (PDF)

Change history

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 51 – ...

Open

CM Commercial ManagerAdmin

MODULE 6

Provisional Sums

Provisional sum allowances, what has been instructed against each, and the saving or extra that results.

TOTAL BUDGET124,000,000.0016 provisional sum(s)

TOTAL INSTRUCTED50,477,392.655 of 16 item(s) with a contract value

TOTAL SAVING28,522,607.35instructed value below budget

BY STATUSPending 15Approved 1

(Saving) / Extra = Contract value – Budget. Savings show in green with a minus sign, extras in red. The totals row at the bottom of the table follows your search and filters. Statuses are managed under Settings → Provisional Sum Statuses.

Q Search provisional sums...

Filters

Export

Import

+ Add Provisional Sum

Item	Description	Status	Contractor	Budget	Contract value
PS-01	Allowance for Marine furniture steel support	Pending	Al Saad General Contracting Co. Ltd.	5,000,000.00	520,531.00
PS-02	Allowance for coordination with utilities	Pending	Al Saad General Contracting Co. Ltd.	2,500,000.00	—
PS-03	Dry stack access ramp	Pending	Al Saad General Contracting Co. Ltd.	1,000,000.00	—
PS-04	ECO Marine habitat to promote marine environment	Pending	Al Saad General Contracting Co. Ltd.	15,000,000.00	—
PS-05	Archl finish coordinated with external public realm	Pending	Al Saad General Contracting Co. Ltd.	2,000,000.00	1,059,783.36
PS-06	Bridge interface	Pending	Al Saad General Contracting Co. Ltd.	5,000,000.00	—
PS-07	Porous edge treatment following wave study	Approved	Al Saad General Contracting Co. Ltd.	12,000,000.00	621,261.23
PS-08	shoring to quay wall due to reduced set back	Pending	Al Saad General Contracting Co. Ltd.	48,000,000.00	48,000,000.00
PS-09	Labs & testing requirements	Pending	Al Saad General Contracting Co. Ltd.	1,000,000.00	—

Budget, instructed value and the (saving) / extra, worked out for you.

Module 7 – Bonds & Insurance

The screenshot shows the 'Bonds & Insurance' module interface. At the top, there are filters for Programme (1TB01031 - Marina Villag...), Asset (1TB01031.01 - The Marina), and Reporting Period (Monthly Report No 51 - ...). The user is logged in as 'CM Commercial Manager Admin'. The left sidebar lists various modules, with 'Bonds & Insurance' selected. The main content area displays a summary of bonds and policies, including counts for expired bonds, provided vs required values, shortfalls, and checks out standing. Below this is a table of bonds and insurance policies expiring soon, with columns for status, description, and expiry date. A search bar and filters are at the bottom.

MODULE 7
Bonds & Insurance
Every bond and insurance policy: what the contract requires, what has been provided, and when it expires.

BONDS & POLICIES
38
29 expired · 0 within 30 days · 0 with...

PROVIDED VS REQUIRED
683,882,463.51 / 314,714,52...
total face value held vs total contrac...

SHORT FALLS
2
0.06 below requirement in total

CHECKS OUT STANDING
Not approved 10
Bank not verified 5

Bonds & insurance expiring soon
29 already expired.
29 within 60 days

expired 679d	G-10b · Professional Indemnity · WSP Middle East	31-Oct-24
expired 649d	G-12 · Workmen's Compensation · WSP Middle East	30-Nov-24
expired 618d	G-05 · Advance Payment Bond · Al Saad General Contracting Co. Ltd.	31-Dec-24
expired 537d	G-03 · Public/Third Party Liability · Al Saad General Contracting Co. Ltd.	22-Mar-25
expired 537d	G-11 · Public/Third Party Liability · WSP Middle East	22-Mar-25
expired 528d	G-04 · Contractors All Risks · Al Saad General Contracting Co. Ltd.	31-Mar-25
expired 511d	G-02 · Professional Indemnity · Al Saad General Contracting Co. Ltd.	17-Apr-25
expired 467d	G-20 · Advance Payment Bond · Al Saad General Contracting Co. Ltd.	31-May-25

[Open the Bonds & Insurance log →](#)

Rows turn amber within 60 days of expiry and red within 30 days or once expired. Contract requirement = the % entered × revised contract value (or the original sum if no cost line is linked), or the fixed SAR amount. Types are managed under Settings → Insurance / Bond Types.

Search bonds & insurance... Filters Export Import + Add Bond / Insurance


Ref Contractor / Consultant Package Type of bond / insurance Policy /

Every bond and policy with its expiry. Rows turn amber 60 days before expiry and red 30 days before or once expired.


Contract requirement is either a percentage of the contract value or a fixed SAR amount; the variance to what was provided is calculated. Bonds expiring soon also appear on the Executive Summary.

Each row has a **Status: Active, Expiring, Expired, Released or Superseded**. A policy is **Released** when its contract is finished, so an old expiry date is not a problem and it is not counted as expired. The dashboard works this out for you from the **Final Account Status** (Closed, Not required or Direct payment), which decides first, and from the contract status in Invoices & Payments (Closed, Completed, Terminated) where a contract has no final account row. Contracts are recognised by their code (031C02), so closing one contract releases the bonds on all of its cost lines (CN.031C02 and CN.031C02-2 alike). When you import the Excel report the FA Status sheet and the CLOSED contracts in Schedule H are read the same way. You can also tick **Contract closed – bond released** on the row yourself. **Superseded** means a newer policy of the same type is held for the same contract, so the old one is ignored too.

Module 8 – Invoices & Payments

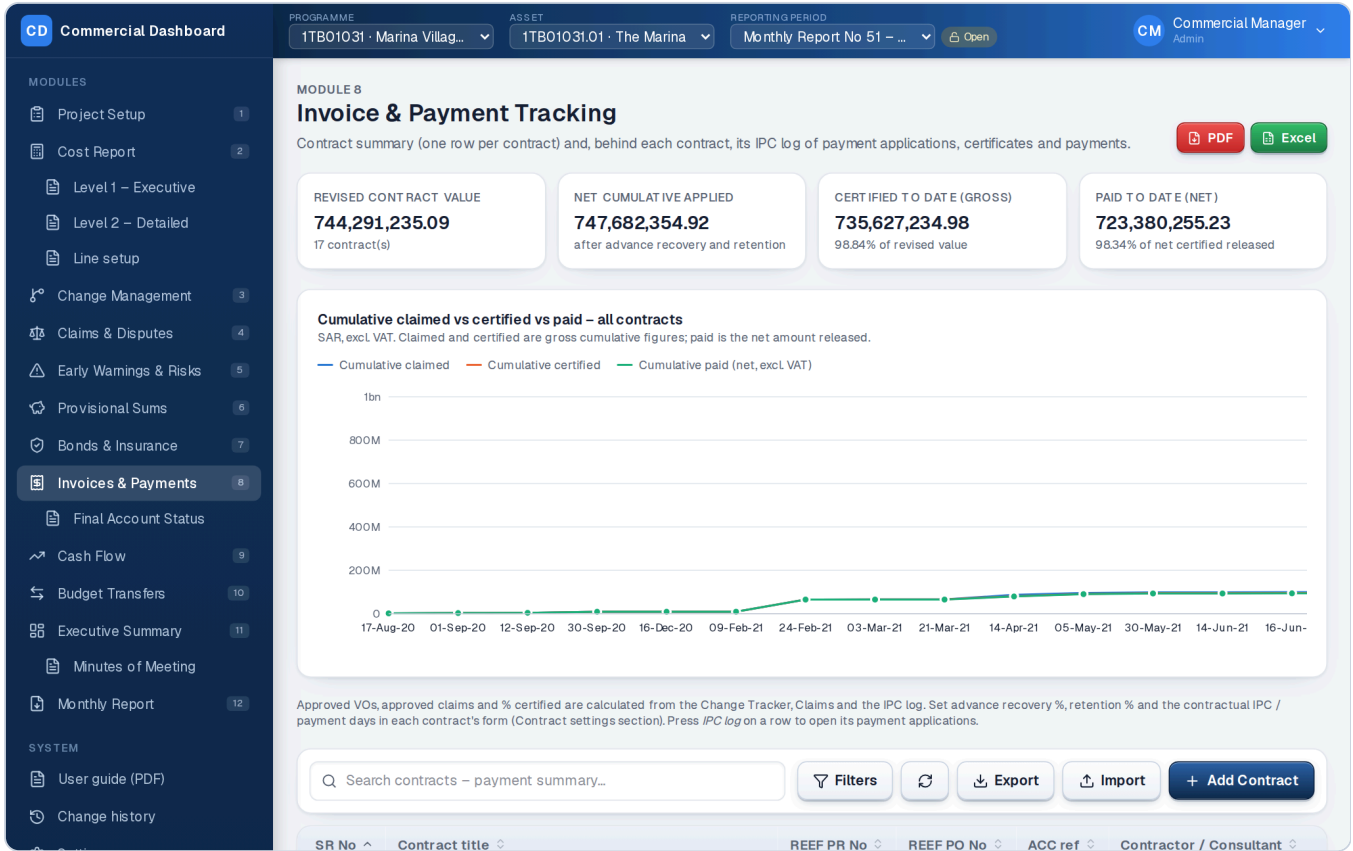

The contract summary (one row per contract) with cumulative applied, certified and paid, and the % certified.

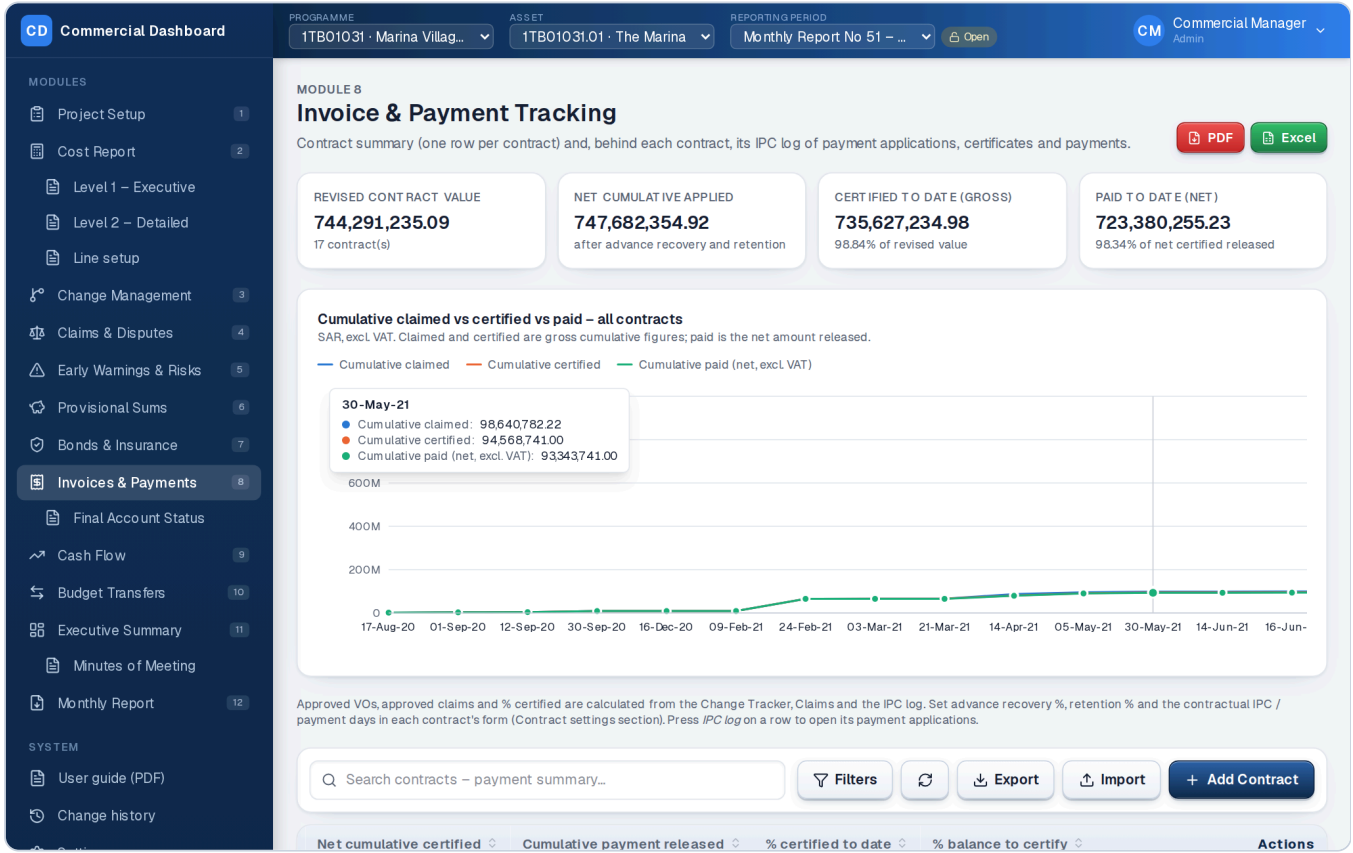

Click a contract to open its IPC log. Add one row per payment application. Due dates for the IPC and the payment are worked out from the contract settings (days to issue IPC, days to pay).

Module 8 – Final Account Status

CD Commercial Dashboard

MODULES

Project Setup

Cost Report

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

SYSTEM

User guide (PDF)

Change history

PROGRAMME

ASSET

REPORTING PERIOD

CM Commercial Manager

1TB01031 · Marina Villag...

1TB01031.01 · The Marina

Monthly Report No 51 – ...

Open

MODULE 8

Final Account Status

One row per contract: is the final account statement open, signed or not required, and when is closure expected. Committed cost and the anticipated final account are read from the cost report line, so the totals tie to Schedule B.

PDF

Excel

OPEN

6

161,839,134.63 anticipated final account - 2 past forecast date

CLOSED (FAS SIGNED)

5

228,091,410.28 anticipated final account

NOT REQUIRED / DIRECT PAYMENT

6

8,907,406.57 anticipated final account

TOTAL PACKAGES

17

398,837,951.48 total anticipated final account

Days remaining turn amber within 60 days of the forecast closure date and red once it has passed (open final accounts only). Link each row to its cost report line so the values stay in step with Schedule B.

Q Search final account status...

Filters

Export

Import

Add Final Account

ACC code	Package / description	Contractor / Consultant
PS.031D01	Five Oceans Marine Survey - Coral Ecology Surveys - 2210091	Five Oceans Environmental Services LLC
PS.031D03	WSP Consultants - Employers Representative	WSP Middle East
PS.031D04	Becon Developments Co - Coastal Conservation Management Plan and Coral Relocation	Beacon Development Company
PS.031D06	Sydney Seaplane - Seaplane Consultant - 1250665	Sydney Seaplanes Asia Limited
PS.031F02	Kaust- King Abdullah University of Science 2250235	KAUST – King Abdullah University of Science & Technol
PS.031F03	Haskoning - Navigation Simulation Study	Haskoning DHV Saudia
CN.031C01	AlSaad - Early Works Package	Al Saad General Contracting Co. Ltd.
CN.031C02	AlSaad-Marina Basin	Al Saad General Contracting Co. Ltd.

One row per contract: is the final account open, signed (closed) or not required, and when closure is expected. The committed cost and anticipated final account come from the cost report line.

The Final Account Status Report

TM The Marina

Commercial Dashboard

MODULES

Project Setup

Cost Report

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management

PROGRAMME

ASSET

REPORTING PERIOD

CM Commercial Manager

1TB01031 · Marina Villag...

1TB01031.01 · The Marina

Monthly Report No 51 – ...

Open

MODULE 8

Final Account Status

One row per contract: is the final account statement open, signed or not required, and when is closure expected. Committed cost and the anticipated final account are read from the cost report line, so the totals tie to Schedule B.

Final account status report

PDF

Excel

Email final account status report

PDF

Excel

OPEN

6

161,839,134.63 anticipated final account - 2 past forecast date

CLOSED (FAS SIGNED)

5

228,091,410.28 anticipated final account

NOT REQUIRED / DIRECT PAYMENT

6

8,907,406.57 anticipated final account

TOTAL PACKAGES

17

398,837,951.48 total anticipated final account

On the Final Account Status page: **Final account status report** (PDF and Excel) and **Email final account status report**.

Page 34 of 57

Final Account Status Report

1TB01031 · Marina Village (Programme 1 – Triple Bay) · Monthly Report No 51 – Sep'26 · DRAFT (period not locked) · generated 10-Sep-26 15:52

PACKAGES TRACKED

17

6 open · 5 closed · 6 not required

OPEN (SAR)

161,839,134.63

anticipated final account of open packages

CLOSED – FAS SIGNED (SAR)

228,091,410.28

NOT REQUIRED / DIRECT PAYMENT (SAR)

8,907,406.57

TOTAL ANTICIPATED FINAL ACCOUNT

398,837,951.48

all tracked packages

UNCOMMITTED ON OPEN PACKAGES

12,849,424.70

still to be agreed

PAST FORECAST CLOSURE DATE

2

0 due within 60 days

NO FORECAST DATE

0

open packages

Commercial narrative

Position at cut-off

As at 30-Sep-26, 17 contract packages are tracked for final account on 1TB01031.01 The Marina: 6 open (SAR 161,839,134.63 anticipated final account), 5 closed with the final account statement signed (SAR 228,091,410.28) and 6 not requiring a final account or paid directly (SAR 8,907,406.57). The anticipated final account across all packages is SAR 398,837,951.48, of which SAR 12,849,424.70 on the open packages is not yet committed and remains to be agreed.

Movement since Monthly Report No 50 – Aug'26

2 packages changed status or anticipated final account (CN.031C10, CN.031C15). The anticipated final account of the tracked packages moved by -5,360,000.00.

Closure programme

2 packages are beyond the forecast closure date and need a revised programme or escalation. The next closure is forecast for 30-Jul-26 (CN.031C12 Al Saad General Contracting Co. Ltd.). Every open package has a forecast closure date.

Outlook and recommended actions

The commercial team's priorities are to close out the overdue final accounts and agree revised dates where the statement cannot be signed this period, agree the SAR 12,849,424.70 of uncommitted value through the change and claims processes so it can be committed before closure. Signed final account statements release the retention and bonds held for each package.

Since Monthly Report No 50 – Aug'26

- CN.031C10 MME Marine Engineering: Open -> Open (AFA +640,000.00)
- CN.031C15 Elmar-Hijaz Boardwalk and Jetties: Open -> Open (AFA -6,000,000.00)

Items requiring attention

- 2 final accounts past the forecast closure date (CN.031C12 Al Saad General Contracting Co. Ltd., PS.031F02 KAUST – King Abdullah University of Science & Technology) – revise the forecast or escalate the closure.
- Largest uncommitted balances still to be agreed: CN.031C10 SAR 6,295,062.89; CN.031C15 SAR 6,264,361.81; PS.031F03 SAR 290,000.00.

Final account status by package

Open packages first, earliest forecast closure first. Committed and anticipated final account are read from the cost report.

Page 1 of the report: headline figures, the narrative (position, movement, closure programme, actions) and the items requiring attention, followed by the package table.

The report reads the Final Account Status register for the month in the top bar and writes the narrative itself: how many packages are open, closed or not required and their anticipated final account, what changed since the last issued report, which closures are overdue or due within 60 days, the uncommitted value still to be agreed, and the recommended actions. The email button opens the same summary in Outlook with the PDF attached, addressed to the distribution list.

Module 9 – Cash Flow

CD Commercial Dashboard

MODULES

Project Setup 1

Cost Report 2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management 3

Claims & Disputes 4

Early Warnings & Risks 5

Provisional Sums 6

Bonds & Insurance 7

Invoices & Payments 8

Final Account Status

Cash Flow 9

Budget Transfers 10

Executive Summary 11

Minutes of Meeting

Monthly Report 12

SYSTEM

User guide (PDF)

Change history

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 51 – ...

Open

CM Commercial Manager

Admin

MODULE 9

Cash Flow

Monthly forecast per contract against the actual payments made, with the cumulative picture and what has been certified but not yet paid.

PDF Excel

Monthly grid

Cumulative chart

Accruals (6)

Months: Sep'20 – Apr'26 Refresh Export (Excel)

Type a forecast in any month and press Tab or click away to save. Actuals = net payments (excl. VAT) by paid date from Payment Tracking, unless overridden. Click an actual to override it; clear the box to go back to the automatic value. Difference = Actual – Forecast (red = more than forecast).

Transaction No	Supplier	Line Description	Coding	CBS	Programme	
—	Five Oceans Environmental Services LLC	Coral Ecology Surveys	—	—	1TB01031	
—	Beacon Development Company	Coastal Conservation Manage...	—	—	1TB01031	
—	Al Saad General Contracting Co. Ltd.	Triple Bay Marina Basin – Early...	—	—	1TB01031	
—	Dredging International Saudi Arabia (JVD)	Triple Bay Marina Basin – Early...	—	—	1TB01031	
—	Five Oceans Environmental Services LLC	Marina Ecological Coral Surveys	—	—	1TB01031	
—	WSP Middle East	Marina Basin Supervision Con...	—	—	1TB01031	
—	Al Saad General Contracting Co. Ltd.	Triple Bay Marina Basin – Desl...	—	—	1TB01031	
—	Five Oceans Environmental Services LLC	Marina Ecological Coral Reloc...	—	—	1TB01031	
—	MME – Majestic Marine Engineering LLC	Design and Construction of FL...	—	—	1TB01031	
—	Al Saad General Contracting Co. Ltd.	Construction of Fixed Jetty for...	—	—	1TB01031	
—	Supreme Rubber LLC	Supply of Marine Furniture	—	—	1TB01031	
—	Etmar Marinas Khaleej LLC	Constructing Boardwalks & Je...	—	—	1TB01031	
—	Al Rajhi Takaful (Insurance)	Al Rajhi Takaful-Insurance – C...	—	—	1TB01031	

Forecast, actual and difference per contract per month, with the cumulative chart. Actuals come from the paid dates in the IPC logs; you can overwrite a cell if needed.

Module 10 – Budget Transfers

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

User guide (PDF)

Change history

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 51 – ...

Open

CM Commercial Manager

Admin

MODULE 10

Budget Transfers

Budget moved between packages. Approved transfers reduce the From package and increase the To package in column F of the cost report.

PDF

Excel

TRANSFERS

30

30 approved

APPROVED AMOUNT MOVED

711,697,476.18

total leaving From packages = total ...

PENDING APPROVAL

0.00

not yet in the cost report

COST REPORT CHECK

Column F Nets to zero

30 approved not applied

⚠

These approved transfers are not in the cost report yet: BT-01(From package has no cost report line); BT-02(From package has no cost report line); BT-03(From package has no cost report line); BT-04(From package has no cost report line); BT-05(From package has no cost report line); BT-06(From package has no cost report line); BT-07(From package has no cost report line); BT-09(From package has no cost report line); BT-10(From package has no cost report line); BT-11(From package has no cost report line); BT-12(From package has no cost report line); BT-13(To package has no cost report line); BT-14(From package has no cost report line); BT-15(From package has no cost report line); BT-16(From package has no cost report line); BT-17(From package has no cost report line); BT-18(From package has no cost report line); BT-19(From package has no cost report line); BT-21(From package has no cost report line); BT-23(From package has no cost report line); BT-24(From package has no cost report line); BT-25(From package has no cost report line); BT-26(From package has no cost report line); BT-27(From package has no cost report line); BT-28(From package has no cost report line); BT-29(From package has no cost report line); BT-30(From package has no cost report line); BT-31(From package has no cost report line); BT-31b(From package has no cost report line); BT-32(From package has no cost report line). Open the transfer and choose the From / To cost line, or add the missing line on the Cost Report Line setup tab.

Net movement by package (as applied to cost report column F)

Package	Out	In	Net
No approved transfers applied yet.			

A transfer lands on the package's Level 2 line automatically. If a package has more than one line (several contractors), pick the line in the form. The *In cost report* column shows whether each transfer is currently applied. Column F on the Cost Report is now live.

Q Search budget transfers...

Filters

↺

Export

Import

+ Add Budget transfer

Item	Description	Status	From package	To package
------	-------------	--------	--------------	------------

Transfers between packages. Approved transfers linked to cost lines feed column F.

Page 37 of 57

Module 11 – Minutes of Meeting

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

User guide (PDF)

Change history

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 51 – ...

Open

CM Commercial ManagerAdmin

< Executive Summary

MODULE 11

Minutes of Meeting

One row per meeting. Open the minutes to record items and actions; anything still open is carried forward to the next meeting automatically.

PDFExcel

Q Search minutes of meeting...

Filters

Export

Import

+ Add Meeting

Meeting No	Title	Meeting date	Reporting period	Chair	Attendees
MCM-50	Monthly Commercial Meeting – August 2026	02-Sep-26	Monthly Report No 50 – Aug'26	Michael Hansen	M. Hansen, B. Lombard

1 of 1 minutes of meeting · double-click a row to edit

One meeting per month. Open items are carried forward automatically to the next meeting.

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

User guide (PDF)

Change history

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 51 – ...

Open

CM Commercial ManagerAdmin

< Executive Summary

MODULE 11

Minutes of Meeting

One row per meeting. Open the minutes to record items and actions; anything still open is carried forward to the next meeting automatically.

PDFExcel

Q Search minutes of meeting...

Filters

Export

Import

+ Add Meeting

Meeting date	Reporting period	Chair	Attendees	Actions
p-26	Monthly Report No 50 – Aug'26	Michael Hansen	M. Hansen, B. Lombard, N. Chintawar, S. Fairfield (p...	Open minutes🕒✎🗑

1 of 1 minutes of meeting · double-click a row to edit

Inside a meeting: attendees, discussion items and actions with owner, due date and status.

9. Locking a month and generating the report

CD Commercial Dashboard

MODULES

Project Setup1

Cost Report2

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management3

Claims & Disputes4

Early Warnings & Risks5

Provisional Sums6

Bonds & Insurance7

Invoices & Payments8

Final Account Status

Cash Flow9

Budget Transfers10

Executive Summary11

Minutes of Meeting

Monthly Report12

SYSTEM

User guide (PDF)

Change history

PROGRAMME1TB01031 · Marina Villag...

ASSET1TB01031.01 · The Marina

REPORTING PERIODMonthly Report No 51 – ...Open

CM Commercial ManagerAdmin

< Settings

REPORT CONTROL

Reporting Periods

One row per monthly report. Lock a period at month end to take a snapshot of every register.

Month-end: press *Lock* on a period to freeze it. The app stores a copy (snapshot) of every module register at that moment so later reports can show *This Period* vs *Previous Period*. Unlock only if you need to correct something.

Q Search reporting periods...

Filters

Export

Import

+ Add Reporting Period2

Label	Status	Locked at	Locked by	Aconex ref	Actions
Report No 51 – Sep'26	Open	—	—	—	Lock1
Report No 50 – Aug'26	Locked	10-Sep-26	Commercial Manager	AMAALA/THE MARINA/MONTHLY REPORT 50	Unlock

2 of 2 reporting periods · double-click a row to edit

Settings → Reporting Periods. 1 Lock or Unlock a period (Admin). 2 Add the next month.

Locking takes a snapshot of every register and of the cost report. From then on the month is read-only and the next month compares itself against it ("previous period" and "movement" columns).

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina PROJECT PERIOD: Monthly Report No 51 – ... Open

MODULES

- Project Setup 1
- Cost Report 2
 - Level 1 – Executive
 - Level 2 – Detailed
 - Line setup
- Change Management 3
- Claims & Disputes 4
- Early Warnings & Risks 5
- Provisional Sums 6
- Bonds & Insurance 7
- Invoices & Payments 8
 - Final Account Status
- Cash Flow 9
- Budget Transfers 10
- Executive Summary 11
 - Minutes of Meeting
- Monthly Report 12**

SYSTEM

- User guide (PDF)
- Change history

MODULE 12

Generate Monthly Report

Cover, index, minutes of meeting, executive summary and Schedules A to J as PDF or Excel, built from the locked snapshot of the chosen period.

Reporting period: Monthly Report No 51 – Sep'26 · Open Generate PDF Generate Excel

Open – report is a DRAFT from live data Lock the period under Settings → Reporting Periods (or on Project Setup) to freeze the figures before issuing.

Have the month in Excel already?
Upload your existing monthly report workbook and the app records it against a period. Import past months in order to build the history, then each new month shows its movement. Import monthly workbook

Contents

- Cover page with project particulars and the Prepared / Reviewed / Approved block
- Index with checklist status and distribution list
- Minutes of Meeting for the period (carried-forward and new items)
- Executive Summary: KPIs, open items, key issues, actions, cost chart
- Schedule A** Cost Report – Level 1 (Executive) ○
- Schedule B** Cost Report – Level 2 (Detailed) ○
- Schedule C** Change Management Tracker ○
- Schedule D** Early Warnings & Risks / Opportunities ○
- Schedule E** Claims & Disputes ○
- Schedule F** Provisional Sums ○
- Schedule G** Bonds & Insurance ○
- Schedule H** Invoice & Payment Tracking and Final Account Status ○
- Schedule I** Cash Flow ○
- Schedule J** Budget Transfers ○

Sign-off block (current period)

PREPARED BY	REVIEWED BY	APPROVED BY
no date	no date	no date

Fill these in on [Project Setup](#) → [Report control](#). Aconex reference and key issues come from the same place.

Monthly Report. **1** Choose the period. **2** Generate PDF. **3** Generate Excel.

The PDF contains the cover page with the sign-off block, the index, the minutes of meeting, the executive summary and Schedules A to J. The Excel has one sheet per schedule. If the period is still open the report is marked as a **draft from live data**; lock the period to issue the final version.

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 51 - ... Open

MODULE 12

Generate Monthly Report

Cover, index, minutes of meeting, executive summary and Schedules A to J as PDF or Excel, built from the locked snapshot of the chosen period.

Reporting period: Monthly Report No 51 – Sep'26 · Open

[Open – report is a DRAFT from live data](#) Lock the period under Settings → Reporting Periods (or on Project Setup) to freeze the figures before issuing.

[Generate PDF](#) [Generate Excel](#)

Have the month in Excel already?
Upload your existing monthly report workbook and the app records it against a period. Import past months in order to build the history, then each new month shows its movement.

[Import monthly workbook](#)

Contents

- Cover page with project particulars and the Prepared / Reviewed / Approved block
- Index with checklist status and distribution list
- Minutes of Meeting for the period (carried-forward and new items)
- Executive Summary: KPIs, open items, key issues, actions, cost chart
- Schedule A** Cost Report – Level 1 (Executive)
- Schedule B** Cost Report – Level 2 (Detailed)
- Schedule C** Change Management Tracker
- Schedule D** Early Warnings & Risks / Opportunities
- Schedule E** Claims & Disputes
- Schedule F** Provisional Sums
- Schedule G** Bonds & Insurance
- Schedule H** Invoice & Payment Tracking and Final Account Status
- Schedule I** Cash Flow
- Schedule J** Budget Transfers

Sign-off block (current period)

PREPARED BY: no date REVIEWED BY: no date APPROVED BY: no date

Fill these in on [Project Setup](#) → [Report control](#). Aconex reference and key issues come from the same place.

The contents of the report and the sign-off block for the current period.

All reports (library): change, re-upload or delete a report

< Monthly Report

MODULE 12

All reports (library)

Every monthly report the dashboard holds: where it came from, whether it is issued, and the tools to open, change, re-upload, lock, unlock or delete it.

Report	Cut-off	Status	Source	Issued snapshot	Last change
Monthly Report No 51 – Sep'26 Report No 51	30-Sep-26	Open	Manual entry	live data	10-Sep-26
Report No 51: Open Downloads Re-upload Change Lock Delete					
Monthly Report No 50 – Aug'26 Report No 50	31-Aug-26	Issued (locked)	Workbook import	530 records · 47 cost lines	10-Sep-26
Report No 50: Open Downloads Re-upload Change Unlock Delete					

Re-upload opens the monthly workbook import with this report pre-selected; the workbook's rows update the existing ones by their references. A locked report is unlocked first (Admin) and should be locked again after the import. **Delete** removes the report, its issued snapshot and its checklist only; the live registers are not touched.

Monthly Report → **All reports (library)** (also in the left menu). One row per report with its cut-off, status, where it came from (the workbook file, when and by whom, or "Manual entry"), the data it holds (Live for the latest report, Stored copy or Issued copy for the others) and the tools: **Open** (select it in the top bar), **Downloads**, **Re-upload**, **Change**, **Lock / Unlock** and the bin.

- **Re-upload** opens the monthly workbook import with that report pre-selected, so you can load a corrected or newer version of the same month. Rows are matched by their references: the report is refreshed, not duplicated, and stored as that report's own data. A locked report is unlocked first (Admin,

after a confirmation); tick "Lock the period after importing" to issue it again. For a month older than the latest report, the latest report's live figures are put back automatically when the import finishes.

- **Change** edits the report number, the cut-off date or the label. Leave the label blank to rebuild it from the number and date. The number decides the order of the reports and therefore which report the movement is measured against.
- **Delete** (Admin) removes the report, its issued snapshot and its checklist after you type the report number to confirm. The live registers – cost lines, changes, claims, payments – are never touched by a delete, so deleting a wrongly created period is safe.
- **Lock / Unlock** work as on the Project Setup page; locking an older report while a newer one exists asks for a confirmation.

10. Settings, users and backups

Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031.01 · The Marina REPORTING PERIOD: Monthly Report No 51 - ...

Settings

Dropdown lists, project structure, reporting periods and users. Every list supports add / edit / delete, search, Excel import & export and change history.

Database backup [Download database](#)

Cloud backup is off (no BACKUP_GITHUB_* or BACKUP_S3_* settings). The database is the file data/commercial.db; use *Download database* to keep a copy. On a hosting service, set the backup settings so the database survives restarts.

Changes are uploaded within about 20 seconds, plus one dated copy per day. To restore, place the downloaded file at data/commercial.db (or upload it to the backup storage as backups/commercial.db) and restart the app.

PROJECT STRUCTURE

- Programmes** 1 → Top-level programmes (e.g. 1TB01031).
- Assets** 3 → Assets within a programme (e.g. 1TB01031.01).
- Clients** 1 → The employer / client organisations.
- Locations** 1 → Where the programmes / assets are located.

REPORT CONTROL

- Reporting Periods** 2 → One row per monthly report. Lock a period at month end to take a snapshot of every register.


COMMERCIAL LISTS

- Packages** 50 → Work packages / contracts that the cost report is broken down by.
- Contractors & Consultants** 13 → Every party you hold a contract or purchase order with.


DROPDOWN LISTS

Settings: every dropdown list, the project structure, reporting periods, users, the database backup and the Start over card (Admin only).

- **Dropdown lists** (packages, contractors, statuses, bond types, cost categories...): add or rename values here. The forms pick them up immediately.
- **Programmes and Assets**: the codes and names shown in the top bar.
- **Reporting Periods**: add the next month, lock and unlock (chapter 9).
- **Users**: add colleagues and choose their role (chapter 11).
- **Database backup**: the data is backed up automatically to a private GitHub repository within 20 seconds of every change. "Download database" gives you a copy to keep.
- **Start over**: wipes all project data (not users or settings). Only for a fresh start after a test import. It asks you to type DELETE.

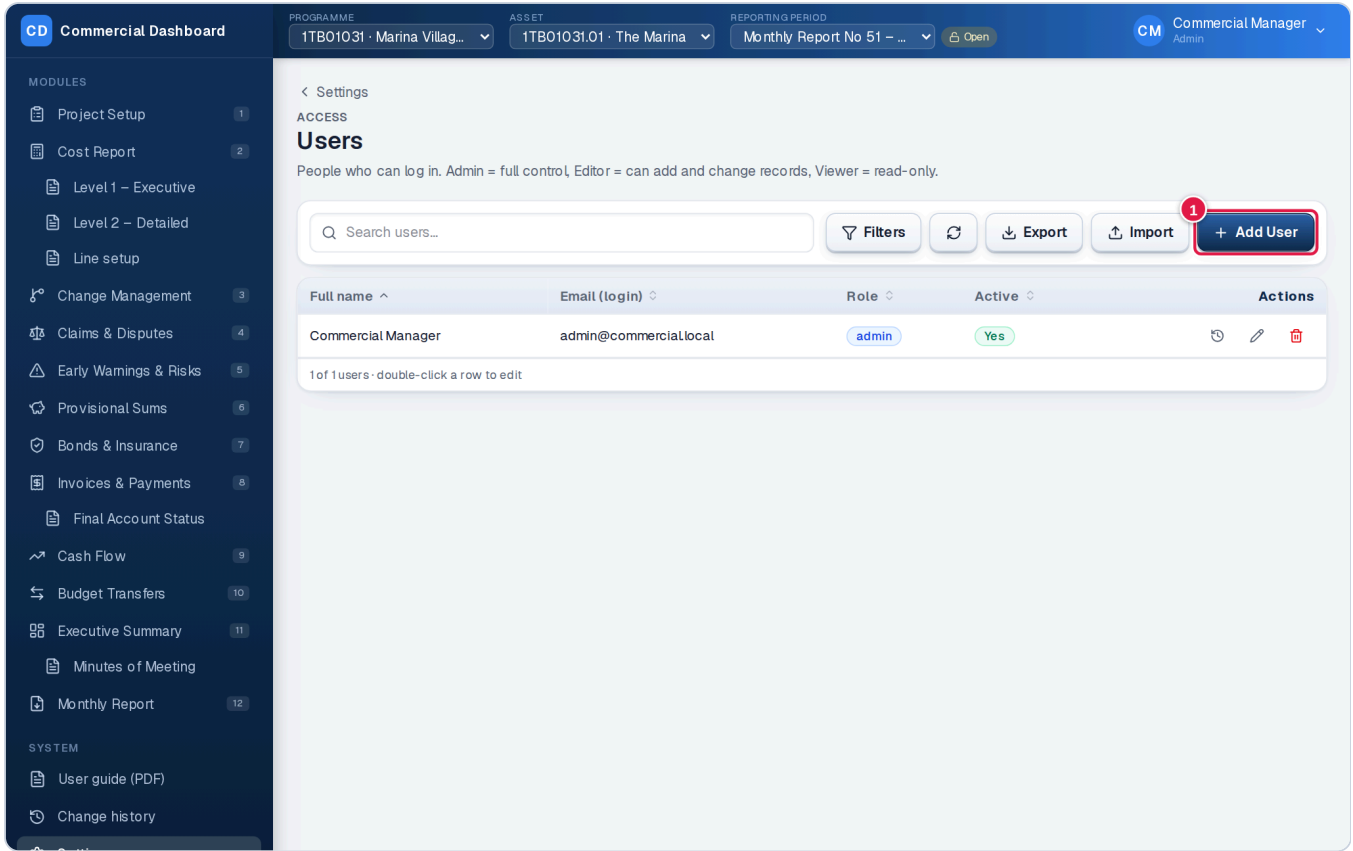

Settings → Users. **1** Add a user: name, email, role and a first password. They can change the password later.

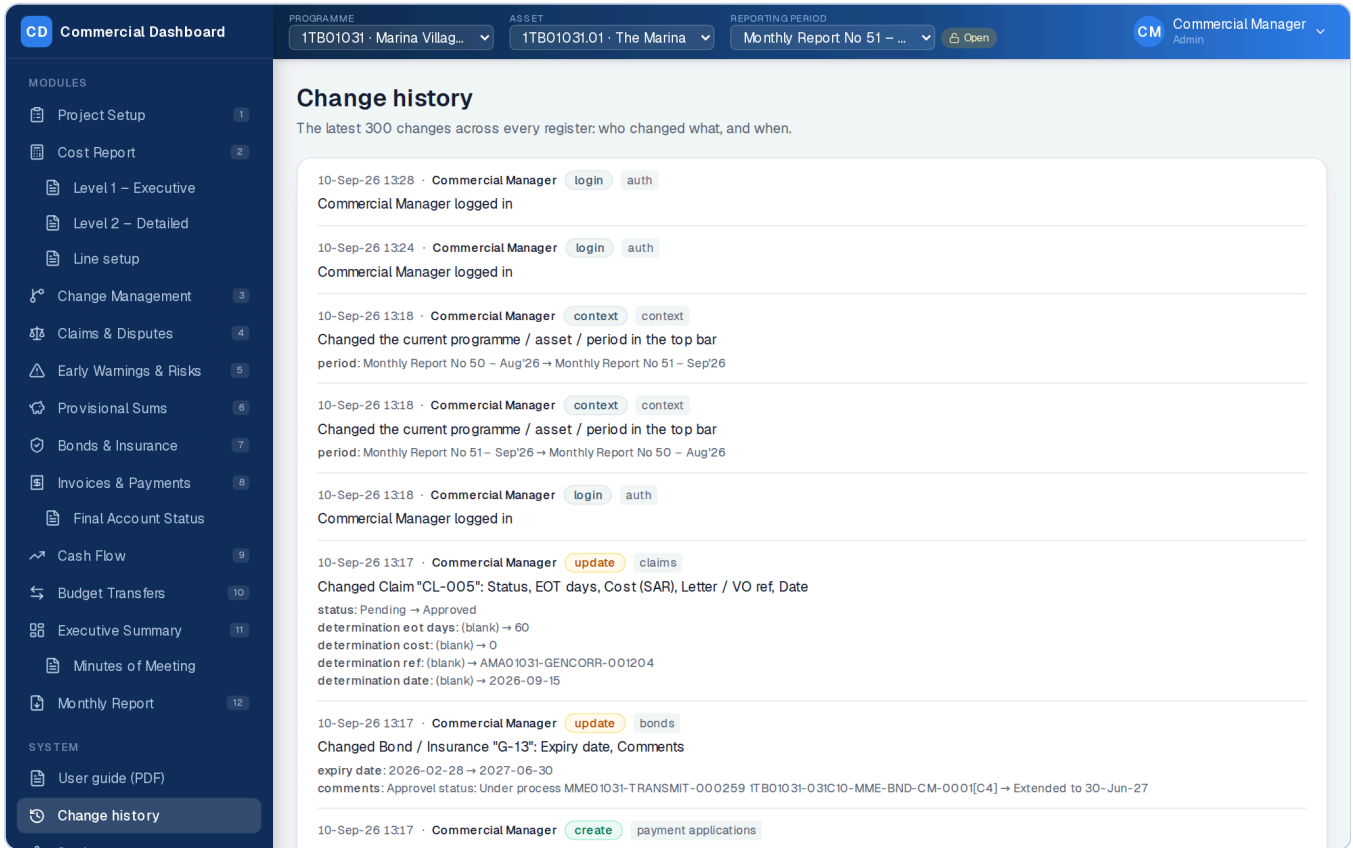

Change history (System → Change history) lists every change made by anyone, newest first.

11. Who can do what

Role	Can see	Can add / edit / delete	Can lock periods, manage users, back up, start over
Viewer	Everything	No	No
Reports only (download)	Only the Reports & downloads page	No. Can pick a month and download every report as PDF or Excel, and open the user guide. Every other page and button is hidden and blocked.	No
Data entry (add only)	Everything	Can add new rows in every module (a new change, claim, IPC, bond, meeting action, cost line...) and run every PDF, Excel and "Email the Report". Cannot edit or delete existing rows, enter cash flow, change report control or key issues, or import a workbook.	No
Editor	Everything	Yes, in every module	No
Admin	Everything	Yes, in every module	Yes

Give Viewer to people who only read the report, Data entry to colleagues who log new items for you, Editor to the commercial team, and Admin to one or two people who issue the report.

Two accounts are created for you the first time the dashboard starts: **User-1** (login **user1@commercial.local**) and **User-2** (login **user2@commercial.local**). They are **Reports only** users: when they log in they land on the Reports & downloads page and can do nothing else. Ask the Admin for the starting password and change it under Settings → Users as soon as possible. The Admin can give them another role there at any time.

The cost report as a presentation (PowerPoint and PDF slides)

Executive Summary, top right. **1 PowerPoint** downloads the monthly cost report as a short (10–13 slides), colourful, animated and fully editable presentation. **2 PDF slides** is the same presentation as a PDF. **3 Excel dashboard** downloads the whole dashboard as one Excel workbook (see below). The Reports & downloads page has the same buttons, for any month.

The presentation is built from the report selected in the top bar and carries its status (Issued or Draft) in the footer of every slide. Each slide has its own colour band, coloured headline tiles and either charts or tables that fill the page. Only sections with something to show are included: a month with no claims, no cash-flow figures or no earlier report to compare with simply has no claims, cash-flow or movement slide, and tiles that would show zero are left out. The slides that can appear are: title; executive summary with headline tiles, a written summary and the anticipated-final-account build-up; cost report Level 1 in the Excel "Level 01" layout with a budget-against-forecast chart; the largest packages and the lines driving the variance; movement since the previous report; change management with the status of every stage; early warnings and risks; claims and disputes; invoices and payments with the cumulative claimed / certified / paid curve; cash flow (monthly and cumulative); bonds and insurance; provisional sums and budget transfers; and key issues and open actions.

The dashboard as an Excel workbook

The **Excel dashboard** button (and "Commercial Dashboard (Excel)" on the Reports & downloads page) gives you the whole dashboard for the selected month in one workbook, laid out like the website: a **Dashboard** sheet with the six headline tiles, the six open-item tiles, links to every module, six native Excel charts, the headlines, key issues and open actions; then one sheet per module – Level 1, Level 2, Movement, Change Management, Claims & Disputes, Early Warnings & Risks, Provisional Sums, Bonds & Insurance, Invoices & Payments, Final Account Status, Cash Flow, Budget Transfers and Minutes & Actions. Each module sheet starts with the summary figures and a chart, exactly as the dashboard page does, followed by the full register.

The workbook is live: Level 1 is built by formula from Level 2, the Dashboard tiles read Level 1, and the module summaries are COUNTIF / SUMIF formulas over the register on the same sheet. Change a figure in a register and the summary, the tile and the chart follow. The charts are ordinary Excel charts (right-click → Select Data to change them). Figures that the dashboard works out from several registers together – open change items, expired bonds, the package ranking and the payment curve – are written as values for that month.

When you present the PowerPoint, every slide fades in and its tiles, charts and tables appear one after the other automatically – no clicks are needed. The animations are ordinary PowerPoint animations: open the Animations tab → Animation Pane to change or remove them.

Everything in the PowerPoint is editable. The charts are native PowerPoint charts (right-click → Edit Data), the tables are real tables, and the text is text. Change a number, a colour or a wording, add your own slide, and present. The PDF version is for e-mailing or printing; the layout and colours are the same as the PowerPoint.

The Reports & downloads page

The screenshot displays the 'Reports & downloads' page in the The Marina Commercial Dashboard. The top navigation bar includes the 'TM' logo, 'The Marina Commercial Dashboard', and filters for 'PROGRAMME' (1TB01031 - Marina Villag...), 'ASSET' (1TB01031.01 - The Marina), and 'REPORTING PERIOD' (Monthly Report No 51 - ...). A user profile 'User-1' is visible in the top right.

The left sidebar contains 'REPORTS' and 'Reports & downloads' (selected), along with a 'User guide (PDF)' link.

The main content area is titled '1TB01031 - 1TB01031.01 Reports & downloads'. It instructs users to 'Choose the month, then download any report as a print-ready PDF or a formatted Excel file.'

The 'REPORTING PERIOD' section shows two active reports: 'Monthly Report No 51 - Sep'26' and 'Monthly Report No 50 - Aug'26'. A note indicates 'Draft - live data' with a 'cut-off 30-Sep-26'.

The 'Full monthly report - Monthly Report No 51 - Sep'26' section features a dark blue header and buttons for 'PDF' and 'Excel' downloads. Below this, it states: 'Cover, index, minutes, executive summary, movement and Schedules A to J in one file.'

The 'SUMMARIES' section lists several reports, each with 'PDF' and 'Excel' download buttons:

- Executive Summary**: Headline figures, open items, payment tracker, key issues and actions.
- Movement since the previous report**: Cost report movement, key period movements, status counts, register changes.
- Claims Status Report**: Executive claims report with narrative.
- Final Account Status Report**: Executive final account report with narrative.
- Minutes of Meeting**: Meetings and actions of the period.

The 'SCHEDULES' section lists four reports, each with 'PDF' and 'Excel' download buttons:

- Schedule A - Cost Report - Level 1 (Executive)**: Asset x category summary.
- Schedule B - Cost Report - Level 2 (Detailed)**: Line by line cost report.
- Schedule C - Change Management Tracker**: Register as printed in the monthly report.
- Schedule D - Early Warnings & Risks / Opportunities**.

Everyone has it under **System** → **Reports & downloads**; for a Reports-only user it is the whole dashboard. Pick the month at the top, then download the full monthly report or any single report as PDF or Excel.

12. Security: how the dashboard and its documents are protected

Everything in the dashboard sits behind a login, and the protection works in layers. Nothing is public: even the user guide PDF needs a login.

Layer	What it does
Encrypted connection	The site is only served over HTTPS. The browser is told to always use HTTPS (HSTS), never to show the dashboard inside another website (no framing), and search engines are told not to index it.
Login and sessions	Passwords are stored as salted bcrypt hashes; nobody, not even the Admin, can read them. A login lasts 7 days on that browser, in a cookie the page scripts cannot read and that is never sent to other websites. Sessions are signed with a secret key that exists only on the server.
Password rules	At least 10 characters with letters and numbers, not your name, not a common word. Accounts created with a starting password must choose their own password at the first login before they can see anything. Anyone can change their own password from the menu under their name.
Brute-force protection	After 5 wrong passwords an email address or a network address is locked for 15 minutes; 30 attempts from one address in 15 minutes are refused. Every failed and successful login is written to the Change history with the network address.
Roles	Every page and every server call checks the role from the database, not just the login token, so a change under Settings → Users applies immediately. Reports-only users cannot reach anything but the Reports page.
Cross-site protection	Requests that change data are accepted only when they come from the dashboard's own address, so a malicious website you happen to visit cannot act on the dashboard with your login. Browser security headers (content security policy, no MIME sniffing, no referrer leakage) are sent with every page.
Uploads	Workbook imports accept only genuine .xlsx files up to 40 MB; they are parsed in a separate process with a memory cap and deleted after 30 minutes. Claim EAR documents (any file type, up to 60 MB each) are kept on the server's private disk under the case, are never served to anyone but logged-in Editors and Admins, and are deleted with the case.
Data and backups	The database lives on the server's private disk. Backups go to your own private GitHub repository with a token that only the server holds. The database download is Admin-only.

What you and your colleagues must do

- Use a strong, unique password and never share it; never write it in an email or chat.
- Give each person their own account; use **Viewer** or **Reports only** for anyone who does not need to enter data, and set accounts to **Inactive** as soon as someone leaves.
- Log out on shared or public computers (menu under your name → Log out).
- Keep the backup GitHub repository private and do not share the backup token.

- The PDF and Excel files you download are your copies: store them in your company's document system, not on personal devices or public drives.
- If you suspect a leaked password, change it at once and ask the Admin to review the Change history for unfamiliar logins.

13. Automation: Claim EAR (Employer's Assessment Report)

When a contractor submits an extension of time or cost claim, the Employer answers with an **Employer's Assessment Report (EAR)**. Writing one by hand means reading the whole claim folder, checking the contract, and drafting twenty or more pages in the house template. The **Automation** → **Claim EAR** page does the reading and the first draft for you: you upload the documents, press one button, and download a print-ready Word file laid out on your own template. For a **revised** submission it writes the new report on top of the previous EAR, with every difference shown as a tracked change by **Commercial Manager**, so the reviewer sees exactly what moved.

Who can use it. Editors and Admins. Viewers, Data entry and Reports-only accounts do not see the Automation menu. The drafting engine needs a key set by the administrator in the hosting settings (`ANTHROPIC_API_KEY` on Render); until it is set, the page shows an orange banner and Create EAR produces a skeleton laid out from your template instead of the full report.

Step 1: create a case

TM

The Marina

Commercial Dashboard

MODULES

Project Setup

Cost Report

Level 1 – Executive

Level 2 – Detailed

Line setup

Change Management

Claims & Disputes

Early Warnings & Risks

Provisional Sums

Bonds & Insurance

Invoices & Payments

Final Account Status

Cash Flow

Budget Transfers

Executive Summary

Minutes of Meeting

Monthly Report

New month (manual entry)

STAND-ALONE IMPORTS

Monthly report workbook

PROGRAMME

1TB01031 · Marina Villag...

ASSET

1TB01031.01 · The Marina

REPORTING PERIOD

Monthly Report No 51 – ...

Open

CM

Commercial Manager

Admin

AUTOMATION

Claim EAR – Employer's Assessment Report

Upload the contractor's claim folder, your EAR template and the contract documents; the dashboard writes the Employer's Assessment Report as a print-ready Word file. For a revised submission it also takes the previous EAR and previous submission, and writes the new report with tracked changes.

Drafting engine not configured.

Add ANTHROPIC_API_KEY in the hosting settings (Render → Environment) to have the full report written; until then Create EAR produces a skeleton laid out from your template.

Start a new assessment

One case per contractor claim. Give it a name, then upload the claim folder, your EAR template and the contract folder on the next screen.

1

Case title

e.g. EOT Claim No 3 – Quay wall drawings

Contractor

Claim ref

2

Revised submission

3

Create case

Contractor	Claim ref	Submission	Documents	Status	Report	Last change
Marina Marine Works Co	CL-003	Revision 1	4 files · 24 KB	Generated	Word	2026-09-10 · Commercial Manager
Marina Marine Works Co	CL-003	Original	6 files · 24 KB	Generated	Word	2026-09-10 · Commercial Manager

4

Open →

Automation → Claim EAR. **1** Name the case (one per contractor claim). **2** Tick **Revised submission** when the contractor has re-submitted and you already issued an EAR. **3** Create case. **4** Open an existing case. The list shows how many documents each case holds, its status and a link to the last Word report.

Page 50 of 57

Step 2: upload the documents

TM The Marina
Commercial Dashboard

PROGRAMME: 1TB01031 · Marina Villag... ASSET: 1TB01031C01 · The Marina REPORTING PERIOD: Monthly Report No 51 – ... **CM Commercial Manager** Admin

< Claim EAR cases

AUTOMATION · CLAIM EAR

EOT Claim No 3 – Quay wall drawings

Marina Marine Works Co · Contract 1TB01031C02 · Claim CL-003

Drafting engine not configured. Documents can be uploaded and a skeleton EAR laid out from your template, but the full assessment is written only when the server has an ANTHROPIC_API_KEY (Render → Environment). Ask the administrator to add it, then press Create EAR again.

Case details Original submission Save details

Case title: EOT Claim No 3 – Quay wall dra Contractor: Marina Marine Works Co Contract No: 1TB01031C02 Claim reference: CL-003

Contractor's submission ref: MMW-RSG-L-0412 Submission date: 08/20/2026 ☐ This is a revised submission

1 Contractor's claim & supporting documents 4 Upload folder Add files

The whole claim folder: narrative, notices, programmes (XER), delay analysis, cost build-ups, correspondence, photos – any file type.

File Type	File Name	Size	Status
PDF	01 Narrative/claim.pdf	2 KB	✓
Excel	02 Analysis/events.xlsx	6 KB	✓
Text	03 Programme/programme.xer	1 KB	✓
Image	04 Photos/site-photo.png	6 KB	⚠

Files marked with a warning could not be read fully (scanned PDF, image or a format the engine cannot open). Hover to see why.

2 EAR template (Word or PDF) 1 Choose file

Your Employer's Assessment Report template. Its headings, order and wording drive the structure of the report.

File Type	File Name	Size	Status
Word	template.docx	8 KB	✓

3 Contract documents 1 Upload folder Add files

The whole contract folder: conditions of contract, particular conditions, specifications, programme requirements – any file type.

File Type	File Name	Size	Status
PDF	Conditions/particular-conditions.pdf	2 KB	✓

Create EAR (Word)


6 documents · 24 KB. The engine reads the whole submission and the contract, follows your template, and writes a print-ready report.

Download EAR (Word) Create again

✓ **EAR - EOT Claim No 3 Quay wall drawings.docx** created 2026-09-10 18:20. Skeleton only – the drafting engine is not configured (add ANTHROPIC_API_KEY on the server). 6 documents received. Not readable: 1 file.

All amounts in SAR. Dates DD-MMM-YY

A case. **1** Case details: contractor, contract number, claim and submission references (they go on the report's cover block) – Save. **2** **Upload folder** sends the contractor's whole claim folder, sub-folders included. **3** Choose your EAR template (Word or PDF). **4** Upload the contract folder. **5** Create EAR. **6** Download the Word file.

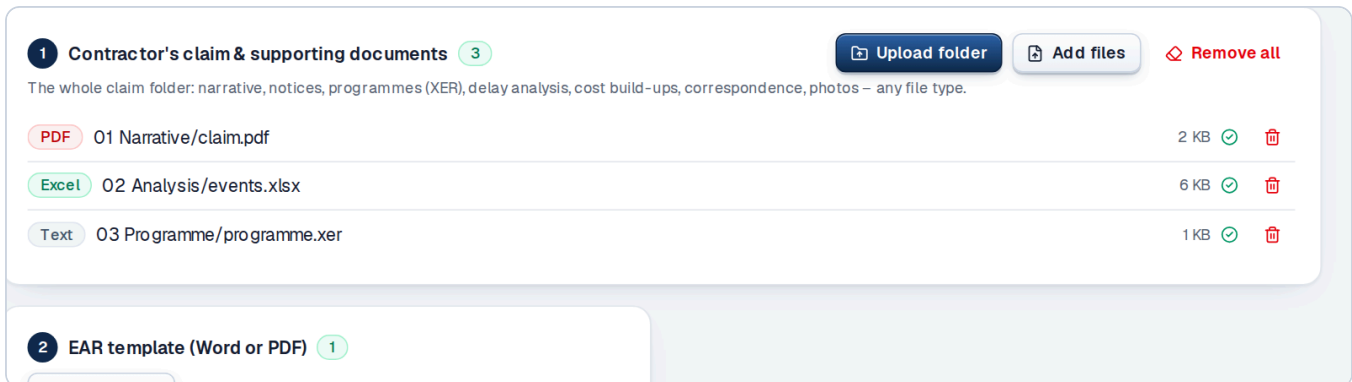

Once a group holds documents, a red **Remove all** button appears beside Upload folder and Add files. One click (and a confirmation) empties that group so you can upload a corrected folder.

- 1 **Contractor's claim & supporting documents.** Click **Upload folder** and pick the folder you received from the contractor: the narrative, notices and letters, the delay analysis, the programmes (XER), cost build-ups, photographs. Every file type is accepted (PDF, Word, Excel, images, XER, e-mails, anything). Sub-folder names are kept, and the report cites documents by them. Use **Add files** to add single files later.
- 2 **EAR template.** One Word file (a PDF also works, see below): your Employer's Assessment Report template. The report is written **into a copy of that file**, so its fonts, colours, heading styles, cover page, revision-history block, header and footer, page size and margins are exactly those of the template; nothing about its look is changed. Its headings, in their order, are the headings of the report (the engine may add sub-headings under them, one per delay event for example). Only the numbering (1.0, 1.1, 1.1.1, Table 1, Table 2 ...) is regenerated to fit the new content, in the template's own style. A previously issued EAR is an ideal template. With a PDF template the headings are still followed, but the file is laid out in the dashboard's standard Word style because a PDF's fonts and styles cannot be copied.
- 3 **Contract documents.** Upload the contract folder: conditions of contract, particular conditions, specifications, programme requirements, key letters. The report quotes the clause numbers from here.
- 4 **Remove all** next to the upload buttons empties a group in one click (after a confirmation), for example to replace a whole claim folder with a newer one; the bin icon on a row removes a single document.
- 5 Each document gets a badge for its type and a green tick when its text could be read. An orange triangle means the engine cannot see inside it: a scanned PDF without text (run OCR in Acrobat and upload it again), an image (kept as evidence and named in the report), or a format such as .msg, .zip or .dwg. Hover the triangle for the reason.

Large folders. Files go up one at a time in small pieces, so a 300 MB claim folder simply takes a few minutes; keep the page open until the counter finishes. Each file may be up to 60 MB and a case up to 800 MB.

Step 3: create the report

Press **Create EAR**. The engine reads the whole submission, the contract and the template, then writes the report: entitlement and notice compliance, the delay analysis (critical path, concurrency, float, mitigation), quantum (rates, prolongation, duplication with variations), with claimed-against-assessed tables, the Employer's position for each delay event, a conclusion and recommendation, the documents relied upon and a list of information gaps to request from the contractor. Every finding cites the clause and the file it comes from. Writing takes a few minutes for a large claim; the green box then names the file and how many documents were read. Click **Download EAR (Word)**.

The Word file is fully editable and looks like your template: same fonts and heading colours, the cover page filled with the contract number, contractor, claim reference and date, the revision-history block, the table of contents, the numbered paragraphs, the tables in the template's table style with numbered captions, and an "Assessment at a glance" table at the start of the first section. Read it, adjust what you want, and issue it. Press **Create again** after adding documents to rewrite it.

"This document contains fields that may refer to other files. Update?" Word asks this the first time you open the report. Answer **Yes**: it fills in the page numbers of the table of contents.

Revised submissions: tracked changes

The screenshot displays the 'Claim EAR cases' interface in The Marina Commercial Dashboard. The top navigation bar shows the programme '1TB01031 · Marina Villag...', asset '1TB01031.01 · The Marina', and reporting period 'Monthly Report No 51'. The user is logged in as 'CM Commercial Manager Admin'.

The left sidebar lists various modules, with 'Claim EAR' highlighted under the 'AUTOMATION' section. The main content area shows the details for 'EOT Claim No 3 – Quay wall drawings (Rev 1)' under the programme 'Marina Marine Works Co · Claim CL-003'.

A red box highlights the checkbox 'This is a revised submission', which is checked. This checkbox is part of the 'Case details' section, which also includes fields for Case title, Contractor, Contract No, Claim reference, Contractor's submission ref, Submission date, and Revision number.

Below the case details, there are several sections for uploading documents:

- 1 Contractor's claim & supporting documents**: Includes a 'Upload folder' button and a list of documents, such as '01 Narrative/claim-rev1.pdf' (2 KB).
- 2 EAR template (Word or PDF)**: Includes a 'Choose file' button and a list of documents, such as 'template.docx' (8 KB).
- 3 Contract documents**: Includes a 'Upload folder' button and a message: 'No documents yet – upload the whole folder; sub-folders are kept.'
- 4 Previous EAR issued by the Employer**: Includes a 'Choose file' button and a list of documents, such as 'EAR-original.docx' (12 KB).
- 5 Contractor's previous submission**: Includes a 'Choose file' button and a list of documents, such as 'claim.pdf' (2 KB).

At the bottom, there is a section for 'Create revised EAR (Word, tracked changes)' with a 'Download EAR (Word)' button and a 'Create again' button. A green message box at the bottom states: 'EAR - EOT Claim No 3 Quay wall drawings Rev 1 - Rev 1.docx created 2026-09-10 18:20. Skeleton only – the drafting engine is not configured (add ANTHROPIC_API_KEY on the server). 4 documents received.'

A revised case. **1** Tick **This is a revised submission** and enter the revision number; two more groups appear. **2** Upload the previous EAR you issued (Word or PDF). **3** Upload the contractor's previous submission. **4** Create revised EAR.

When the contractor re-submits, create a new case (or untick and re-tick the box on the old one), tick **revised submission**, upload the new claim folder as usual, and add the **previous EAR** and the **previous submission**. The engine keeps the previous report's structure and wording wherever it is still right, changes only what the new evidence justifies, and adds a section "Changes in the revised submission". The Word file is written on top of the previous EAR with **Track Changes switched on**: every insertion and deletion is a tracked change by **Commercial Manager**, dated the day it was written. Open it in Word, use

Review → **Next** to walk through the differences, and Accept or Reject each one as you would with a colleague's mark-up.

The previous EAR can be the Word file the dashboard produced last time or any Word/PDF you wrote yourself; a Word file gives the cleanest comparison because its paragraphs and tables line up exactly.

Good practice

- Name the case after the claim and the letter reference; fill the contract number and submission date so the cover block is right first time.
- The report is a draft prepared for you, not a determination. Check every figure against the submission before it is issued; the "Information gaps" list at the end is a ready-made request letter to the contractor.
- Delete a case (the bin icon on the list, Admin only) when the claim is closed; that removes its documents from the server.

14. If something goes wrong

What you see	What to do
"Login failed" on the office laptop	Try your phone or another browser. If the phone works, the office network is blocking the site; ask IT to allow the address.
The page takes a long time or shows a 502 message	The free hosting sleeps after 15 minutes without visitors and needs up to a minute to wake up. Wait, then reload once.
A field turns red when saving	Read the message under the field. Usually a required field is empty or a value is not in the dropdown list.
"This period is locked"	You are trying to change an issued month. Switch the top bar to the open month, or ask an Admin to unlock.
A dropdown does not have the package / contractor you need	Ask an Admin to add it under Settings, or tick "create missing values" when importing a workbook.
The import lists rows with errors	The rest of the file was imported. Fix the cells named in the message in Excel, then import the same file again choosing the same period; fixed rows are updated, nothing is duplicated.
The Level 1 – Level 2 check is red	A cost line is missing an asset or category. Open Cost Report → Line setup and complete the line.
Claim EAR shows "Drafting engine not configured"	The administrator must add ANTHROPIC_API_KEY in the hosting settings (Render → Environment) and redeploy. Until then Create EAR gives a skeleton only.
A claim document has an orange triangle	The engine cannot read inside it: a scanned PDF (run OCR and upload again), an image (fine, it is kept as evidence) or a .msg / .zip / .dwg file (save the content as PDF).
"Writing the report" runs for a long time or the connection drops	A big claim takes several minutes. Wait, then reload the case page: if the green box shows the file, it was saved; otherwise press Create EAR again.
A report was imported into the wrong month, or twice	Open Monthly Report → All reports (library). Use Change to correct its number or cut-off, Re-upload to load the right workbook into it, or the bin to delete a period created by mistake.
Period movement shows 0.00 and the "previous" figures equal this report's	Both reports hold the same stored figures (this happened with older versions when a report was locked after the next month's data was loaded). Open Monthly Report → All reports and use Re-upload on the month that is wrong: each report is stored on import and the latest month's live figures are put back automatically.
"... has no stored data of its own" when locking	The report was created before its data was stored and a newer report exists. Re-upload its workbook from All reports (library); it is stored on import and can then be locked.

Numbers on the Executive Summary look wrong	Check the top bar period, then the source module (a change not linked to a cost line, an early warning left Open, an IPC with a wrong cumulative value).
---	--

Health check for support: <https://commercial-dashboard-kkz4.onrender.com/api/health> shows whether the database and the backup are working.

Questions or ideas for the dashboard? Note them in the minutes of meeting under "Dashboard" so they are not forgotten.
